

MONTHLY PROGRESS REPORT

KENDALL COUNTY

NEW OFFICE BUILDING

December 12, 2023





November Monthly Report

Construction Management Services

December 12, 2023

Contents

Section 1: Project Update

Section 2: Project Cost Report

Section 3: Schedule

Section 4: Construction Field Reports and Photos

Section 5: Architectural & Engineering Field Reports

SECTION 1: PROJECT UPDATE



Kendall County

New Office Building

Monthly Project Summary 11/30/2023

Work Completed in November 2023

To date we have completed the following activities:

- Demo Existing South Parking Lot & Fill
- Parking Lot Stone South Lot
- Asphalt Binder South Lot
- Demo Existing West Lot & Fill
- Parking Lot Stone West Lot
- Asphalt Binder West Lot
- Concrete Flatwork around South & West Parking Lots
- Light Gauge Bearing wall Framing First Floor

We are currently progressing on the following activities:

- Structural Steel Light Gauge Trusses
- Excavation for New ADA Ramp Addition at Retaining Wall

The following phases of construction scheduled for the near future:

- Concrete work For New ADA Ramp at Retaining Wall
- Roof Deck
- Storefront & Window Install
- Roofing

SECTION 2: PROJECT COST REPORT



Kendall County – New Office Building

Cost Report & Contingency Reductions Through 11/30/23


PCO #	Date Approved By Owner	Contractor	Description	Potential Contingency Reduction Amount	Contingency Reduction Amount Approved	Comments
CONTINGENCY REDUCTIONS APPROVED IN OCTOBER:					\$45,035	
CONTINGENCY REDUCTIONS APPROVED IN NOVEMBER 2023:					\$75,448	
7		LCI	PR-006 Credit for Mailboxes in 119	(\$630)	(\$630)	
		LCI/Jensons	Temp Heat & Gas Hook up @ Fire Station	\$6,000	\$6,000	
		Plainfield Grading	Backcharge for re-staking of the curb in the south parking lot	(\$825)	(\$825)	
		Abbey Paving	Re-staking of the curb in the south parking lot	\$825	\$825	
		Abbey Paving	Temporary Striping in the South Parking Lot	\$605	\$605	
		Abbey Paving	Temporary Striping in the West Parking Lot	\$605	\$605	
CONTINGENCY REDUCTIONS APPROVED IN DECEMBER 2023:					\$6,580	

SEE THE FOLLOWING POTENTIAL COSTS THAT HAVE BEEN IDENTIFIED:

2331		Plainfield Grading	Water main run under slab to sprinkler room	\$11,021		Needs review by A/E/CM
		CSN Electric	Potential Electrical Changes	\$2,510		Needs review by A/E/CM
		Midwestern Concrete	New Ramp vs Stair to Old Fire Station Concrete Added Cost	\$32,000		
2		LCI	New Ramp vs Stair to Old Fire Station Additional handrail	\$23,672		Researching another quote for this work
		Plainfield Grading	Additional Undercuts at South Parking Lot as Req'd by the Geotech Engineer	\$10,000		Estimated cost by CCCS
		Plainfield Grading	Additional Undercuts at West Parking Lot, angled parking, drive into site from Ridge Road	\$100,000		Estimated cost by CCCS

SECTION 3: SCHEDULE





SECTION 4: CONSTRUCTION
FIELD REPORTS AND PHOTOS



Form detail

#59: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Nov 2, 2023
Submitted by	Ken Gleason
Status	Closed
Last update	Nov 3, 2023, 10:57 AM CDT
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Partly Cloudy



Temperature: 29°F

Wind: ↑ 5mph

Humidity: 82%

12:00 PM

Partly Cloudy



Temperature: 47°F

Wind: ↗ 10mph

Humidity: 55%

4:00 PM

Partly Cloudy



Temperature: 54°F

Wind: ↗ 10mph

Humidity: 49%

Updated Nov 3, 2023 at 3:57 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	1	8	worked on preparation for the topping pour to take place tomorrow for the precast section of building, as well as setting plastic barriers over openings to basement section.
BP #3 Exc / Site Util - Plainfield Grading	6	48	crew worked on setting up the south parking lot to get ready for curb install to get started tomorrow with the paving crew.
BP #4 Building Concrete - Premium Concrete Inc	10	80	crew worked on pouring SOG for the 1st floor today.
Totals	17	136	

References

Photos (17)



IMG_0529

Taken on Nov 2, 2023, 9:21 AM CDT

Added on Nov 2, 2023, 3:59 PM CDT

Added by Ken Gleason



IMG_0528

Taken on Nov 2, 2023, 9:21 AM CDT

Added on Nov 2, 2023, 3:59 PM CDT

Added by Ken Gleason



IMG_0525

Taken on Nov 2, 2023, 9:13 AM CDT

Added on Nov 2, 2023, 3:59 PM CDT

Added by Ken Gleason



IMG_0531

Taken on Nov 2, 2023, 9:23 AM CDT

Added on Nov 2, 2023, 3:59 PM CDT

Added by Ken Gleason



IMG_0526

Taken on Nov 2, 2023, 9:13 AM CDT

Added on Nov 2, 2023, 4:00 PM CDT

Added by Ken Gleason



IMG_0534

Taken on Nov 2, 2023, 2:37 PM CDT

Added on Nov 2, 2023, 4:00 PM CDT

Added by Ken Gleason



IMG_0537

Taken on Nov 2, 2023, 2:40 PM CDT

Added on Nov 2, 2023, 4:00 PM CDT

Added by Ken Gleason



IMG_0530

Taken on Nov 2, 2023, 9:23 AM CDT

Added on Nov 2, 2023, 4:00 PM CDT

Added by Ken Gleason



IMG_0532

Taken on Nov 2, 2023, 9:27 AM CDT

Added on Nov 2, 2023, 4:00 PM CDT

Added by Ken Gleason



IMG_0527

Taken on Nov 2, 2023, 9:13 AM CDT

Added on Nov 2, 2023, 4:00 PM CDT

Added by Ken Gleason



IMG_0533

Taken on Nov 2, 2023, 9:27 AM CDT

Added on Nov 2, 2023, 4:00 PM CDT

Added by Ken Gleason



IMG_0541

Taken on Nov 2, 2023, 2:42 PM CDT

Added on Nov 2, 2023, 4:00 PM CDT

Added by Ken Gleason



IMG_0536

Taken on Nov 2, 2023, 2:39 PM CDT

Added on Nov 2, 2023, 4:00 PM CDT

Added by Ken Gleason



IMG_0535

Taken on Nov 2, 2023, 2:38 PM CDT

Added on Nov 2, 2023, 4:00 PM CDT

Added by Ken Gleason



IMG_0542

Taken on Nov 2, 2023, 2:44 PM CDT

Added on Nov 3, 2023, 10:57 AM CDT

Added by Ken Gleason



IMG_0539

Taken on Nov 2, 2023, 2:41 PM CDT

Added on Nov 3, 2023, 10:57 AM CDT

Added by Ken Gleason



IMG_0540

Taken on Nov 2, 2023, 2:42 PM CDT

Added on Nov 3, 2023, 10:57 AM CDT

Added by Ken Gleason

Form detail

#61: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Nov 6, 2023
Submitted by	Ken Gleason
Status	Closed
Last update	Nov 6, 2023, 3:33 PM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0.04 inches

🍏 Weather [View Sources](#)

7:00 AM

Mostly Cloudy



Temperature: 52°F

Wind: ↑ 12mph

Humidity: 80%

12:00 PM

Mostly Cloudy



Temperature: 67°F

Wind: → 14mph

Humidity: 67%

4:00 PM

Partly Cloudy



Temperature: 66°F

Wind: → 10mph

Humidity: 58%

Updated Nov 21, 2023 at 3:21 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	3	24	crew started working on LG steel framing of walls on first floor
BP #3 Exc / Site Util - Plainfield Grading	2	16	crew worked on prof rolling and undercuts needed at south parking lot
Totals	5	40	

References

Photos (5)



IMG_0556

Taken on Nov 6, 2023, 11:24 AM CST

Added on Nov 6, 2023, 3:33 PM CST

Added by Ken Gleason



IMG_0554

Taken on Nov 6, 2023, 9:27 AM CST

Added on Nov 6, 2023, 3:33 PM CST

Added by Ken Gleason



IMG_0557

Taken on Nov 6, 2023, 11:24 AM CST

Added on Nov 6, 2023, 3:33 PM CST

Added by Ken Gleason



IMG_0553

Taken on Nov 6, 2023, 9:24 AM CST

Added on Nov 6, 2023, 3:33 PM CST

Added by Ken Gleason



IMG_0555

Taken on Nov 6, 2023, 9:27 AM CST

Added on Nov 6, 2023, 3:33 PM CST

Added by Ken Gleason

Form detail

#62: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Nov 8, 2023
Submitted by	Ken Gleason
Status	Closed
Last update	Nov 8, 2023, 5:33 PM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0.12 inches

🍏 Weather [View Sources](#)

7:00 AM

Cloudy



Temperature: 50°F

Wind: ← 8mph

Humidity: 83%

12:00 PM

Cloudy



Temperature: 58°F

Wind: ← 6mph

Humidity: 81%

4:00 PM

Rain



Temperature: 58°F

Wind: ↓ 5mph

Humidity: 87%

Updated Nov 21, 2023 at 3:22 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	4	32	crew worked on framing LG steel exterior first floor walls
BP #13 Electrical - CSN Electric	1	8	worked on setting up new electric piping and boxes in basement level
BP #3 Exc / Site Util - Plainfield Grading	2	16	crew worked on excavation for sidewalk next to new drive between curb and 111 building
BP #5 Asphalt, C&Gs, Site Concrete - Abbey Paving	3	24	crew worked on south parking lot stone and prep for binder course of pavement to go down
Totals	10	80	

References

Photos (8)



IMG_0571

Taken on Nov 8, 2023, 12:56 PM CST

Added on Nov 8, 2023, 1:08 PM CST

Added by Ken Gleason



IMG_0565

Taken on Nov 8, 2023, 9:20 AM CST

Added on Nov 8, 2023, 1:08 PM CST

Added by Ken Gleason



IMG_0568

Taken on Nov 8, 2023, 12:56 PM CST

Added on Nov 8, 2023, 1:09 PM CST

Added by Ken Gleason



IMG_0567

Taken on Nov 8, 2023, 12:55 PM CST

Added on Nov 8, 2023, 1:09 PM CST

Added by Ken Gleason



IMG_0564

Taken on Nov 8, 2023, 9:16 AM CST

Added on Nov 8, 2023, 1:09 PM CST

Added by Ken Gleason



IMG_0569

Taken on Nov 8, 2023, 12:56 PM CST

Added on Nov 8, 2023, 1:09 PM CST

Added by Ken Gleason



IMG_0566

Taken on Nov 8, 2023, 9:20 AM CST

Added on Nov 8, 2023, 5:33 PM CST

Added by Ken Gleason



IMG_0570

Taken on Nov 8, 2023, 12:56 PM CST

Added on Nov 8, 2023, 5:33 PM CST

Added by Ken Gleason

Form detail

#63: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Nov 9, 2023
Submitted by	Ken Gleason
Status	Closed
Last update	Nov 9, 2023, 4:00 PM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0.04 inches

🍏 Weather [View Sources](#)

7:00 AM

Clear



Temperature: 36°F

Wind: → 5mph

Humidity: 86%

12:00 PM

Clear



Temperature: 54°F

Wind: → 10mph

Humidity: 47%

4:00 PM

Clear



Temperature: 54°F

Wind: → 8mph

Humidity: 46%

Updated Nov 21, 2023 at 3:23 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	4	32	crew worked on installing LG exterior stud walls at first floor today
BP #3 Exc / Site Util - Plainfield Grading	2	16	crew worked on excavation and grading for concrete sidewalk and path to 111 building entry door
BP #13 Electrical - CSN Electric	2	16	crew worked in basement for power as well as exterior lighting for south parking lot.
Totals	8	64	

References

Photos (15)



IMG_0574

Taken on Nov 9, 2023, 10:55 AM CST

Added on Nov 9, 2023, 3:50 PM CST

Added by Ken Gleason



IMG_0580

Taken on Nov 9, 2023, 3:34 PM CST

Added on Nov 9, 2023, 3:50 PM CST

Added by Ken Gleason



IMG_0576

Taken on Nov 9, 2023, 1:59 PM CST

Added on Nov 9, 2023, 3:50 PM CST

Added by Ken Gleason



IMG_0577

Taken on Nov 9, 2023, 3:34 PM CST

Added on Nov 9, 2023, 3:50 PM CST

Added by Ken Gleason



IMG_0582

Taken on Nov 9, 2023, 3:35 PM CST

Added on Nov 9, 2023, 3:50 PM CST

Added by Ken Gleason



IMG_0581

Taken on Nov 9, 2023, 3:34 PM CST

Added on Nov 9, 2023, 3:50 PM CST

Added by Ken Gleason



IMG_0583

Taken on Nov 9, 2023, 3:35 PM CST

Added on Nov 9, 2023, 3:50 PM CST

Added by Ken Gleason



IMG_0579

Taken on Nov 9, 2023, 3:34 PM CST

Added on Nov 9, 2023, 3:50 PM CST

Added by Ken Gleason



IMG_0584

Taken on Nov 9, 2023, 3:36 PM CST

Added on Nov 9, 2023, 3:50 PM CST

Added by Ken Gleason



IMG_0588

Taken on Nov 9, 2023, 3:38 PM CST

Added on Nov 9, 2023, 3:50 PM CST

Added by Ken Gleason



IMG_0578

Taken on Nov 9, 2023, 3:34 PM CST

Added on Nov 9, 2023, 4:00 PM CST

Added by Ken Gleason



IMG_0586

Taken on Nov 9, 2023, 3:37 PM CST

Added on Nov 9, 2023, 4:00 PM CST

Added by Ken Gleason



IMG_0585

Taken on Nov 9, 2023, 3:36 PM CST

Added on Nov 9, 2023, 4:00 PM CST

Added by Ken Gleason



IMG_0587

Taken on Nov 9, 2023, 3:38 PM CST

Added on Nov 9, 2023, 4:00 PM CST

Added by Ken Gleason



IMG_0589

Taken on Nov 9, 2023, 3:38 PM CST

Added on Nov 9, 2023, 4:00 PM CST

Added by Ken Gleason

Form detail

#65: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Nov 13, 2023
Submitted by	Ken Gleason
Status	Closed
Last update	Nov 13, 2023, 3:07 PM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Clear



Temperature: 35°F

Wind: → 4mph

Humidity: 84%

12:00 PM

Clear



Temperature: 61°F

Wind: ↘ 10mph

Humidity: 40%

4:00 PM

Clear



Temperature: 58°F

Wind: ↘ 6mph

Humidity: 35%

Updated Nov 21, 2023 at 3:23 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	4	32	crew worked on LG stud framing first floor wall
BP #3 Exc / Site Util - Plainfield Grading	3	24	crew worked on excavation and pipe work to tie downspouts to storm drain
BP #13 Electrical - CSN Electric	2	16	crew worked on underground piping for site lighting
Totals	9	72	

References

Photos (5)



IMG_0607

Taken on Nov 13, 2023, 2:14 PM CST

Added on Nov 13, 2023, 3:07 PM CST

Added by Ken Gleason



IMG_0608

Taken on Nov 13, 2023, 2:15 PM CST

Added on Nov 13, 2023, 3:07 PM CST

Added by Ken Gleason



IMG_0606

Taken on Nov 13, 2023, 2:14 PM CST

Added on Nov 13, 2023, 3:07 PM CST

Added by Ken Gleason



IMG_0609

Taken on Nov 13, 2023, 2:15 PM CST

Added on Nov 13, 2023, 3:07 PM CST

Added by Ken Gleason



IMG_0610

Taken on Nov 13, 2023, 2:15 PM CST

Added on Nov 13, 2023, 3:07 PM CST

Added by Ken Gleason

Form detail

#66: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Nov 14, 2023
Submitted by	Ken Gleason
Status	Closed
Last update	Nov 15, 2023, 8:02 AM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Clear



Temperature: 30°F

Wind: ↻ 2mph

Humidity: 83%

12:00 PM

Clear



Temperature: 59°F

Wind: ↑ 12mph

Humidity: 34%

4:00 PM

Clear



Temperature: 58°F

Wind: ↑ 7mph

Humidity: 35%

Updated Nov 15, 2023 at 2:02 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	4	32	crew worked on LG stud wall framing
BP #13 Electrical - CSN Electric	2	16	crew worked on exterior site lighting
BP #3 Exc / Site Util - Plainfield Grading	3	24	crew worked on demo of west parking lot
Totals	9	72	

References

Photos (7)



IMG_0615

Taken on Nov 14, 2023, 11:11 AM CST

Added on Nov 14, 2023, 3:22 PM CST

Added by Ken Gleason



IMG_0614

Taken on Nov 14, 2023, 11:10 AM CST

Added on Nov 14, 2023, 3:22 PM CST

Added by Ken Gleason



IMG_0611

Taken on Nov 14, 2023, 11:09 AM CST

Added on Nov 14, 2023, 3:22 PM CST

Added by Ken Gleason



IMG_0613

Taken on Nov 14, 2023, 11:10 AM CST

Added on Nov 14, 2023, 3:22 PM CST

Added by Ken Gleason



IMG_0617

Taken on Nov 14, 2023, 11:12 AM CST

Added on Nov 14, 2023, 3:22 PM CST

Added by Ken Gleason



IMG_0616

Taken on Nov 14, 2023, 11:11 AM CST

Added on Nov 14, 2023, 3:22 PM CST

Added by Ken Gleason



IMG_0612

Taken on Nov 14, 2023, 11:09 AM CST

Added on Nov 15, 2023, 8:02 AM CST

Added by Ken Gleason

Form detail

#67: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Nov 15, 2023
Submitted by	Ken Gleason
Status	Closed
Last update	Nov 15, 2023, 1:21 PM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Clear



Temperature: 35°F

Wind: ↑ 4mph

Humidity: 75%

12:00 PM

Clear



Temperature: 62°F

Wind: ↗ 7mph

Humidity: 45%

4:00 PM

Clear



Temperature: 62°F

Wind: ↗ 4mph

Humidity: 49%

Updated Nov 21, 2023 at 3:25 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	4	32	crew worked on LG steel stud wall framing on first floor
BP #13 Electrical - CSN Electric	1	8	worked on electrical connections for parking lot south
BP #3 Exc / Site Util - Plainfield Grading	6	48	crew worked on grading west lot, proof roll did not pass. undercuts to begin, 2' of soil needs removed and filled with ca 1
Totals	11	88	

References

Photos (10)



IMG_0626

Taken on Nov 15, 2023, 1:20 PM CST
Added on Nov 15, 2023, 1:21 PM CST
Added by Ken Gleason



IMG_0620

Taken on Nov 15, 2023, 11:25 AM CST
Added on Nov 15, 2023, 1:21 PM CST
Added by Ken Gleason



IMG_0621

Taken on Nov 15, 2023, 11:25 AM CST
Added on Nov 15, 2023, 1:21 PM CST
Added by Ken Gleason



IMG_0625

Taken on Nov 15, 2023, 1:20 PM CST
Added on Nov 15, 2023, 1:21 PM CST
Added by Ken Gleason



IMG_0618

Taken on Nov 15, 2023, 10:55 AM CST

Added on Nov 15, 2023, 1:21 PM CST

Added by Ken Gleason



IMG_0623

Taken on Nov 15, 2023, 1:19 PM CST

Added on Nov 15, 2023, 1:21 PM CST

Added by Ken Gleason



IMG_0624

Taken on Nov 15, 2023, 1:19 PM CST

Added on Nov 15, 2023, 1:21 PM CST

Added by Ken Gleason




IMG_0622

Taken on Nov 15, 2023, 11:25 AM CST

Added on Nov 15, 2023, 1:21 PM CST

Added by Ken Gleason

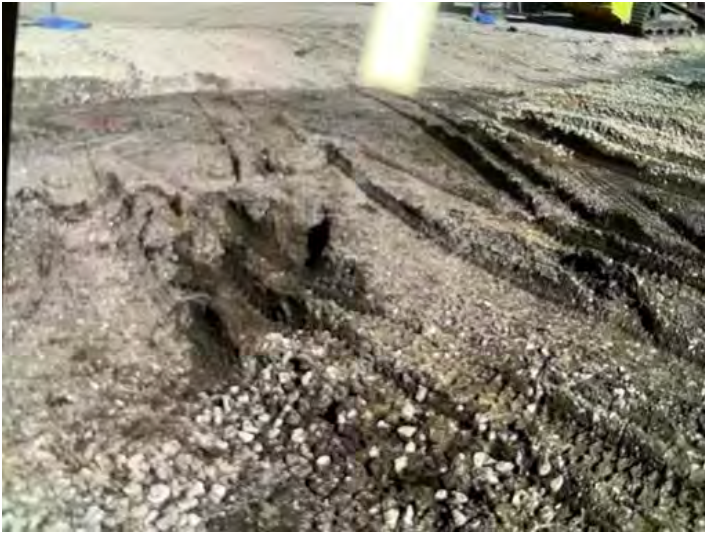

IMG_0627

Taken on Nov 15, 2023, 1:20 PM CST

Added on Nov 15, 2023, 1:21 PM CST

Added by Ken Gleason



IMG_0619

Taken on Nov 15, 2023, 10:55 AM CST

Added on Nov 15, 2023, 1:21 PM CST

Added by Ken Gleason

Form detail

#68: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Nov 16, 2023
Submitted by	Ken Gleason
Status	Closed
Last update	Nov 16, 2023, 3:25 PM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Mostly Clear



Temperature: 40°F

Wind: ↑ 4mph

Humidity: 82%

12:00 PM

Partly Cloudy



Temperature: 64°F

Wind: ↑ 14mph

Humidity: 53%

4:00 PM

Cloudy



Temperature: 62°F

Wind: ↑ 13mph

Humidity: 69%

Updated Nov 21, 2023 at 3:25 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	6	48	crew worked on LG steel wall framing of first floor
BP #3 Exc / Site Util - Plainfield Grading	4	36	crew worked on undercuts of the west lot. lot was proof rolled on Wednesday, soils compaction was tested by TSC and failed the proof roll. recommendation to take out two feet depth of bad soils around entire parking lot area and fill with 3 inch stone for better compaction prior to laying pavement for parking lot.
BP #13 Electrical - CSN Electric	2	16	crew worked on lighting for south parking lot
Totals	12	100	

References

Photos (20)



IMG_0635

Taken on Nov 16, 2023, 11:16 AM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0629

Taken on Nov 16, 2023, 11:15 AM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0631

Taken on Nov 16, 2023, 11:15 AM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0633

Taken on Nov 16, 2023, 11:15 AM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0638

Taken on Nov 16, 2023, 11:36 AM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0636

Taken on Nov 16, 2023, 11:36 AM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0630

Taken on Nov 16, 2023, 11:15 AM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason




IMG_0628

Taken on Nov 16, 2023, 11:14 AM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason

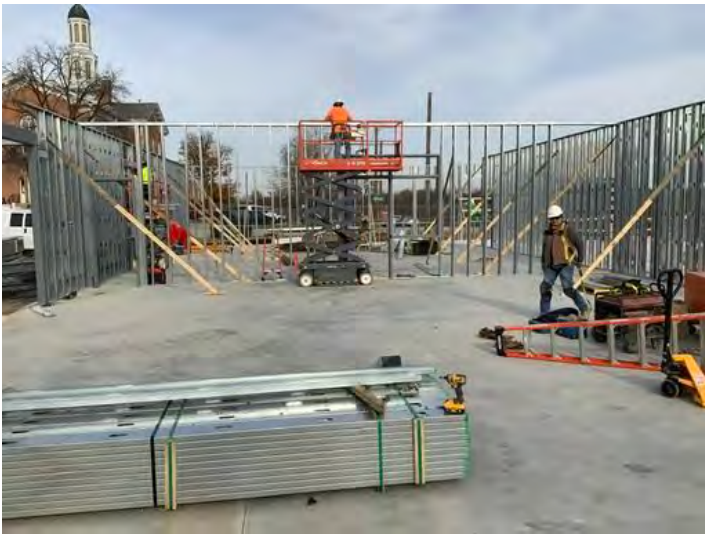

IMG_0634

Taken on Nov 16, 2023, 11:16 AM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0639

Taken on Nov 16, 2023, 11:37 AM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0637

Taken on Nov 16, 2023, 11:36 AM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0642

Taken on Nov 16, 2023, 11:37 AM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0640

Taken on Nov 16, 2023, 11:37 AM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0632

Taken on Nov 16, 2023, 11:15 AM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0641

Taken on Nov 16, 2023, 11:37 AM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0643

Taken on Nov 16, 2023, 2:18 PM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0645

Taken on Nov 16, 2023, 2:19 PM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0646

Taken on Nov 16, 2023, 2:20 PM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0647

Taken on Nov 16, 2023, 2:20 PM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason



IMG_0644

Taken on Nov 16, 2023, 2:19 PM CST

Added on Nov 16, 2023, 3:25 PM CST

Added by Ken Gleason

Form detail

#70: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Nov 20, 2023
Submitted by	Ken Gleason
Status	Closed
Last update	Nov 21, 2023, 1:49 PM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0.24 inches

🍏 Weather [View Sources](#)

7:00 AM

Cloudy



Temperature: 42°F

Wind: ← 12mph

Humidity: 67%

12:00 PM

Cloudy



Temperature: 50°F

Wind: ← 14mph

Humidity: 59%

4:00 PM

Cloudy



Temperature: 48°F

Wind: ← 12mph

Humidity: 61%

Updated Nov 21, 2023 at 7:49 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	7	56	crew worked on interior LG wall framing as well as hanging the dens glass material on exterior of stud walls
BP #3 Exc / Site Util - Plainfield Grading	3	24	crew worked on excavations along west side of site for diagonal parking stalls. broken storm drain line was found and will be replaced, at area under old south driveway entrance of main st.
BP #13 Electrical - CSN Electric	2	16	crew worked on exterior piping for the west parking lot and interior basement piping as well
BP #5 Asphalt, C&Gs, Site Concrete - Abbey Paving	7	56	crew worked on forming and pouring concrete curbs for the west parking lot
Totals	19	152	

References

Photos (17)



IMG_0671

Taken on Nov 20, 2023, 2:37 PM CST
Added on Nov 20, 2023, 3:46 PM CST
Added by Ken Gleason



IMG_0664

Taken on Nov 20, 2023, 8:11 AM CST
Added on Nov 20, 2023, 3:46 PM CST
Added by Ken Gleason



IMG_0677

Taken on Nov 20, 2023, 2:55 PM CST
Added on Nov 20, 2023, 3:47 PM CST
Added by Ken Gleason



IMG_0666

Taken on Nov 20, 2023, 2:34 PM CST
Added on Nov 20, 2023, 3:47 PM CST
Added by Ken Gleason



IMG_0665

Taken on Nov 20, 2023, 2:34 PM CST

Added on Nov 20, 2023, 3:47 PM CST

Added by Ken Gleason



IMG_0672

Taken on Nov 20, 2023, 2:50 PM CST

Added on Nov 20, 2023, 3:47 PM CST

Added by Ken Gleason



IMG_0667

Taken on Nov 20, 2023, 2:36 PM CST

Added on Nov 20, 2023, 3:47 PM CST

Added by Ken Gleason



IMG_0676

Taken on Nov 20, 2023, 2:51 PM CST

Added on Nov 20, 2023, 3:47 PM CST

Added by Ken Gleason



IMG_0668

Taken on Nov 20, 2023, 2:36 PM CST

Added on Nov 20, 2023, 3:47 PM CST

Added by Ken Gleason



IMG_0663

Taken on Nov 20, 2023, 8:10 AM CST

Added on Nov 20, 2023, 3:47 PM CST

Added by Ken Gleason



IMG_0674

Taken on Nov 20, 2023, 2:50 PM CST

Added on Nov 20, 2023, 3:47 PM CST

Added by Ken Gleason



IMG_0670

Taken on Nov 20, 2023, 2:37 PM CST

Added on Nov 21, 2023, 1:49 PM CST

Added by Ken Gleason



IMG_0675

Taken on Nov 20, 2023, 2:51 PM CST

Added on Nov 21, 2023, 1:49 PM CST

Added by Ken Gleason



IMG_0678

Taken on Nov 20, 2023, 2:55 PM CST

Added on Nov 21, 2023, 1:49 PM CST

Added by Ken Gleason



IMG_0669

Taken on Nov 20, 2023, 2:37 PM CST

Added on Nov 21, 2023, 1:49 PM CST

Added by Ken Gleason



IMG_0662

Taken on Nov 20, 2023, 8:09 AM CST

Added on Nov 21, 2023, 1:49 PM CST

Added by Ken Gleason



IMG_0673

Taken on Nov 20, 2023, 2:50 PM CST

Added on Nov 21, 2023, 1:49 PM CST

Added by Ken Gleason

Form detail

#71: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Nov 21, 2023
Submitted by	Ken Gleason
Status	Closed
Last update	Nov 21, 2023, 4:18 PM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0.47 inches

🍏 Weather [View Sources](#)

7:00 AM

Drizzle



Temperature: 42°F

Wind: ↓ 7mph

Humidity: 95%

12:00 PM

Cloudy



Temperature: 41°F

Wind: ↘ 12mph

Humidity: 89%

4:00 PM

Cloudy



Temperature: 40°F

Wind: ↘ 13mph

Humidity: 82%

Updated Nov 21, 2023 at 10:10 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	0	0	crew was not on site today, inclement weather due to rain
BP #3 Exc / Site Util - Plainfield Grading	5	40	crew worked on undercuts needed at entryway from ridge rd to the west parking lot as well as starting to excavate for the concrete pad on east side of building
BP #13 Electrical - CSN Electric	2	16	crew worked on electrical in basement today
Totals	7	56	

References

Photos (11)



IMG_0680

Taken on Nov 21, 2023, 12:25 PM CST

Added on Nov 21, 2023, 4:18 PM CST

Added by Ken Gleason



IMG_0683

Taken on Nov 21, 2023, 12:26 PM CST

Added on Nov 21, 2023, 4:18 PM CST

Added by Ken Gleason



IMG_0682

Taken on Nov 21, 2023, 12:26 PM CST

Added on Nov 21, 2023, 4:18 PM CST

Added by Ken Gleason



IMG_0681

Taken on Nov 21, 2023, 12:26 PM CST

Added on Nov 21, 2023, 4:18 PM CST

Added by Ken Gleason



IMG_0679

Taken on Nov 21, 2023, 12:24 PM CST

Added on Nov 21, 2023, 4:18 PM CST

Added by Ken Gleason



IMG_0685

Taken on Nov 21, 2023, 12:27 PM CST

Added on Nov 21, 2023, 4:18 PM CST

Added by Ken Gleason



IMG_0687

Taken on Nov 21, 2023, 12:27 PM CST

Added on Nov 21, 2023, 4:18 PM CST

Added by Ken Gleason



IMG_0686

Taken on Nov 21, 2023, 12:27 PM CST

Added on Nov 21, 2023, 4:18 PM CST

Added by Ken Gleason



IMG_0684

Taken on Nov 21, 2023, 12:27 PM CST

Added on Nov 21, 2023, 4:18 PM CST

Added by Ken Gleason



IMG_0689

Taken on Nov 21, 2023, 12:28 PM CST

Added on Nov 21, 2023, 4:18 PM CST

Added by Ken Gleason



IMG_0688

Taken on Nov 21, 2023, 12:28 PM CST

Added on Nov 21, 2023, 4:18 PM CST

Added by Ken Gleason

Form detail

#72: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Nov 22, 2023
Submitted by	Ken Gleason
Status	Closed
Last update	Nov 27, 2023, 1:09 PM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0.01 inches

🍏 Weather [View Sources](#)

7:00 AM

Partly Cloudy



Temperature: 32°F

Wind: → 4mph

Humidity: 95%

12:00 PM

Mostly Cloudy



Temperature: 44°F

Wind: → 7mph

Humidity: 77%

4:00 PM

Partly Cloudy



Temperature: 43°F

Wind: ↗ 8mph

Humidity: 74%

Updated Nov 27, 2023 at 7:09 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	7	56	crew worked on LG steel framing and dens glass on first floor
BP #3 Exc / Site Util - Plainfield Grading	6	48	crew worked on undercuts at diagonal parking along min st and preparing the area at concrete pad at east side of basement for mechanicals
BP #5 Asphalt, C&Gs, Site Concrete - Abbey Paving	8	64	crew worked on stone work for the west parking lot
BP #13 Electrical - CSN Electric	2	16	crew worked on underground piping for west parking lot
Totals	23	184	

References

Photos (12)



IMG_0697

Taken on Nov 22, 2023, 8:30 AM CST

Added on Nov 22, 2023, 3:05 PM CST

Added by Ken Gleason



IMG_0705

Taken on Nov 22, 2023, 1:46 PM CST

Added on Nov 27, 2023, 1:08 PM CST

Added by Ken Gleason



IMG_0694

Taken on Nov 22, 2023, 8:26 AM CST

Added on Nov 27, 2023, 1:08 PM CST

Added by Ken Gleason



IMG_0703

Taken on Nov 22, 2023, 1:44 PM CST

Added on Nov 27, 2023, 1:08 PM CST

Added by Ken Gleason



IMG_0706

Taken on Nov 22, 2023, 1:47 PM CST
Added on Nov 27, 2023, 1:08 PM CST
Added by Ken Gleason



IMG_0704

Taken on Nov 22, 2023, 1:45 PM CST
Added on Nov 27, 2023, 1:08 PM CST
Added by Ken Gleason



IMG_0696

Taken on Nov 22, 2023, 8:30 AM CST
Added on Nov 27, 2023, 1:08 PM CST
Added by Ken Gleason



IMG_0695

Taken on Nov 22, 2023, 8:29 AM CST
Added on Nov 27, 2023, 1:08 PM CST
Added by Ken Gleason



IMG_0701

Taken on Nov 22, 2023, 1:44 PM CST
Added on Nov 27, 2023, 1:08 PM CST
Added by Ken Gleason



IMG_0700

Taken on Nov 22, 2023, 1:43 PM CST
Added on Nov 27, 2023, 1:09 PM CST
Added by Ken Gleason



IMG_0702

Taken on Nov 22, 2023, 1:44 PM CST
Added on Nov 27, 2023, 1:09 PM CST
Added by Ken Gleason



IMG_0707

Taken on Nov 22, 2023, 1:47 PM CST
Added on Nov 27, 2023, 1:09 PM CST
Added by Ken Gleason

Form detail

#73: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Nov 27, 2023
Submitted by	Ken Gleason
Status	Closed
Last update	Nov 28, 2023, 8:49 AM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Mostly Clear



Temperature: 21°F

Wind: → 8mph

Humidity: 76%

12:00 PM

Mostly Cloudy



Temperature: 25°F

Wind: → 13mph

Humidity: 71%

4:00 PM

Partly Cloudy



Temperature: 22°F

Wind: → 14mph

Humidity: 72%

Updated Nov 28, 2023 at 2:49 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	4	32	crew worked on LG steel wall framing of first floor
BP #3 Exc / Site Util - Plainfield Grading	2	16	crew worked on backfilling east side of site along with grading parking area along Main Street
BP #13 Electrical - CSN Electric	2	16	crew worked on electrical piping in basement
Totals	8	64	


References

Photos (6)



IMG_0714

Taken on Nov 27, 2023, 1:17 PM CST
Added on Nov 27, 2023, 3:07 PM CST
Added by Ken Gleason

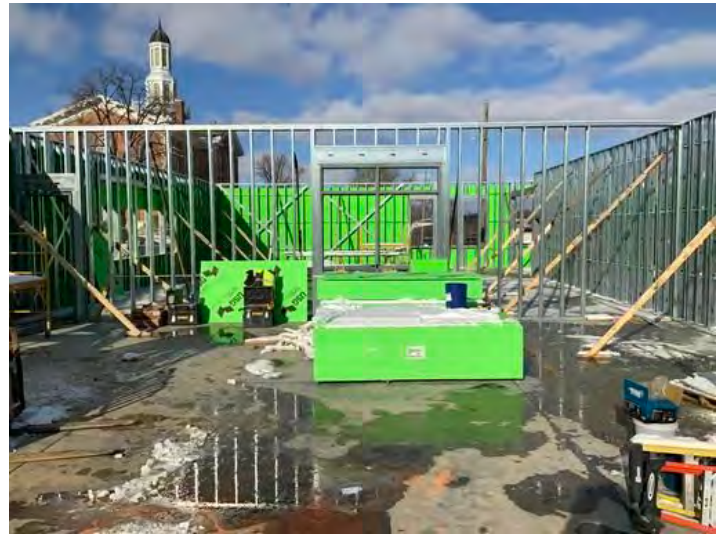

IMG_0718

Taken on Nov 27, 2023, 1:21 PM CST
Added on Nov 27, 2023, 3:07 PM CST
Added by Ken Gleason



IMG_0715

Taken on Nov 27, 2023, 1:17 PM CST
Added on Nov 28, 2023, 8:49 AM CST
Added by Ken Gleason



IMG_0717

Taken on Nov 27, 2023, 1:20 PM CST
Added on Nov 28, 2023, 8:49 AM CST
Added by Ken Gleason



IMG_0719

Taken on Nov 27, 2023, 1:21 PM CST
Added on Nov 28, 2023, 8:49 AM CST
Added by Ken Gleason



IMG_0716

Taken on Nov 27, 2023, 1:20 PM CST
Added on Nov 28, 2023, 8:49 AM CST
Added by Ken Gleason

Form detail

#73: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Nov 27, 2023
Submitted by	Ken Gleason
Status	Closed
Last update	Nov 28, 2023, 8:49 AM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏Weather [View Sources](#)

7:00 AM

Mostly Clear



Temperature: 21°F

Wind: → 8mph

Humidity: 76%

12:00 PM

Mostly Cloudy



Temperature: 25°F

Wind: → 13mph

Humidity: 71%

4:00 PM

Partly Cloudy



Temperature: 22°F

Wind: → 14mph

Humidity: 72%

Updated Nov 28, 2023 at 2:49 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	4	32	crew worked on LG steel wall framing of first floor
BP #3 Exc / Site Util - Plainfield Grading	2	16	crew worked on backfilling east side of site along with grading parking area along Main Street
BP #13 Electrical - CSN Electric	2	16	crew worked on electrical piping in basement
Totals	8	64	


References

Photos (6)



IMG_0714

Taken on Nov 27, 2023, 1:17 PM CST
Added on Nov 27, 2023, 3:07 PM CST
Added by Ken Gleason

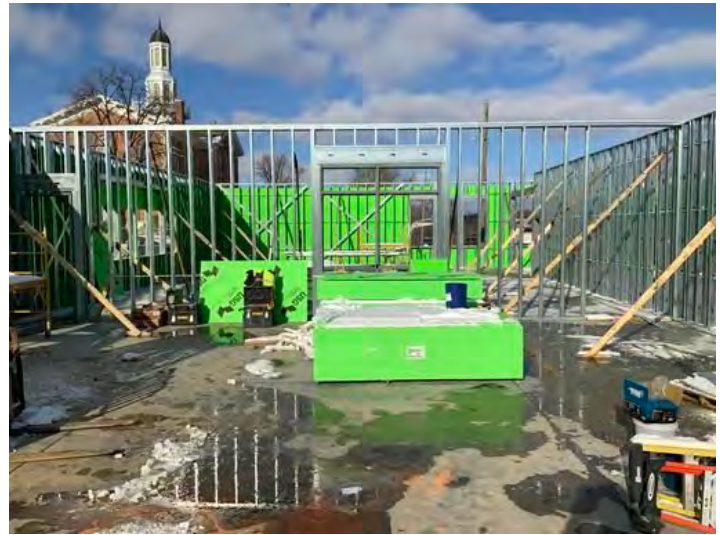

IMG_0718

Taken on Nov 27, 2023, 1:21 PM CST
Added on Nov 27, 2023, 3:07 PM CST
Added by Ken Gleason



IMG_0715

Taken on Nov 27, 2023, 1:17 PM CST
Added on Nov 28, 2023, 8:49 AM CST
Added by Ken Gleason



IMG_0717

Taken on Nov 27, 2023, 1:20 PM CST
Added on Nov 28, 2023, 8:49 AM CST
Added by Ken Gleason



IMG_0719

Taken on Nov 27, 2023, 1:21 PM CST

Added on Nov 28, 2023, 8:49 AM CST

Added by Ken Gleason



IMG_0716

Taken on Nov 27, 2023, 1:20 PM CST

Added on Nov 28, 2023, 8:49 AM CST

Added by Ken Gleason

Form detail

#75: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Nov 29, 2023
Submitted by	Ken Gleason
Status	Closed
Last update	Nov 30, 2023, 9:15 AM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Clear



Temperature: 20°F

Wind: ↗ 6mph

Humidity: 81%

12:00 PM

Clear



Temperature: 36°F

Wind: ↗ 8mph

Humidity: 72%

4:00 PM

Clear



Temperature: 37°F

Wind: ↗ 6mph

Humidity: 76%

Updated Nov 30, 2023 at 3:15 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	6	48	crew worked on setting trusses today
BP #13 Electrical - CSN Electric	2	16	crew worked on electrical piping in the basement
BP #5 Asphalt, C&Gs, Site Concrete - Abbey Paving	8	64	crew worked on forms and pouring of concrete for sidewalks around west parking lot area
Totals	16	128	

References

Photos (12)



IMG_0736

Taken on Nov 29, 2023, 8:34 AM CST

Added on Nov 30, 2023, 9:15 AM CST

Added by Ken Gleason



IMG_0734

Taken on Nov 29, 2023, 8:32 AM CST

Added on Nov 30, 2023, 9:15 AM CST

Added by Ken Gleason



IMG_0738

Taken on Nov 29, 2023, 8:52 AM CST

Added on Nov 29, 2023, 1:38 PM CST

Added by Ken Gleason



IMG_0742

Taken on Nov 29, 2023, 12:39 PM CST

Added on Nov 30, 2023, 9:15 AM CST

Added by Ken Gleason



IMG_0732

Taken on Nov 29, 2023, 8:32 AM CST

Added on Nov 29, 2023, 1:38 PM CST

Added by Ken Gleason



IMG_0739

Taken on Nov 29, 2023, 8:53 AM CST

Added on Nov 30, 2023, 9:15 AM CST

Added by Ken Gleason



IMG_0737

Taken on Nov 29, 2023, 8:35 AM CST

Added on Nov 30, 2023, 9:15 AM CST

Added by Ken Gleason



IMG_0741

Taken on Nov 29, 2023, 12:39 PM CST

Added on Nov 29, 2023, 1:38 PM CST

Added by Ken Gleason



IMG_0743

Taken on Nov 29, 2023, 12:41 PM CST

Added on Nov 29, 2023, 1:38 PM CST

Added by Ken Gleason



IMG_0733

Taken on Nov 29, 2023, 8:32 AM CST

Added on Nov 30, 2023, 9:15 AM CST

Added by Ken Gleason



IMG_0735

Taken on Nov 29, 2023, 8:34 AM CST

Added on Nov 30, 2023, 9:15 AM CST

Added by Ken Gleason



IMG_0731

Taken on Nov 29, 2023, 8:30 AM CST

Added on Nov 29, 2023, 1:38 PM CST

Added by Ken Gleason

Form detail

#76: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Nov 30, 2023
Submitted by	Ken Gleason
Status	Closed
Last update	Nov 30, 2023, 2:59 PM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0.01 inches

🍏 Weather [View Sources](#)

7:00 AM

Cloudy



Temperature: 32°F

Wind: ↑ 7mph

Humidity: 86%

12:00 PM

Partly Cloudy



Temperature: 49°F

Wind: ↗ 12mph

Humidity: 68%

4:00 PM

Mostly Cloudy



Temperature: 48°F

Wind: ↗ 6mph

Humidity: 77%

Updated Dec 5, 2023 at 3:20 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	6	48	crew worked on setting trusses today
BP #5 Asphalt, C&Gs, Site Concrete - Abbey Paving	9	72	crew worked on removing concrete forms and paving west parking lot
BP #13 Electrical - CSN Electric	2	16	crew worked on electrical piping in basement
Totals	17	136	

References

Photos (7)



IMG_0750

Taken on Nov 30, 2023, 12:51 PM CST

Added on Nov 30, 2023, 2:59 PM CST

Added by Ken Gleason



IMG_0747

Taken on Nov 30, 2023, 12:40 PM CST

Added on Nov 30, 2023, 2:59 PM CST

Added by Ken Gleason



IMG_0746

Taken on Nov 30, 2023, 9:10 AM CST

Added on Nov 30, 2023, 2:59 PM CST

Added by Ken Gleason



IMG_0745

Taken on Nov 30, 2023, 9:09 AM CST

Added on Nov 30, 2023, 2:59 PM CST

Added by Ken Gleason



IMG_0749

Taken on Nov 30, 2023, 12:50 PM CST

Added on Nov 30, 2023, 2:59 PM CST

Added by Ken Gleason



IMG_0748

Taken on Nov 30, 2023, 12:49 PM CST

Added on Nov 30, 2023, 2:59 PM CST

Added by Ken Gleason



IMG_0751

Taken on Nov 30, 2023, 12:51 PM CST

Added on Nov 30, 2023, 2:59 PM CST

Added by Ken Gleason

SECTION 5: ARCHITECTURAL & ENGINEERING FIELD REPORTS



FIELD OBSERVATION CONFIRMATION

Date: 2023-11-07 Observation Time: 3:11 PM
Re: KENDALL COUNTY PHASE 1 CLERK BLDG Weather Conditions: 50F
Client: Kendall County Partly Cloudy
Project: 221071 --
Prepared By: Lauren Kiley Phone: 630.896.4678
Cordogan Clark & Associates Fax: 630.896.4987

Field Report Number: 231107

Est % Completion: 23% Conformance With Schedule (+/-): 0 days

Work In Progress: Exterior wall metal stud framing, electrical service and panel work, site concrete curbs, gutters and sub base prep for asphalt.

Observations:

1. Exterior stud wall framing work is in progress. Stud box headers are installed at windows.
2. Electrical work is in progress in Elec 003A. Transformers and panel installation is in progress.
3. Site concrete curbs and gutters have been formed and poured for south parking lot, and drive up to the west parking lot.
4. Existing ComEd utility pole to remain, curb and gutter along west side of drive shifted to accommodate
5. Concrete slab on grade has been poured.
6. 2" concrete topper on precast was replaced with self leveling concrete to align with adjacent S.O.G.
7. Water main work on Fox Street and infill work is in progress.
8. Wide flange steel hoist beam for elevator appears to be installed.

Items to Verify:

1. Verify curb cuts for accessible path meets ADA requirements.
2. Coordinate urethane flooring coating in Basement with floor mounted electrical equipment.

Information Or Action Required:

1. Detail for window jamb does not align with detail 7/A9.2. Sheathing and insulation cannot be installed as shown, further discussion needed to confirm building insulation is continuous.
2. In the 'soft' area of self leveler on precast there appears to be some damage, provide patch over these areas.

Attachments:

Progress Photos

PHOTOGRAPHIC DOCUMENTATION

Date: 2023-11-07

Observation Time: 3:11 PM

Re: KENDALL COUNTY PHASE 1 CLERK BLDG
Project: 221071

Weather Conditions: 50F
Partly Cloudy



Metal Stud Wall Bracing



Metal Stud Jamb at Windows



Curb and Gutter Shifted along West Side of Drive



Electrical Equipment in Elec 003A

PHOTOGRAPHIC DOCUMENTATION

Date: 2023-11-07

Observation Time: 3:11 PM

Re: KENDALL COUNTY PHASE 1 CLERK BLDG
Project: 221071

Weather Conditions: 50F
Partly Cloudy



Metal Stud Window Head



Overall Progress of Framing



Slab on Grade Pour



Curb Cut at Accessible Path



Self Leveling Damaged in Soft Area



Curb Gutter Extent at West Lot



Steel Beam for Hoistway



Water Main Connection Work

FIELD OBSERVATION CONFIRMATION

Date: 2023-11-21 Observation Time: 3:41 PM
Re: KENDALL COUNTY PHASE 1 CLERK BLDG Weather Conditions: 43F
Client: Kendall County Overcast
Project: 221071 --
Prepared By: Lauren Kiley Phone: 630.896.4678
Cordogan Clark & Associates Fax: 630.896.4987

Field Report Number: 231121

Est % Completion: 25% Conformance With Schedule (+/-): 0 days

Work In Progress: West parking lot curbs and gutters, exterior wall sheathing, site prep for mechanical equipment pad.

Observations:

1. West parking lot concrete curbs and gutters have been poured, sub base prep is in progress for upcoming asphalt pour. South parking lot is complete and owner is currently using.
2. Steel columns and beams at entry and along grid line 3 have been installed.
3. Structural metal stud framing is in progress and near completion.
4. Gypsum board exterior wall sheathing is being installed.
5. Plumbing line appears to have been cored through concrete wall on north side of Sprinkler Room.
6. Light pole concrete poles appear to be in place and poured.
7. Site appears to be excavated for concrete mechanical pad on east, expected to be poured this week.
8. Hollow metal door frame installation is in progress.

Items to Verify:

1. Verify the curb grading is correct at drive island in west parking lot, as it appears to be high.
2. Verify plan dimensions of metal stud framing at entry, as they do not appear to align equally with the steel beams.
3. Architect to verify locations of intermediate roof gutters along the East.
4. Verify exposed height of concrete light pole bases is 24".

Information Or Action Required:

1. Curb and gutter along west side drive, center island and north section, do not align. Confirm in field and further discussion is needed to remedy.
2. Steel beam along grid line 3 will need to be lowered to align with top of metal framing to allow trusses to span across per email from structural on 11/13/2023.
3. Steel angle on south west corner of entry appears to be bent, modify to be straight so it does not effect masonry veneer installation per detail 3/A6.4.
4. Coordinate electrical conduits for car chargers on south with masonry installation, and verify the conduit is out far enough so it does not cause conflict.

Attachments:

Progress Photos

PHOTOGRAPHIC DOCUMENTATION

Date: 2023-11-21

Observation Time: 3:41 PM

Re: KENDALL COUNTY PHASE 1 CLERK BLDG
Project: 221071

Weather Conditions: 43F
Overcast



Steel Beam and Columns along 3



Curbs and Gutters along West Drive



Steel Beams and Columns at Entry



Plumbing Pipe Stub Up on North

PHOTOGRAPHIC DOCUMENTATION

Date: 2023-11-21

Observation Time: 3:41 PM

Re: KENDALL COUNTY PHASE 1 CLERK BLDG
Project: 221071

Weather Conditions: 43F
Overcast



West Parking Lot Progress



Sheathing & Conduits on South



Mechanical Pad Site Prep




Curb Grading at West Lot Island



Bent Steel Angle at Entry



Light Pole Bases

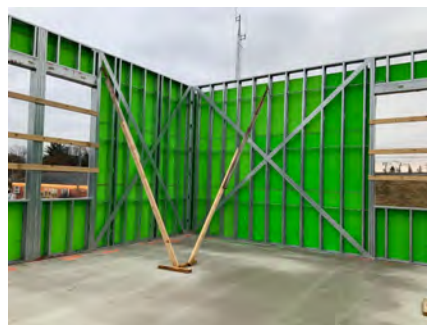

Stud Framing Cross Bracing



Overall Building Progress



CORDOGAN CLARK

ARCHITECTURE ■ ENGINEERING ■ CONSTRUCTION



960 Ridgeway Avenue
Aurora, Illinois 60506
T: 630.896.4678
F: 630.896.4987

Aurora, Illinois
Chicago, Illinois
Davenport, Iowa
Lafayette, Indiana
St. Louis, Missouri
Sawyer, Michigan
Madrid, Spain

cordoganclark.com
