

Form detail

#152: Weekly Report

**Forms**

Location	Kendall County New Office Building
Form date	Mar 29, 2024
Description	
Due date	
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 29, 2024, 12:42 PM CDT
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information


Kendall County New Office Project. CCCS Project Number 221071.

1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	2	8	-	crew worked on ceiling grids and tiles this week, finishing up with drywall and taping, site clean up
-	BP #6 Masonry - Jimmy'z Masonry	-	10	80	-	crew worked on install of brick/stone along south and east walls this week
-	BP #8 Painting - Nedrow Painting	-	1	8	-	worked on first coat of walls on first floor, masking off basement fixtures at ceiling and getting started with paint in the basement as well.
-	BP #10 Fire Protection - CL Doucette Inc	-	1	8	-	worked on adjustments to fire protection piping on first floor today as well as finishing up with fire caulking of penetrations at wall and roof deck
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on electrical wiring at first floor this week and getting started with install of fixtures at first floor as well.
Totals:			17	128	0	

References

Photos (22)

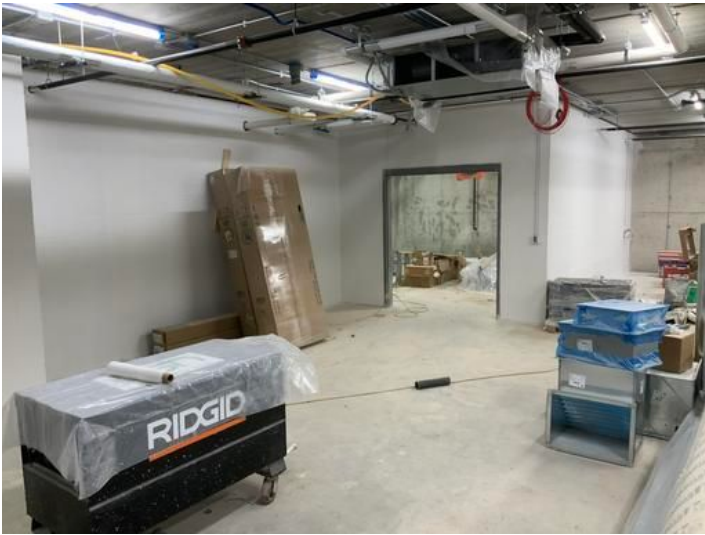

IMG_1532

Taken on Mar 29, 2024, 8:31 AM CDT
Added on Mar 29, 2024, 12:41 PM CDT
Added by Ken Gleason



IMG_1530

Taken on Mar 29, 2024, 8:26 AM CDT
Added on Mar 29, 2024, 12:41 PM CDT
Added by Ken Gleason



IMG_1531

Taken on Mar 29, 2024, 8:27 AM CDT
Added on Mar 29, 2024, 12:41 PM CDT
Added by Ken Gleason



IMG_1534

Taken on Mar 29, 2024, 8:32 AM CDT
Added on Mar 29, 2024, 12:41 PM CDT
Added by Ken Gleason



IMG_1533

Taken on Mar 29, 2024, 8:32 AM CDT
Added on Mar 29, 2024, 12:41 PM CDT
Added by Ken Gleason



IMG_1535

Taken on Mar 29, 2024, 11:11 AM CDT
Added on Mar 29, 2024, 12:41 PM CDT
Added by Ken Gleason



IMG_1540

Taken on Mar 29, 2024, 11:18 AM CDT
Added on Mar 29, 2024, 12:42 PM CDT
Added by Ken Gleason



IMG_1538

Taken on Mar 29, 2024, 11:13 AM CDT
Added on Mar 29, 2024, 12:42 PM CDT
Added by Ken Gleason



IMG_1539

Taken on Mar 29, 2024, 11:18 AM CDT
Added on Mar 29, 2024, 12:42 PM CDT
Added by Ken Gleason



IMG_1541

Taken on Mar 29, 2024, 11:18 AM CDT
Added on Mar 29, 2024, 12:42 PM CDT
Added by Ken Gleason



IMG_1536

Taken on Mar 29, 2024, 11:11 AM CDT
Added on Mar 29, 2024, 12:42 PM CDT
Added by Ken Gleason



IMG_1537

Taken on Mar 29, 2024, 11:12 AM CDT
Added on Mar 29, 2024, 12:42 PM CDT
Added by Ken Gleason



IMG_1542

Taken on Mar 29, 2024, 11:18 AM CDT
Added on Mar 29, 2024, 12:42 PM CDT
Added by Ken Gleason



IMG_1543

Taken on Mar 29, 2024, 11:19 AM CDT
Added on Mar 29, 2024, 12:42 PM CDT
Added by Ken Gleason



IMG_1545

Taken on Mar 29, 2024, 11:19 AM CDT
Added on Mar 29, 2024, 12:42 PM CDT
Added by Ken Gleason



IMG_1544

Taken on Mar 29, 2024, 11:19 AM CDT
Added on Mar 29, 2024, 12:42 PM CDT
Added by Ken Gleason



IMG_1546

Taken on Mar 29, 2024, 11:19 AM CDT

Added on Mar 29, 2024, 12:42 PM CDT

Added by Ken Gleason



IMG_1547

Taken on Mar 29, 2024, 11:20 AM CDT

Added on Mar 29, 2024, 12:42 PM CDT

Added by Ken Gleason



IMG_1549

Taken on Mar 29, 2024, 11:20 AM CDT

Added on Mar 29, 2024, 12:42 PM CDT

Added by Ken Gleason



IMG_1548

Taken on Mar 29, 2024, 11:20 AM CDT

Added on Mar 29, 2024, 12:42 PM CDT

Added by Ken Gleason



IMG_1550

Taken on Mar 29, 2024, 11:21 AM CDT

Added on Mar 29, 2024, 12:42 PM CDT

Added by Ken Gleason



IMG_1551

Taken on Mar 29, 2024, 11:21 AM CDT

Added on Mar 29, 2024, 12:42 PM CDT

Added by Ken Gleason
