

Form detail

#182: Weekly Report

**Forms**

Location	Kendall County New Office Building
Form date	May 10, 2024
Description	
Due date	
Submitted by	Ken Gleason
Status	Closed
Last update	May 10, 2024, 1:32 PM CDT
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	1	8	-	worked on trim/crown moldings in vestibule area today
-	BP #6 Masonry - Jimmy'z Masonry	-	3	24	-	crew worked on expansion joint filling today at exterior as well as CMU corner joints at foundation walls.
-	BP #7 Roofing - Filotto Roofing	-	2	4	-	crew worked on flat roof at front entry above vestibule today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	6	48	-	crew worked on setting tracks for the terrazzo flooring in lobby as well as tile flooring and walls in bathrooms on first floor
-	BP #13 Electrical - CSN Electric	-	2	16	-	crew worked on electrical wiring and trim in basement today
Totals:			14	100	0	

References


Photos (8)




First Floor Bath Wall Tile
Taken on May 10, 2024, 1:04 PM CDT
Added on May 10, 2024, 1:17 PM CDT
Added by Ken Gleason



Expansion Joint Filling
Taken on May 10, 2024, 12:58 PM CDT
Added on May 10, 2024, 1:17 PM CDT
Added by Ken Gleason

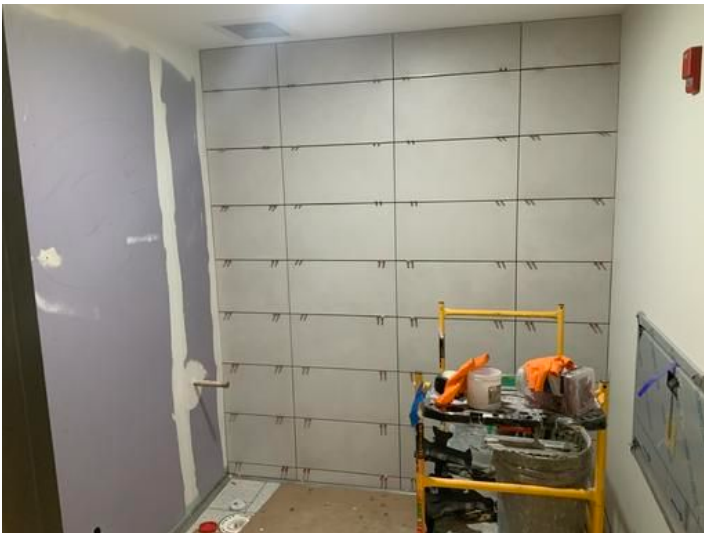

First Floor Bath Wall Tile
Taken on May 10, 2024, 1:05 PM CDT
Added on May 10, 2024, 1:17 PM CDT
Added by Ken Gleason

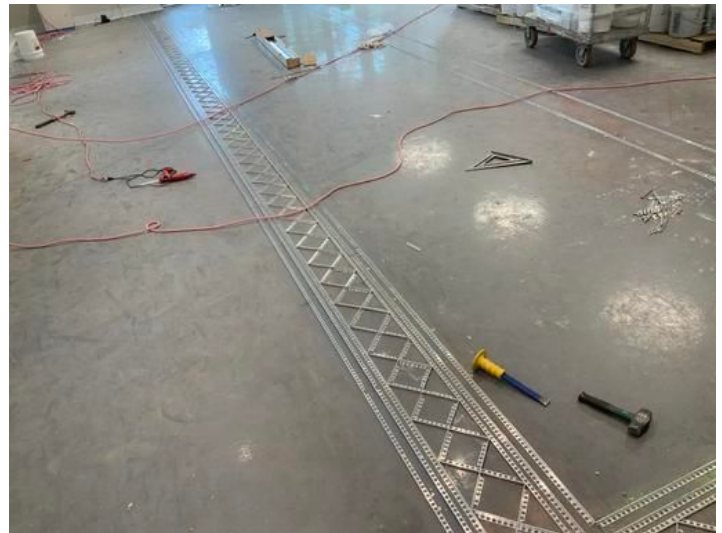

Lobby Terrazzo Tracks
Taken on May 10, 2024, 1:03 PM CDT
Added on May 10, 2024, 1:17 PM CDT
Added by Ken Gleason



Basement Bathroom Grab Bars
Taken on May 9, 2024, 2:53 PM CDT
Added on May 10, 2024, 1:17 PM CDT
Added by Ken Gleason



Lobby Terrazzo Tracks
Taken on May 10, 2024, 1:03 PM CDT
Added on May 10, 2024, 1:17 PM CDT
Added by Ken Gleason



Front Entry Flat Roof
Taken on May 10, 2024, 12:58 PM CDT
Added on May 10, 2024, 1:17 PM CDT
Added by Ken Gleason



Lobby Terrazzo Tracks
Taken on May 10, 2024, 1:03 PM CDT
Added on May 10, 2024, 1:18 PM CDT
Added by Ken Gleason
