

MONTHLY PROGRESS REPORT

# KENDALL COUNTY

NEW OFFICE BUILDING

MAY, 2024





## May Monthly Report

---

Construction Management Services

June 2024

---

### **Contents**

---

Section 1: Project Update

Section 2: Project Cost Report

Section 3: Schedule

Section 4: Construction Field Reports and Photos

Section 5: Architectural & Engineering Field Reports



SECTION 1



## **Kendall County**

### **New Office Building**

Monthly Project Summary 5/31/24  
Work Completed in May 2024

To date we have completed the following activities:

- Flooring – Terrazzo, Vinyl Tile, Carpet
- Painting
- Doors/Finish Carpentry
- Concrete Planters

We are currently progressing on the following activities:

- Elevator Install
- MEP Trim Work
- Roof Overhead Returns/Soffit/Fascia/Gutters
- Flooring – Epoxy
- Casework
- Paint Touch Ups & Final Finishes
- Generator Install & Testing
- FFE Install

The following phases of construction scheduled for the near future:

- Site Excavation
- Concrete – Flatwork/Asphalt Patching
- Landscaping
- Technology Implementation
- Punchlist
- Inspections/Testing/Training



SECTION 2



## Kendall County – New Office Building

### Cost Report & Contingency Reductions

PCO #	Date Approved By Owner	Contractor	Description	Potential Contingency Reduction Amount	Contingency Reduction Amount Approved	Comments
<b>CONTINGENCY REDUCTIONS APPROVED IN OCTOBER 2023:</b>					<b>\$45,035</b>	
<b>CONTINGENCY REDUCTIONS APPROVED IN NOVEMBER 2023:</b>					<b>\$75,448</b>	
<b>CONTINGENCY REDUCTIONS APPROVED IN DECEMBER 2023:</b>					<b>\$6,580</b>	
<b>CONTINGENCY REDUCTIONS APPROVED IN JANUARY 2024:</b>					<b>\$145,632</b>	
<b>CONTINGENCY REDUCTIONS APPROVED IN FEBRUARY 2024:</b>					<b>\$22,713</b>	
<b>CONTINGENCY REDUCTIONS APPROVED IN MARCH 2024:</b>					<b>\$38,046</b>	
<b>CONTINGENCY REDUCTIONS APPROVED IN APRIL 2024:</b>					<b>\$18,295</b>	
<b>CONTINGENCY REDUCTIONS APPROVED IN MAY 2024:</b>					<b>\$17,348</b>	
		Plainfield Grading	Excavation for dampproofing at old fire station, move roof drains, repair clay storm sewer, dig out wet areas along west side Main St & put in CA6, and add'l excavation & backfill for ramp in lieu of stairs.	\$11,517	\$11,517	This work is approved. Contractor was late in sending in paperwork.
		Otis Elevator	Remobilization due to permanent power not being installed.	\$2,000	\$2,000	
		Abbey Paving	Credit to remove wear course and pavers prep	(\$51,535)	(\$51,535)	
		Twin Oaks Landscaping	PR-19 Add'l landscaping & credit for paver install	\$5,859	\$5,859	\$3,000 was shown on Twin Oaks' pay application for labor to install pavers.
		Premium Concrete	Added framing per PR 021 Planter Revisions & concrete work credit	(\$844)	(\$844)	
<b>CONTINGENCY REDUCTIONS TO BE APPROVED IN JUNE 2024:</b>					<b>(\$33,003)</b>	



SECTION 3





Project #	221071					Construction Schedule						
Project Title:	Kendall Co Phase 1 County Building Project					Start Date	Projected Finish	Total Work Days	Work Days Elapsed	Sched % Complete	Baseline Deviation	% Deviation
Location:	107 W. Fox St. Yorkville, IL.					6/28/2023	5/31/2024	338				



Upcoming Milestones				Upcoming Long-Lead Time Material					Report #			46
Ceilings	Paiting Touchups	Flooring	Punchlist	Flagpoles	Spanlite Glass	Mech. Equipment	Inspection Testing	FFE	From:	6/2/2024	to	6/29/2024
5/10/2024	5/28/2024	5/31/2024	6/3/2024	8/30/2024	6/10/2024	Gen-5/24/24	6/3/2024	5/22/2024	Prepared:	6/5/2024	by	KG

Item	Construction Activity Description	Resp	Arch Owner Action Req.	Week 45							Week 46							Week 47							Week 48						
				Week Ending: 06/08							Week Ending: 06/15							Week Ending: 06/22							Week Ending: 06/29						
				Su	M	T	W	TH	F	Sa	Su	M	T	W	TH	F	Sa	Su	M	T	W	TH	F	Sa	Su	M	T	W	TH	F	Sa
				06/02	06/03	06/04	06/05	06/06	06/07	06/08	06/09	06/10	06/11	06/12	06/13	06/14	06/15	06/16	06/17	06/18	06/19	06/20	06/21	06/22	06/23	06/24	06/25	06/26	06/27	06/28	06/29
1	Soffit & Fascia, Gutter & Downspouts	Filotto Roofing			X	X	X	X	X																						
2	Casework	Lite Construction			X	X	X	X	X																						
3	MEP Trimwork	Jensens/CSN/Omega			X	X	X	X	X																						
4	FF&E Instal	Cordogan Clark			X	X	X	X	X																						
5	Doors/Finish Carpentry	Lite Construction			X	X	X	X	X			X	X																		
6	Paint Touch Ups & Final Finishes	Nedrow Painting						X	X			X	X	X	X	X															
7	Generator Instal & Testing	CSN Electric										X	X	X	X	X															
8	Excavation - Site work & Final Grade	Plainfield Ex							X			X	X	X	X	X															
9	Concrete - Flatwork/Asphalt Patching	Abbey Paving										X	X	X	X	X															
10	Flooring	TSI Flooring										X	X	X	X	X															
11	Technology Implementation	IT										X	X	X	X	X															
12	Landscaping	Twin Oaks										X	X	X	X	X															
13	Punchlist	By Trade										X	X	X	X	X															
14	Insepctions/Testing/Training	By Trade										X	X	X	X	X															
15	Final Clean	Lite Construction														X	X	X													
16	Lobby Glass	CSN Electric										X																			
17	Ribbon Cutting Ceremony																			XX											



SECTION 4



## Form detail

## #175: Daily Report



## Forms

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 1, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 2, 2024, 9:18 AM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos


## Supporting information


Kendall County New Office Project. CCCS Project Number 221071.


## Weather

🌧️ Rain: 0.08 inches

🍏 Weather [View Sources](#)

**7:00 AM**    **Mostly Clear**  
 Temperature: 62°F  
 Wind: → 7mph  
 Humidity: 85%

**12:00 PM**    **Mostly Clear**  
 Temperature: 71°F  
 Wind: → 12mph  
 Humidity: 42%

**4:00 PM**    **Mostly Clear**  
 Temperature: 76°F  
 Wind: ↘ 8mph  
 Humidity: 29%

Updated May 2, 2024 at 2:18 PM



## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	3	24	-	crew worked on install of casework at clerk and recorder dept today as well as frieze boards on north side of site
-	BP #3 Exc / Site Util - Plainfield Grading	-	3	24	-	crew worked on site grading at north and south of site as well as excavation for planters at west side.
-	BP #8 Painting - Nedrow Painting	-	1	8	-	worked on painting in basement today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	2	16	-	crew worked on prep work in the lobby area for the terrazzo flooring area today
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on trim work at first floor today as well as starting to set the exterior light poles today
<b>Totals:</b>			<b>12</b>	<b>96</b>	<b>0</b>	

## References

### Photos (7)



IMG\_1792

**Taken on** May 1, 2024, 7:58 AM CDT

**Added on** May 1, 2024, 1:17 PM CDT

**Added by** Ken Gleason



IMG\_1793

**Taken on** May 1, 2024, 11:43 AM CDT

**Added on** May 1, 2024, 1:17 PM CDT

**Added by** Ken Gleason




IMG\_1794

**Taken on** May 1, 2024, 11:44 AM CDT

**Added on** May 1, 2024, 1:17 PM CDT

**Added by** Ken Gleason

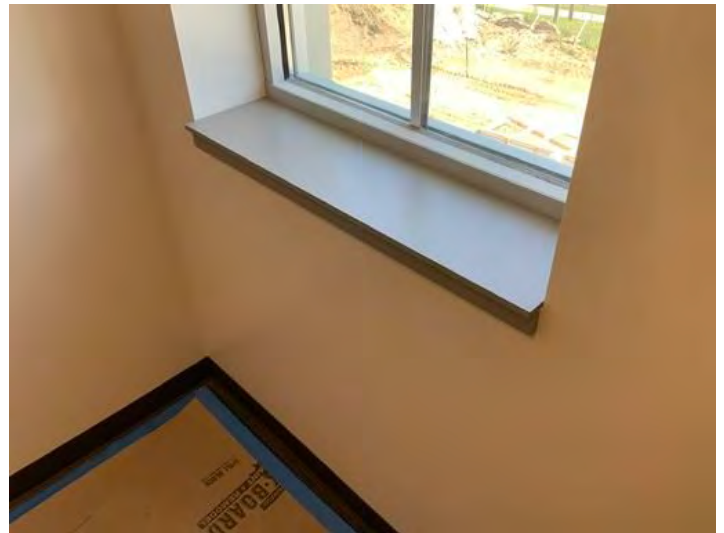

IMG\_1796

**Taken on** May 1, 2024, 12:36 PM CDT

**Added on** May 1, 2024, 1:17 PM CDT

**Added by** Ken Gleason





IMG\_1795

**Taken on** May 1, 2024, 11:44 AM CDT

**Added on** May 1, 2024, 1:17 PM CDT

**Added by** Ken Gleason



IMG\_1798

**Taken on** May 1, 2024, 1:01 PM CDT

**Added on** May 1, 2024, 1:17 PM CDT

**Added by** Ken Gleason



IMG\_1797

**Taken on** May 1, 2024, 1:01 PM CDT

**Added on** May 1, 2024, 1:17 PM CDT

**Added by** Ken Gleason

## Form detail

## #176: Daily Report



## Forms

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 2, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 2, 2024, 3:58 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos

## Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

## Weather

🌧️ Rain: 0.43 inches

🍏 Weather [View Sources](#)

7:00 AM

Mostly Cloudy



Temperature: 56°F

Wind: ← 7mph

Humidity: 64%

12:00 PM

Mostly Cloudy



Temperature: 75°F

Wind: ↻ 10mph

Humidity: 55%

4:00 PM

Cloudy



Temperature: 76°F

Wind: ↑ 7mph

Humidity: 66%

Updated May 6, 2024 at 9:50 PM



## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	3	24	-	ceiling grid in stairway and IT room worked on today, along with casework ballistic glass for desks at clerks space.
-	BP #3 Exc / Site Util - Plainfield Grading	-	2	16	-	crew worked on grading around site and excavation for planters at west side of site
-	BP #8 Painting - Nedrow Painting	-	3	24	-	crew worked on paint in basement today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	4	32	-	crew worked on lobby area with primer as well as bathrooms on first floor to prep for tile work
-	BP #13 Electrical - CSN Electric	-	3	30	-	crew worked on exterior lighting as well as trim work on first floor today
<b>Totals:</b>			<b>15</b>	<b>126</b>	<b>0</b>	

## References

### Photos (15)



IMG\_1799

**Taken on** May 2, 2024, 10:59 AM CDT

**Added on** May 2, 2024, 3:58 PM CDT

**Added by** Ken Gleason



IMG\_1801

**Taken on** May 2, 2024, 11:39 AM CDT

**Added on** May 2, 2024, 3:58 PM CDT

**Added by** Ken Gleason



IMG\_1800

**Taken on** May 2, 2024, 10:59 AM CDT

**Added on** May 2, 2024, 3:58 PM CDT

**Added by** Ken Gleason



IMG\_1802

**Taken on** May 2, 2024, 11:39 AM CDT

**Added on** May 2, 2024, 3:58 PM CDT

**Added by** Ken Gleason



IMG\_1803

**Taken on** May 2, 2024, 2:12 PM CDT

**Added on** May 2, 2024, 3:58 PM CDT

**Added by** Ken Gleason



IMG\_1806

**Taken on** May 2, 2024, 2:13 PM CDT

**Added on** May 2, 2024, 3:58 PM CDT

**Added by** Ken Gleason



IMG\_1807

**Taken on** May 2, 2024, 2:13 PM CDT

**Added on** May 2, 2024, 3:58 PM CDT

**Added by** Ken Gleason



IMG\_1808

**Taken on** May 2, 2024, 2:14 PM CDT

**Added on** May 2, 2024, 3:58 PM CDT

**Added by** Ken Gleason






IMG\_1810

**Taken on** May 2, 2024, 2:15 PM CDT  
**Added on** May 2, 2024, 3:58 PM CDT  
**Added by** Ken Gleason



IMG\_1809

**Taken on** May 2, 2024, 2:14 PM CDT  
**Added on** May 2, 2024, 3:58 PM CDT  
**Added by** Ken Gleason

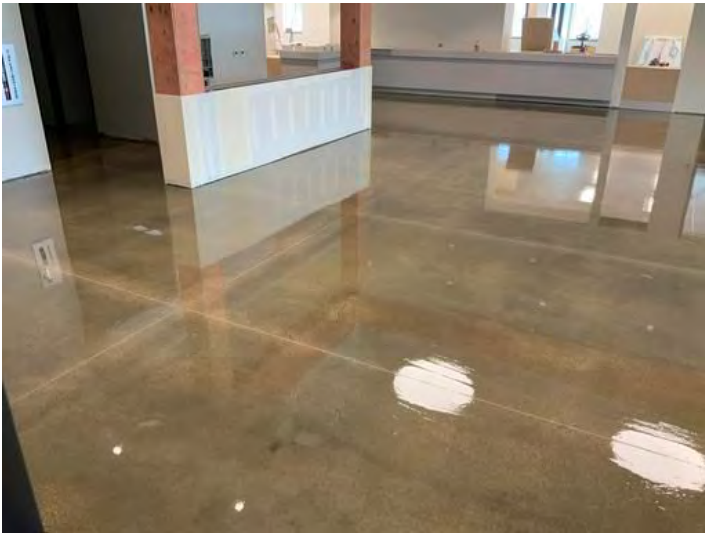

IMG\_1804

**Taken on** May 2, 2024, 2:12 PM CDT  
**Added on** May 2, 2024, 3:58 PM CDT  
**Added by** Ken Gleason



IMG\_1811

**Taken on** May 2, 2024, 2:15 PM CDT  
**Added on** May 2, 2024, 3:58 PM CDT  
**Added by** Ken Gleason



IMG\_1805

**Taken on** May 2, 2024, 2:12 PM CDT  
**Added on** May 2, 2024, 3:58 PM CDT  
**Added by** Ken Gleason



IMG\_1812

**Taken on** May 2, 2024, 2:16 PM CDT  
**Added on** May 2, 2024, 3:58 PM CDT  
**Added by** Ken Gleason



IMG\_1813

**Taken on** May 2, 2024, 2:31 PM CDT  
**Added on** May 2, 2024, 3:58 PM CDT  
**Added by** Ken Gleason

## Form detail

## #177: Weekly Report

**Forms**

---

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 3, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 3, 2024, 5:00 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos

---

**Supporting information**

Kendall County New Office Project. CCCS Project Number 221071.

---



## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	3	24	-	crew worked on casework at clerk and recorder departments, ceiling tile install, solid surface window sill install, door install at basement.
-	BP #8 Painting - Nedrow Painting	-	1	8	-	worked on painting of basement door jambs and doors today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	4	32	-	crews worked on lobby area flooring of the terrazzo and the toilets 1 and 2 for tile on the first floor today
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on light fixture install and MEP trim work at first floor along with wire mold install in basement.
<b>Totals:</b>			<b>11</b>	<b>88</b>	<b>0</b>	

## References

### Photos (11)



IMG\_1818

**Taken on** May 3, 2024, 11:45 AM CDT

**Added on** May 3, 2024, 5:00 PM CDT

**Added by** Ken Gleason



IMG\_1822

**Taken on** May 3, 2024, 12:07 PM CDT

**Added on** May 3, 2024, 5:00 PM CDT

**Added by** Ken Gleason



IMG\_1815

**Taken on** May 3, 2024, 11:14 AM CDT

**Added on** May 3, 2024, 5:00 PM CDT

**Added by** Ken Gleason



IMG\_1823

**Taken on** May 3, 2024, 12:07 PM CDT

**Added on** May 3, 2024, 5:00 PM CDT

**Added by** Ken Gleason




IMG\_1816  
**Taken on** May 3, 2024, 11:17 AM CDT  
**Added on** May 3, 2024, 5:00 PM CDT  
**Added by** Ken Gleason



IMG\_1820  
**Taken on** May 3, 2024, 11:45 AM CDT  
**Added on** May 3, 2024, 5:00 PM CDT  
**Added by** Ken Gleason



IMG\_1821  
**Taken on** May 3, 2024, 11:46 AM CDT  
**Added on** May 3, 2024, 5:00 PM CDT  
**Added by** Ken Gleason

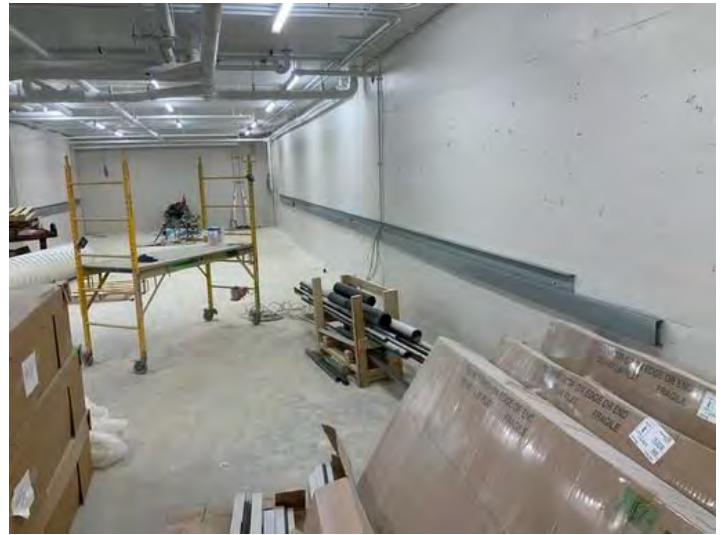

IMG\_1824  
**Taken on** May 3, 2024, 12:07 PM CDT  
**Added on** May 3, 2024, 5:00 PM CDT  
**Added by** Ken Gleason





IMG\_1817

**Taken on** May 3, 2024, 11:17 AM CDT

**Added on** May 3, 2024, 5:00 PM CDT

**Added by** Ken Gleason



IMG\_1814

**Taken on** May 3, 2024, 11:14 AM CDT

**Added on** May 3, 2024, 5:00 PM CDT

**Added by** Ken Gleason



IMG\_1819

**Taken on** May 3, 2024, 11:45 AM CDT

**Added on** May 3, 2024, 5:00 PM CDT

**Added by** Ken Gleason

## Form detail

## #178: Daily Report



## Forms

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 6, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 6, 2024, 2:52 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos

## Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

## Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Cloudy



Temperature: 50°F

Wind: ← 3mph

Humidity: 80%

12:00 PM

Mostly Clear



Temperature: 69°F

Wind: ← 6mph

Humidity: 58%

4:00 PM

Mostly Clear



Temperature: 76°F

Wind: ← 9mph

Humidity: 51%

Updated May 6, 2024 at 9:50 PM

## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	3	24	-	crew worked on knee walls in voter operation room, exterior Kendall county signage, clerk and recorder sub counters today
-	BP #8 Painting - Nedrow Painting	-	1	8	-	worked on painting handrails in stairway, doors in basement today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	4	32	-	crew worked on terrazzo flooring at lobby and tile flooring in bathrooms on first floor today
-	BP #10 Fire Protection - CL Doucette Inc	-	1	8	-	worked on final adjustments and install of sprinkler heads along with line fill today
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on generator install today along with wiring in basement for electrical outlets
<b>Totals:</b>			<b>12</b>	<b>96</b>	<b>0</b>	



## References

### Photos (12)



IMG\_1829

**Taken on** May 6, 2024, 10:08 AM CDT

**Added on** May 6, 2024, 2:52 PM CDT

**Added by** Ken Gleason



IMG\_1825

**Taken on** May 6, 2024, 10:05 AM CDT

**Added on** May 6, 2024, 2:52 PM CDT

**Added by** Ken Gleason




IMG\_1834

**Taken on** May 6, 2024, 2:41 PM CDT

**Added on** May 6, 2024, 2:52 PM CDT

**Added by** Ken Gleason

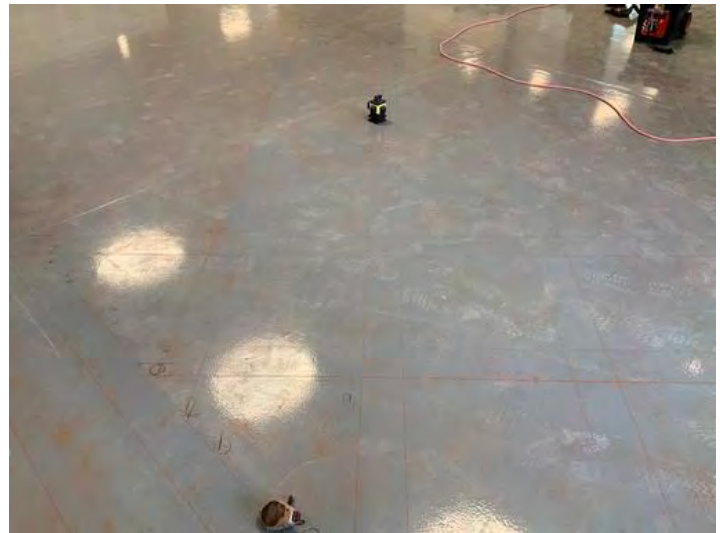

IMG\_1828

**Taken on** May 6, 2024, 10:07 AM CDT

**Added on** May 6, 2024, 2:52 PM CDT

**Added by** Ken Gleason



IMG\_1832

**Taken on** May 6, 2024, 2:40 PM CDT  
**Added on** May 6, 2024, 2:52 PM CDT  
**Added by** Ken Gleason




IMG\_1827

**Taken on** May 6, 2024, 10:07 AM CDT  
**Added on** May 6, 2024, 2:52 PM CDT  
**Added by** Ken Gleason



IMG\_1826

**Taken on** May 6, 2024, 10:05 AM CDT  
**Added on** May 6, 2024, 2:52 PM CDT  
**Added by** Ken Gleason

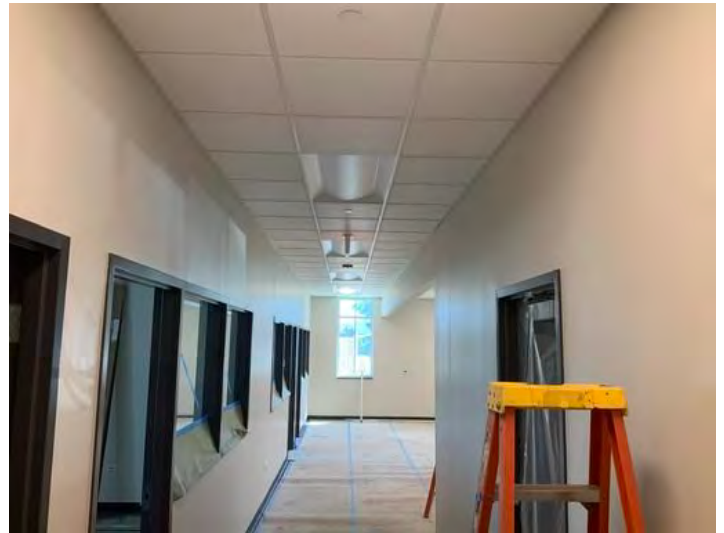

IMG\_1836

**Taken on** May 6, 2024, 2:42 PM CDT  
**Added on** May 6, 2024, 2:52 PM CDT  
**Added by** Ken Gleason





IMG\_1833

**Taken on** May 6, 2024, 2:40 PM CDT  
**Added on** May 6, 2024, 2:52 PM CDT  
**Added by** Ken Gleason



IMG\_1835

**Taken on** May 6, 2024, 2:42 PM CDT  
**Added on** May 6, 2024, 2:52 PM CDT  
**Added by** Ken Gleason



IMG\_1837

**Taken on** May 6, 2024, 2:42 PM CDT  
**Added on** May 6, 2024, 2:52 PM CDT  
**Added by** Ken Gleason



IMG\_1838

**Taken on** May 6, 2024, 2:42 PM CDT  
**Added on** May 6, 2024, 2:52 PM CDT  
**Added by** Ken Gleason



## Form detail

## #179: Daily Report



## Forms

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 7, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 7, 2024, 7:27 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos

## Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

## Weather

🌧️ Rain: 0.51 inches

🍏 Weather [View Sources](#)

7:00 AM

**Thunderstorms**



Temperature: 60°F

Wind: ↻ 10mph

Humidity: 83%

12:00 PM

**Partly Cloudy**



Temperature: 72°F

Wind: ↑ 9mph

Humidity: 79%

4:00 PM

**Mostly Clear**



Temperature: 74°F

Wind: ↗ 12mph

Humidity: 71%

Updated May 8, 2024 at 12:19 AM

## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	2	16	-	crew worked on solid surface tops in office at north interior and finishing solid surface tops throughout. prepping casework in clerk and recorder areas
-	BP #9 Flooring - TSI Commercial Floor Covering	-	8	64	-	crew worked on setting tracks for the terrazzo flooring in the lobby as well as worked on the tile install in the bathrooms on the first floor
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on generator as well as the install of the electrical trimming in the basement today
<b>Totals:</b>			<b>13</b>	<b>104</b>	<b>0</b>	

## References

### Photos (5)



IMG\_1839

**Taken on** May 7, 2024, 9:01 AM CDT

**Added on** May 7, 2024, 7:25 PM CDT

**Added by** Ken Gleason




IMG\_1843

**Taken on** May 7, 2024, 2:08 PM CDT

**Added on** May 7, 2024, 7:25 PM CDT

**Added by** Ken Gleason

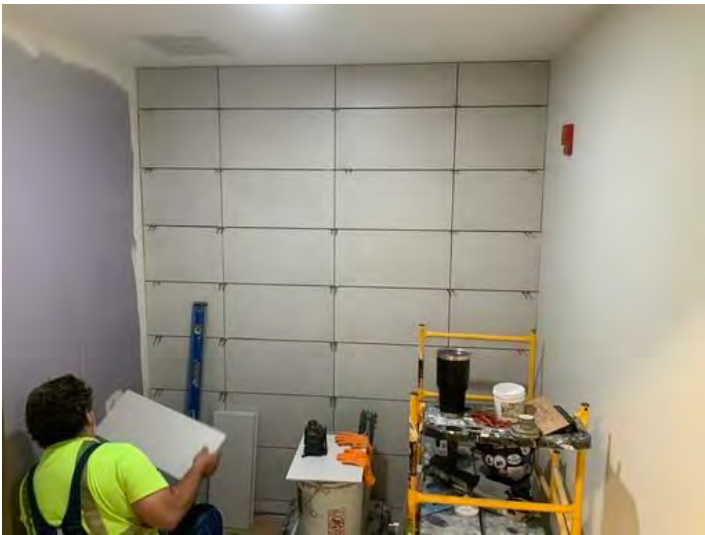

IMG\_1840

**Taken on** May 7, 2024, 9:03 AM CDT

**Added on** May 7, 2024, 7:25 PM CDT

**Added by** Ken Gleason



IMG\_1842

**Taken on** May 7, 2024, 2:08 PM CDT

**Added on** May 7, 2024, 7:25 PM CDT

**Added by** Ken Gleason





IMG\_1841

**Taken on** May 7, 2024, 2:08 PM CDT

**Added on** May 7, 2024, 7:25 PM CDT

**Added by** Ken Gleason

## Form detail

## #180: Daily Report



## Forms

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 8, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 8, 2024, 7:09 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos


## Supporting information


Kendall County New Office Project. CCCS Project Number 221071.


## Weather

🌧️ Rain: 0.04 inches

🍏 Weather [View Sources](#)

**7:00 AM**    **Mostly Clear**  
 Temperature: 54°F  
 Wind: ↻ 2mph  
 Humidity: 83%

**12:00 PM**    **Clear**  
 Temperature: 76°F  
 Wind: ↻ 4mph  
 Humidity: 45%

**4:00 PM**    **Partly Cloudy**  
 Temperature: 80°F  
 Wind: ↻ 6mph  
 Humidity: 37%

Updated May 9, 2024 at 12:05 AM

## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	2	16	-	crew worked on hanging trim pieces/tack and white boards along with ceiling tiles today
-	BP #6 Masonry - Jimmy'z Masonry	-	3	24	-	crew worked on filling expansion joints at exterior brick/stone
-	BP #7 Roofing - Filotto Roofing	-	2	16	-	crew worked on flat roof sections today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	6	48	-	crew worked on terrazzo flooring at lobby as well as bathroom tile work on first floor today
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on electrical power in basement today
<b>Totals:</b>			<b>16</b>	<b>128</b>	<b>0</b>	



## References

### Photos (5)



IMG\_1848

**Taken on** May 8, 2024, 12:54 PM CDT

**Added on** May 8, 2024, 7:09 PM CDT

**Added by** Ken Gleason



IMG\_1845

**Taken on** May 8, 2024, 12:52 PM CDT

**Added on** May 8, 2024, 7:09 PM CDT

**Added by** Ken Gleason




IMG\_1844

**Taken on** May 8, 2024, 12:52 PM CDT

**Added on** May 8, 2024, 7:09 PM CDT

**Added by** Ken Gleason

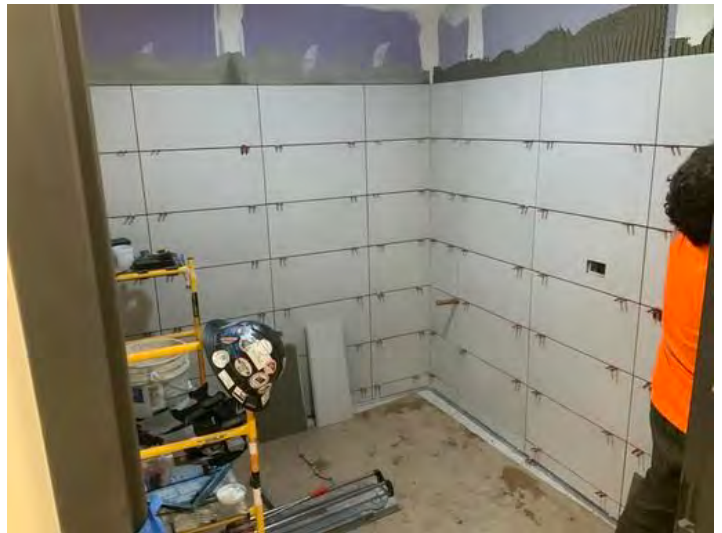

IMG\_1846

**Taken on** May 8, 2024, 12:52 PM CDT

**Added on** May 8, 2024, 7:09 PM CDT

**Added by** Ken Gleason



IMG\_1847

**Taken on** May 8, 2024, 12:53 PM CDT

**Added on** May 8, 2024, 7:09 PM CDT

**Added by** Ken Gleason

## Form detail

## #181: Daily Report



## Forms

Location	Kendall County New Office Building
Form date	May 9, 2024
Description	
Due date	
Submitted by	Ken Gleason
Status	Closed
Last update	May 9, 2024, 3:11 PM CDT
Last updated by	Ken Gleason
Included references	Assets   Files   Forms   Issues   Photos

## Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

## Weather

🌧️ Rain: 0.55 inches

🍏 Weather [View Sources](#)

7:00 AM

Cloudy



Temperature: 55°F

Wind: ↙ 8mph

Humidity: 90%

12:00 PM

Cloudy



Temperature: 61°F

Wind: ↙ 13mph

Humidity: 76%

4:00 PM

Drizzle



Temperature: 57°F

Wind: ↓ 14mph

Humidity: 79%

Updated May 9, 2024 at 8:01 PM



## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	1	8	-	worked on filling voids in basement between tops of CMU walls and precast flooring today
-	BP #6 Masonry - Jimmy'z Masonry	-	1	8	-	worked on filling joint lines where CMU walls meet concrete foundation in basement today. rained out of exterior stone work today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	6	48	-	crew worked on terrazzo flooring in lobby area as well as tile work in bathrooms on first floor
-	BP #13 Electrical - CSN Electric	-	2	16	-	crew worked on electrical outlets and switches in basement today
<b>Totals:</b>			<b>10</b>	<b>80</b>	<b>0</b>	

## References

### Photos (16)



IMG\_1856

**Taken on** May 9, 2024, 2:38 PM CDT  
**Added on** May 9, 2024, 3:10 PM CDT  
**Added by** Ken Gleason



IMG\_1854

**Taken on** May 9, 2024, 2:37 PM CDT  
**Added on** May 9, 2024, 3:10 PM CDT  
**Added by** Ken Gleason



IMG\_1857

**Taken on** May 9, 2024, 2:38 PM CDT  
**Added on** May 9, 2024, 3:10 PM CDT  
**Added by** Ken Gleason



IMG\_1859

**Taken on** May 9, 2024, 2:39 PM CDT  
**Added on** May 9, 2024, 3:10 PM CDT  
**Added by** Ken Gleason



IMG\_1855

**Taken on** May 9, 2024, 2:37 PM CDT  
**Added on** May 9, 2024, 3:11 PM CDT  
**Added by** Ken Gleason



IMG\_1858

**Taken on** May 9, 2024, 2:38 PM CDT  
**Added on** May 9, 2024, 3:11 PM CDT  
**Added by** Ken Gleason



IMG\_1860


**Taken on** May 9, 2024, 2:40 PM CDT  
**Added on** May 9, 2024, 3:11 PM CDT  
**Added by** Ken Gleason



IMG\_1862


**Taken on** May 9, 2024, 2:41 PM CDT  
**Added on** May 9, 2024, 3:11 PM CDT  
**Added by** Ken Gleason



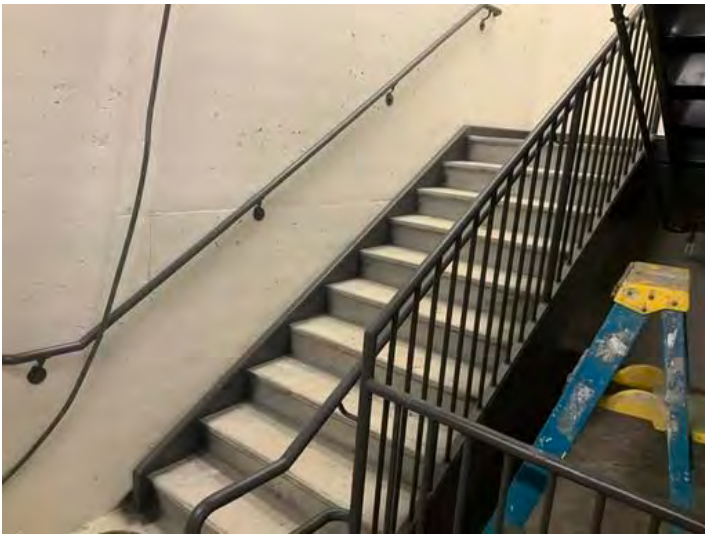

IMG\_1864

**Taken on** May 9, 2024, 2:51 PM CDT  
**Added on** May 9, 2024, 3:11 PM CDT  
**Added by** Ken Gleason

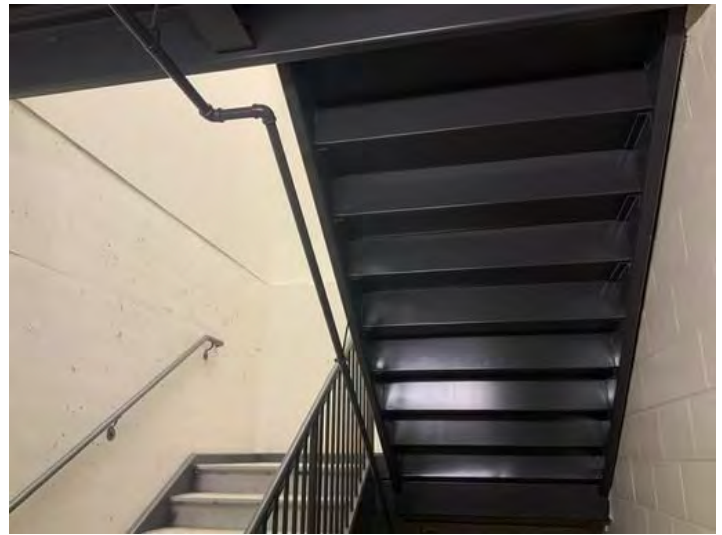

IMG\_1865

**Taken on** May 9, 2024, 2:51 PM CDT  
**Added on** May 9, 2024, 3:11 PM CDT  
**Added by** Ken Gleason



IMG\_1861

**Taken on** May 9, 2024, 2:40 PM CDT  
**Added on** May 9, 2024, 3:11 PM CDT  
**Added by** Ken Gleason




IMG\_1863

**Taken on** May 9, 2024, 2:41 PM CDT  
**Added on** May 9, 2024, 3:11 PM CDT  
**Added by** Ken Gleason



IMG\_1867

**Taken on** May 9, 2024, 2:52 PM CDT  
**Added on** May 9, 2024, 3:11 PM CDT  
**Added by** Ken Gleason

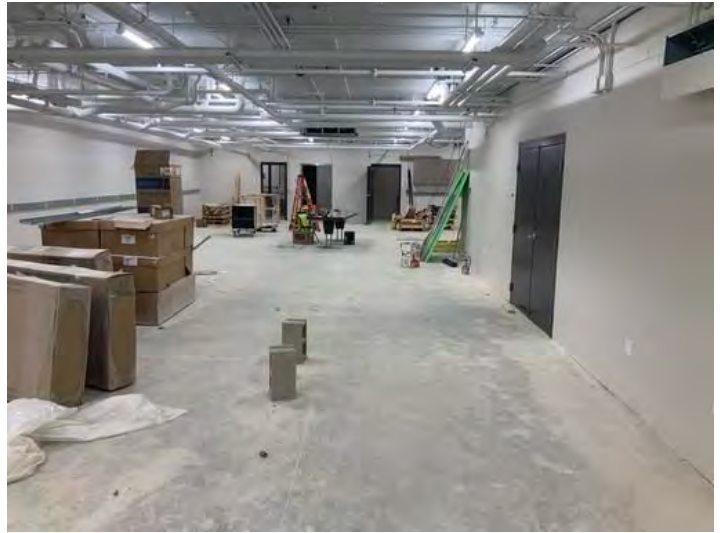

IMG\_1868

**Taken on** May 9, 2024, 2:52 PM CDT  
**Added on** May 9, 2024, 3:11 PM CDT  
**Added by** Ken Gleason



IMG\_1866

**Taken on** May 9, 2024, 2:51 PM CDT  
**Added on** May 9, 2024, 3:11 PM CDT  
**Added by** Ken Gleason



IMG\_1869

**Taken on** May 9, 2024, 2:53 PM CDT  
**Added on** May 9, 2024, 3:11 PM CDT  
**Added by** Ken Gleason

## Form detail

## #182: Weekly Report

**Forms**

**Location** Kendall County New Office Building

**Form date** May 10, 2024

**Description**

**Due date**

**Submitted by** Ken Gleason

**Status** Closed

**Last update** May 10, 2024, 1:32 PM CDT

**Last updated by** Ken Gleason

**Included references** Assets | Files | Forms | Issues | Photos

**Supporting information**

Kendall County New Office Project. CCCS Project Number 221071.



## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	1	8	-	worked on trim/crown moldings in vestibule area today
-	BP #6 Masonry - Jimmy'z Masonry	-	3	24	-	crew worked on expansion joint filling today at exterior as well as CMU corner joints at foundation walls.
-	BP #7 Roofing - Filotto Roofing	-	2	4	-	crew worked on flat roof at front entry above vestibule today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	6	48	-	crew worked on setting tracks for the terrazzo flooring in lobby as well as tile flooring and walls in bathrooms on first floor
-	BP #13 Electrical - CSN Electric	-	2	16	-	crew worked on electrical wiring and trim in basement today
<b>Totals:</b>			<b>14</b>	<b>100</b>	<b>0</b>	

## References


### Photos (8)




First Floor Bath Wall Tile  
**Taken on** May 10, 2024, 1:04 PM CDT  
**Added on** May 10, 2024, 1:17 PM CDT  
**Added by** Ken Gleason



Expansion Joint Filling  
**Taken on** May 10, 2024, 12:58 PM CDT  
**Added on** May 10, 2024, 1:17 PM CDT  
**Added by** Ken Gleason

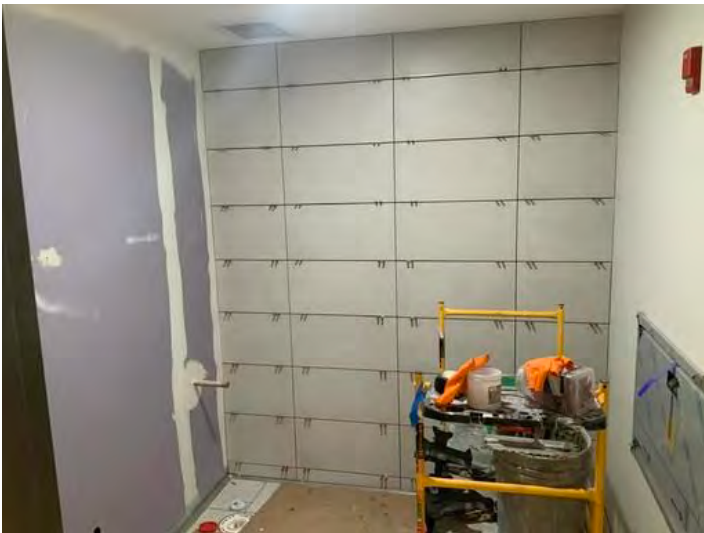

First Floor Bath Wall Tile  
**Taken on** May 10, 2024, 1:05 PM CDT  
**Added on** May 10, 2024, 1:17 PM CDT  
**Added by** Ken Gleason

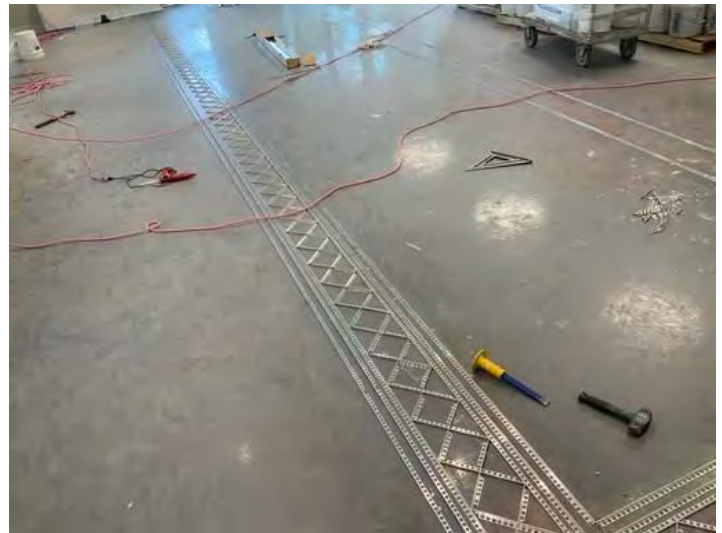

Lobby Terrazzo Tracks  
**Taken on** May 10, 2024, 1:03 PM CDT  
**Added on** May 10, 2024, 1:17 PM CDT  
**Added by** Ken Gleason



**Basement Bathroom Grab Bars**  
**Taken on** May 9, 2024, 2:53 PM CDT  
**Added on** May 10, 2024, 1:17 PM CDT  
**Added by** Ken Gleason



**Lobby Terrazzo Tracks**  
**Taken on** May 10, 2024, 1:03 PM CDT  
**Added on** May 10, 2024, 1:17 PM CDT  
**Added by** Ken Gleason



**Front Entry Flat Roof**  
**Taken on** May 10, 2024, 12:58 PM CDT  
**Added on** May 10, 2024, 1:17 PM CDT  
**Added by** Ken Gleason



**Lobby Terrazzo Tracks**  
**Taken on** May 10, 2024, 1:03 PM CDT  
**Added on** May 10, 2024, 1:18 PM CDT  
**Added by** Ken Gleason



## Form detail

## #183: Daily Report



## Forms

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 13, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 13, 2024, 3:41 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos

## Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

## Weather

🌧️ Rain: 0.35 inches

🍏 Weather [View Sources](#)

7:00 AM

Partly Cloudy



Temperature: 60°F

Wind: ↗ 3mph

Humidity: 73%

12:00 PM

Mostly Cloudy



Temperature: 79°F

Wind: ↗ 5mph

Humidity: 52%

4:00 PM

Cloudy



Temperature: 73°F

Wind: ↗ 10mph

Humidity: 61%

Updated May 13, 2024 at 9:35 PM

## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	1	8	-	worked on filling gaps in basement with rock wool and site clean up today
-	BP #6 Masonry - Jimmy'z Masonry	-	2	16	-	crew worked on filling the expansion joints around exterior of building today
-	BP #7 Roofing - Filotto Roofing	-	2	16	-	crew worked on flat roof sections with soffit and fascia today.
-	BP #11 Plumbing - Omega Plumbing	-	2	16	-	crew worked on setting toilets in first floor bathrooms that tile has been completed. also worked on slop sink install at janitors closet on first floor
-	BP #13 Electrical - CSN Electric	-	2	16	-	crew worked on electrical trim work on first floor today
<b>Totals:</b>			<b>9</b>	<b>72</b>	<b>0</b>	

## References

### Photos (9)



IMG\_1882

**Taken on** May 13, 2024, 10:16 AM CDT

**Added on** May 13, 2024, 3:40 PM CDT

**Added by** Ken Gleason




IMG\_1887

**Taken on** May 13, 2024, 10:18 AM CDT

**Added on** May 13, 2024, 3:40 PM CDT

**Added by** Ken Gleason

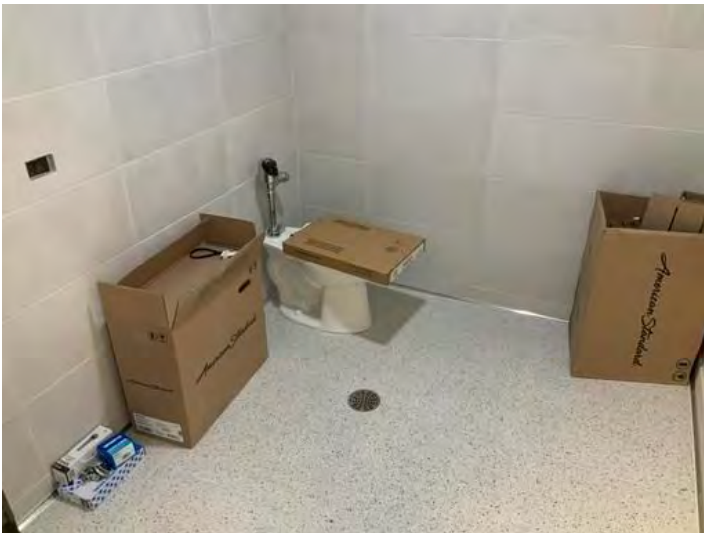

IMG\_1884

**Taken on** May 13, 2024, 10:17 AM CDT

**Added on** May 13, 2024, 3:40 PM CDT

**Added by** Ken Gleason




IMG\_1879

**Taken on** May 10, 2024, 1:04 PM CDT

**Added on** May 13, 2024, 3:40 PM CDT

**Added by** Ken Gleason



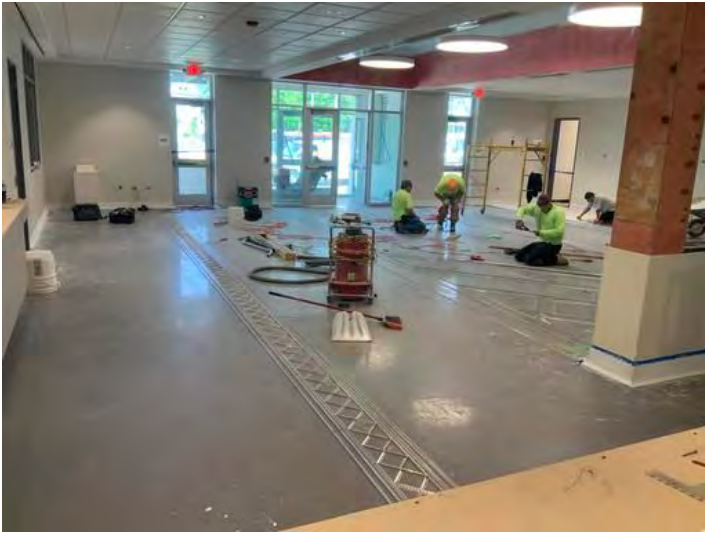

IMG\_1886

**Taken on** May 13, 2024, 10:17 AM CDT

**Added on** May 13, 2024, 3:41 PM CDT

**Added by** Ken Gleason



IMG\_1880

**Taken on** May 10, 2024, 1:05 PM CDT

**Added on** May 13, 2024, 3:41 PM CDT

**Added by** Ken Gleason




IMG\_1885

**Taken on** May 13, 2024, 10:17 AM CDT

**Added on** May 13, 2024, 3:41 PM CDT

**Added by** Ken Gleason

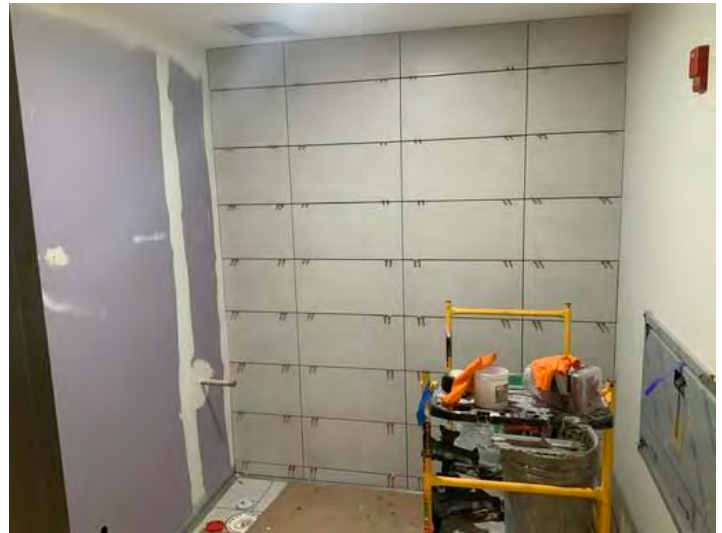

IMG\_1881

**Taken on** May 10, 2024, 1:05 PM CDT

**Added on** May 13, 2024, 3:41 PM CDT

**Added by** Ken Gleason



IMG\_1883

**Taken on** May 13, 2024, 10:16 AM CDT

**Added on** May 13, 2024, 3:41 PM CDT

**Added by** Ken Gleason

## Form detail

## #184: Daily Report



## Forms

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 14, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 14, 2024, 5:05 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos

## Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

## Weather

🌧️ Rain: 0.12 inches

🍏 Weather [View Sources](#)

7:00 AM

**Thunderstorms**



Temperature: 56°F

Wind: ← 6mph

Humidity: 95%

12:00 PM

**Cloudy**



Temperature: 64°F

Wind: ↙ 8mph

Humidity: 80%

4:00 PM

**Mostly Cloudy**



Temperature: 67°F

Wind: ↙ 10mph

Humidity: 71%

Updated May 15, 2024 at 1:19 PM



## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	1	8	-	worked on counter in lactation room, started crown molding in vestibule today
-	BP #6 Masonry - Jimmy'z Masonry	-	2	16	-	crew worked on filling expansion joints at exterior today
-	BP #7 Roofing - Filotto Roofing	-	2	16	-	crew worked on soffits at north side of building today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	6	48	-	crew worked on tile install at bathrooms on first floor today as well as continued with terrazzo flooring install at lobby area
-	BP #11 Plumbing - Omega Plumbing	-	2	16	-	crew worked on install of sinks and toilets in bathrooms on first floor today
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on install of electrical trim at first floor knee walls in voter operations today as well as trim in basement.
-	BP #15 Elevator - Otis Elevator Company	-	2	16	-	crew worked on elevator install today.
<b>Totals:</b>			<b>18</b>	<b>144</b>	<b>0</b>	

## References

### Photos (12)



IMG\_1892

**Taken on** May 14, 2024, 8:06 AM CDT  
**Added on** May 14, 2024, 5:05 PM CDT  
**Added by** Ken Gleason



IMG\_1890

**Taken on** May 14, 2024, 8:06 AM CDT  
**Added on** May 14, 2024, 5:05 PM CDT  
**Added by** Ken Gleason



IMG\_1891

**Taken on** May 14, 2024, 8:06 AM CDT  
**Added on** May 14, 2024, 5:05 PM CDT  
**Added by** Ken Gleason




IMG\_1895

**Taken on** May 14, 2024, 8:09 AM CDT  
**Added on** May 14, 2024, 5:05 PM CDT  
**Added by** Ken Gleason



IMG\_1889

**Taken on** May 14, 2024, 8:06 AM CDT  
**Added on** May 14, 2024, 5:05 PM CDT  
**Added by** Ken Gleason

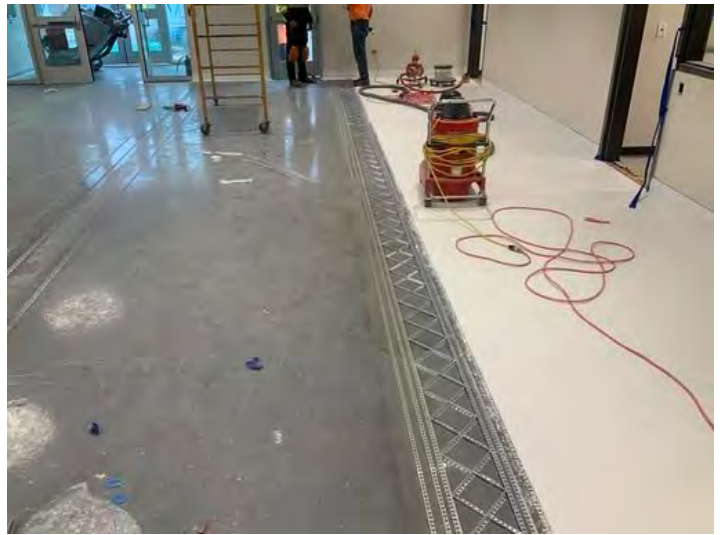

IMG\_1888

**Taken on** May 14, 2024, 8:06 AM CDT  
**Added on** May 14, 2024, 5:05 PM CDT  
**Added by** Ken Gleason



IMG\_1897

**Taken on** May 14, 2024, 11:58 AM CDT  
**Added on** May 14, 2024, 5:05 PM CDT  
**Added by** Ken Gleason



IMG\_1894

**Taken on** May 14, 2024, 8:07 AM CDT  
**Added on** May 14, 2024, 5:05 PM CDT  
**Added by** Ken Gleason





IMG\_1893

**Taken on** May 14, 2024, 8:06 AM CDT  
**Added on** May 14, 2024, 5:05 PM CDT  
**Added by** Ken Gleason



IMG\_1898

**Taken on** May 14, 2024, 12:33 PM CDT  
**Added on** May 14, 2024, 5:05 PM CDT  
**Added by** Ken Gleason



IMG\_1896

**Taken on** May 14, 2024, 8:11 AM CDT  
**Added on** May 14, 2024, 5:05 PM CDT  
**Added by** Ken Gleason



IMG\_1899

**Taken on** May 14, 2024, 12:33 PM CDT  
**Added on** May 14, 2024, 5:05 PM CDT  
**Added by** Ken Gleason

## Form detail

## #185: Daily Report



## Forms

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 15, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 15, 2024, 5:21 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos


## Supporting information


Kendall County New Office Project. CCCS Project Number 221071.


## Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

**7:00 AM**    **Mostly Clear**  
 Temperature: 53°F  
 Wind: ↙ 7mph  
 Humidity: 79%

**12:00 PM**    **Clear**  
 Temperature: 69°F  
 Wind: ↙ 8mph  
 Humidity: 56%

**4:00 PM**    **Mostly Clear**  
 Temperature: 73°F  
 Wind: ↙ 6mph  
 Humidity: 43%

Updated May 16, 2024 at 7:39 PM

## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	2	16	-	crew worked on exterior dens glass install at front entry today
-	BP #3 Exc / Site Util - Plainfield Grading	-	2	16	-	crew worked on planters at west side of site as well as excavation and grading the other sides of site to prep for concrete sidewalks and drive pads
-	BP #7 Roofing - Filotto Roofing	-	2	16	-	crew worked on soffit at north side of site today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	5	40	-	crew worked on terrazzo flooring at lobby area as well as tile in bathrooms on first floor
-	BP #11 Plumbing - Omega Plumbing	-	2	16	-	crew worked on install of trim plumbing at first floor and basement today
-	BP #13 Electrical - CSN Electric	-	1	8	-	crew worked on prep work for electrical light poles at parking lot today
<b>Totals:</b>			<b>14</b>	<b>112</b>	<b>0</b>	



### References

#### Photos (8)



IMG\_1905  
**Taken on** May 15, 2024, 1:02 PM CDT  
**Added on** May 15, 2024, 5:20 PM CDT  
**Added by** Ken Gleason



IMG\_1901  
**Taken on** May 15, 2024, 12:59 PM CDT  
**Added on** May 15, 2024, 5:20 PM CDT  
**Added by** Ken Gleason



IMG\_1903  
**Taken on** May 15, 2024, 1:00 PM CDT  
**Added on** May 15, 2024, 5:20 PM CDT  
**Added by** Ken Gleason



IMG\_1900  
**Taken on** May 15, 2024, 12:59 PM CDT  
**Added on** May 15, 2024, 5:20 PM CDT  
**Added by** Ken Gleason





IMG\_1902

**Taken on** May 15, 2024, 12:59 PM CDT

**Added on** May 15, 2024, 5:20 PM CDT

**Added by** Ken Gleason



IMG\_1904

**Taken on** May 15, 2024, 1:00 PM CDT

**Added on** May 15, 2024, 5:20 PM CDT

**Added by** Ken Gleason




IMG\_1907

**Taken on** May 15, 2024, 1:03 PM CDT

**Added on** May 15, 2024, 5:20 PM CDT

**Added by** Ken Gleason

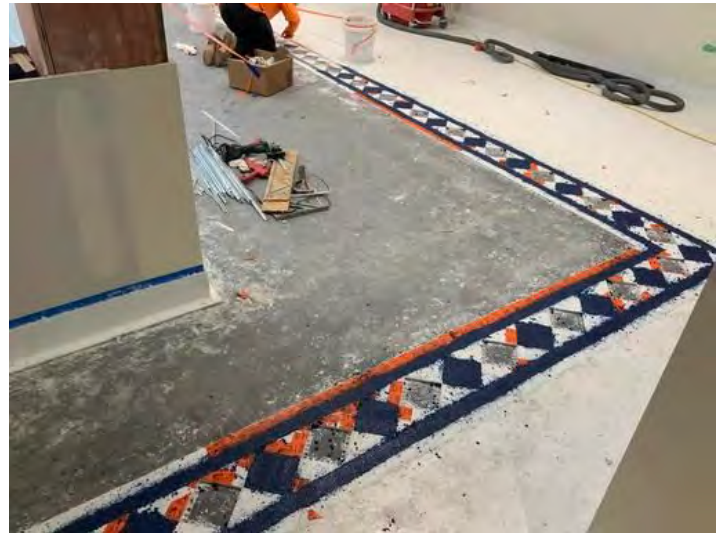

IMG\_1906

**Taken on** May 15, 2024, 1:02 PM CDT

**Added on** May 15, 2024, 5:21 PM CDT

**Added by** Ken Gleason

## Form detail

## #186: Daily Report



## Forms

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 16, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 16, 2024, 3:34 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos

## Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

## Weather

🌧️ Rain: 0.20 inches

🍏 Weather [View Sources](#)

7:00 AM

Partly Cloudy



Temperature: 53°F

Wind: ↻ 2mph

Humidity: 80%

12:00 PM

Cloudy



Temperature: 73°F

Wind: ↑ 9mph

Humidity: 69%

4:00 PM

Cloudy



Temperature: 71°F

Wind: ↗ 12mph

Humidity: 71%

Updated May 16, 2024 at 9:26 PM

## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	1	8	-	worked on grab bars and holders in bathrooms on first floor today
-	BP #3 Exc / Site Util - Plainfield Grading	-	2	16	-	crew worked on final grading throughout site today in preparation for concrete and flat work
-	BP #5 Asphalt, C&Gs, Site Concrete - Abbey Paving	-	6	48	-	crew worked on site prep for concrete flat work to start tomorrow as well as install of bollards around south east corner of building
-	BP #7 Roofing - Filotto Roofing	-	2	16	-	crew worked on soffit and fascia install at southern side of site today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	6	48	-	crew worked on terrazzo floor install as well as tile work in bathrooms on first floor today
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on underground exterior piping for light pole install around site today
<b>Totals:</b>			<b>20</b>	<b>160</b>	<b>0</b>	



## References

### Photos (11)



IMG\_1908

**Taken on** May 16, 2024, 11:34 AM CDT

**Added on** May 16, 2024, 3:34 PM CDT

**Added by** Ken Gleason



IMG\_1911

**Taken on** May 16, 2024, 12:00 PM CDT

**Added on** May 16, 2024, 3:34 PM CDT

**Added by** Ken Gleason



IMG\_1914

**Taken on** May 16, 2024, 12:03 PM CDT

**Added on** May 16, 2024, 3:34 PM CDT

**Added by** Ken Gleason



IMG\_1910

**Taken on** May 16, 2024, 11:34 AM CDT

**Added on** May 16, 2024, 3:34 PM CDT

**Added by** Ken Gleason





IMG\_1909

**Taken on** May 16, 2024, 11:34 AM CDT

**Added on** May 16, 2024, 3:34 PM CDT

**Added by** Ken Gleason



IMG\_1912

**Taken on** May 16, 2024, 12:01 PM CDT

**Added on** May 16, 2024, 3:34 PM CDT

**Added by** Ken Gleason



IMG\_1915

**Taken on** May 16, 2024, 12:03 PM CDT

**Added on** May 16, 2024, 3:34 PM CDT

**Added by** Ken Gleason



IMG\_1913

**Taken on** May 16, 2024, 12:02 PM CDT

**Added on** May 16, 2024, 3:34 PM CDT

**Added by** Ken Gleason





IMG\_1918

**Taken on** May 16, 2024, 12:51 PM CDT

**Added on** May 16, 2024, 3:34 PM CDT

**Added by** Ken Gleason



IMG\_1917

**Taken on** May 16, 2024, 12:05 PM CDT

**Added on** May 16, 2024, 3:34 PM CDT

**Added by** Ken Gleason



IMG\_1916

**Taken on** May 16, 2024, 12:04 PM CDT

**Added on** May 16, 2024, 3:34 PM CDT

**Added by** Ken Gleason

## Form detail

## #187: Weekly Report

**Forms**

---

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 17, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 17, 2024, 4:18 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	<a href="#">Assets</a>   <a href="#">Files</a>   <a href="#">Forms</a>   <a href="#">Issues</a>   <a href="#">Photos</a>

---

**Supporting information**

Kendall County New Office Project. CCCS Project Number 221071.

---



## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	1	8	-	worked on bathroom grab bars and hand rails in first floor bathrooms today
-	BP #3 Excav/Site Util - Plainfield Grading	-	2	16	-	crew worked on final grading of site in preparation of landscapers by adding black dirt in islands in parking lots and for flat work to be started next week.
-	BP #4 Building Concrete - Premium Concrete Inc	-	7	56	-	crew worked on forms and pouring concrete for planters at west side of site today
-	BP #5 Asphalt, C&G's, Site Concrete - Abbey Paving	-	7	56	-	crew worked on flat work sidewalks and drive pad at north, south and east side of site today
-	BP #7 Roofing - Filotto Roofing	-	2	16	-	crew worked on soffit and fascia at south side of building today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	6	48	-	crew worked on terrazzo flooring in lobby area as well as tile and grout work in bathrooms on first floor today
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on install of exterior parking lot light poles today
<b>Totals:</b>			<b>28</b>	<b>224</b>	<b>0</b>	

## References

### Photos (13)



IT Room

**Taken on** May 17, 2024, 3:57 PM CDT

**Added on** May 17, 2024, 4:08 PM CDT

**Added by** Ken Gleason



Lobby Terrazzo Flooring

**Taken on** May 17, 2024, 3:56 PM CDT

**Added on** May 17, 2024, 4:08 PM CDT

**Added by** Ken Gleason



Drive Ramp NE Corner

**Taken on** May 17, 2024, 3:59 PM CDT

**Added on** May 17, 2024, 4:08 PM CDT

**Added by** Ken Gleason



Drive Ramp NE Corner

**Taken on** May 17, 2024, 12:13 PM CDT

**Added on** May 17, 2024, 4:08 PM CDT

**Added by** Ken Gleason





Planter Boxes West Side

**Taken on** May 17, 2024, 12:07 PM CDT

**Added on** May 17, 2024, 4:08 PM CDT

**Added by** Ken Gleason



Drive Pad East Side

**Taken on** May 17, 2024, 12:05 PM CDT

**Added on** May 17, 2024, 4:08 PM CDT

**Added by** Ken Gleason



Drive Pad and Sidewalk Southeast Corner

**Taken on** May 17, 2024, 9:50 AM CDT

**Added on** May 17, 2024, 4:08 PM CDT

**Added by** Ken Gleason



IT Room

**Taken on** May 17, 2024, 3:58 PM CDT

**Added on** May 17, 2024, 4:08 PM CDT

**Added by** Ken Gleason





First Floor Bathrooms

**Taken on** May 17, 2024, 12:14 PM CDT

**Added on** May 17, 2024, 4:08 PM CDT

**Added by** Ken Gleason



Lobby Terrazzo Flooring

**Taken on** May 17, 2024, 12:15 PM CDT

**Added on** May 17, 2024, 4:08 PM CDT

**Added by** Ken Gleason



Drive Pad NE Corner

**Taken on** May 17, 2024, 3:59 PM CDT

**Added on** May 17, 2024, 4:08 PM CDT

**Added by** Ken Gleason



Drive Pad and Sidewalk SE Corner

**Taken on** May 17, 2024, 12:05 PM CDT

**Added on** May 17, 2024, 4:08 PM CDT

**Added by** Ken Gleason



Lobby Terrazzo Flooring

**Taken on** May 17, 2024, 12:15 PM CDT

**Added on** May 17, 2024, 4:09 PM CDT

**Added by** Ken Gleason

## Form detail

## #188: Daily Report



## Forms

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 20, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 20, 2024, 3:27 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos

## Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

## Weather

🌧️ Rain: 0.24 inches

🍏 Weather [View Sources](#)

7:00 AM

Partly Cloudy



Temperature: 65°F

Wind: ↻ 4mph

Humidity: 75%

12:00 PM

Cloudy



Temperature: 82°F

Wind: ↗ 14mph

Humidity: 61%

4:00 PM

Windy



Temperature: 81°F

Wind: ↗ 16mph

Humidity: 59%

Updated May 20, 2024 at 8:25 PM



## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	1	8	-	worked on hanging grab bars and mirrors in bathrooms on first floor today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	5	40	-	crew worked on terrazzo flooring in lobby area today
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on installing light poles at exterior parking lot and sidewalk areas today
-	BP #4 Building Concrete - Premium Concrete Inc	-	2	16	-	crew worked on rebar at west side planters today
<b>Totals:</b>			<b>11</b>	<b>88</b>	<b>0</b>	

## References

### Photos (8)



IMG\_1939

**Taken on** May 20, 2024, 2:49 PM CDT

**Added on** May 20, 2024, 3:27 PM CDT

**Added by** Ken Gleason



IMG\_1943

**Taken on** May 20, 2024, 2:54 PM CDT

**Added on** May 20, 2024, 3:27 PM CDT

**Added by** Ken Gleason



IMG\_1940

**Taken on** May 20, 2024, 2:49 PM CDT

**Added on** May 20, 2024, 3:27 PM CDT

**Added by** Ken Gleason



IMG\_1942

**Taken on** May 20, 2024, 2:54 PM CDT

**Added on** May 20, 2024, 3:27 PM CDT

**Added by** Ken Gleason




IMG\_1941

**Taken on** May 20, 2024, 2:54 PM CDT  
**Added on** May 20, 2024, 3:27 PM CDT  
**Added by** Ken Gleason



IMG\_1938

**Taken on** May 20, 2024, 2:49 PM CDT  
**Added on** May 20, 2024, 3:27 PM CDT  
**Added by** Ken Gleason

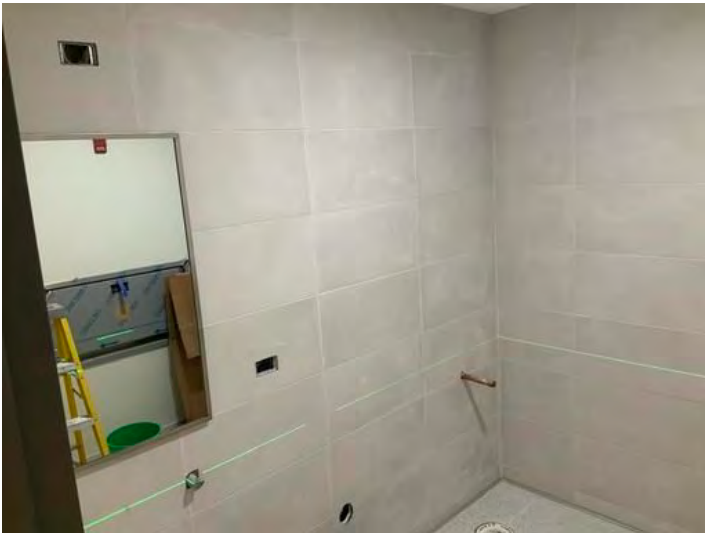

IMG\_1944

**Taken on** May 20, 2024, 2:55 PM CDT  
**Added on** May 20, 2024, 3:27 PM CDT  
**Added by** Ken Gleason



IMG\_1937

**Taken on** May 20, 2024, 2:48 PM CDT  
**Added on** May 20, 2024, 3:27 PM CDT  
**Added by** Ken Gleason



## Form detail

## #189: Daily Report



## Forms

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 22, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 22, 2024, 4:00 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos

## Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

## Weather

🌧️ Rain: 0.00 inches

🍏 Weather [View Sources](#)

7:00 AM

Partly Cloudy



Temperature: 60°F

Wind: → 12mph

Humidity: 76%

12:00 PM

Mostly Clear



Temperature: 70°F

Wind: → 13mph

Humidity: 56%

4:00 PM

Windy



Temperature: 75°F

Wind: → 17mph

Humidity: 38%

Updated May 22, 2024 at 8:49 PM

## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	3	24	-	crew worked on install of wall panels at voter operations as well as interior site clean up and prep for furniture today
-	BP #4 Building Concrete - Premium Concrete Inc	-	4	32	-	crew worked on rebar and forms for planters at west side of building today
-	BP #7 Roofing - Filotto Roofing	-	2	16	-	crew worked on soffit and fascia at east side of building today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	4	32	-	crew worked on terrazzo flooring install at lobby area today
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on forms for exterior lighting today
<b>Totals:</b>			<b>16</b>	<b>128</b>	<b>0</b>	

## References

### Photos (10)



IMG\_1945

**Taken on** May 22, 2024, 3:14 PM CDT

**Added on** May 22, 2024, 4:00 PM CDT

**Added by** Ken Gleason



IMG\_1947

**Taken on** May 22, 2024, 3:15 PM CDT

**Added on** May 22, 2024, 4:00 PM CDT

**Added by** Ken Gleason



IMG\_1949

**Taken on** May 22, 2024, 3:16 PM CDT

**Added on** May 22, 2024, 4:00 PM CDT

**Added by** Ken Gleason



IMG\_1946

**Taken on** May 22, 2024, 3:14 PM CDT

**Added on** May 22, 2024, 4:00 PM CDT

**Added by** Ken Gleason





IMG\_1952

**Taken on** May 22, 2024, 3:17 PM CDT  
**Added on** May 22, 2024, 4:00 PM CDT  
**Added by** Ken Gleason



IMG\_1951

**Taken on** May 22, 2024, 3:16 PM CDT  
**Added on** May 22, 2024, 4:00 PM CDT  
**Added by** Ken Gleason



IMG\_1954

**Taken on** May 22, 2024, 3:26 PM CDT  
**Added on** May 22, 2024, 4:00 PM CDT  
**Added by** Ken Gleason



IMG\_1948

**Taken on** May 22, 2024, 3:15 PM CDT  
**Added on** May 22, 2024, 4:00 PM CDT  
**Added by** Ken Gleason



IMG\_1953

**Taken on** May 22, 2024, 3:17 PM CDT  
**Added on** May 22, 2024, 4:00 PM CDT  
**Added by** Ken Gleason



IMG\_1950

**Taken on** May 22, 2024, 3:16 PM CDT  
**Added on** May 22, 2024, 4:00 PM CDT  
**Added by** Ken Gleason

## Form detail

## #190: Daily Report



## Forms

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 23, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 23, 2024, 3:24 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos

## Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

## Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Clear



Temperature: 57°F

Wind: ↗ 1mph

Humidity: 74%

12:00 PM

Clear



Temperature: 77°F

Wind: ↑ 4mph

Humidity: 38%

4:00 PM

Mostly Clear



Temperature: 82°F

Wind: ↑ 4mph

Humidity: 31%

Updated May 24, 2024 at 4:14 PM



## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	1	8	-	worked on exterior door install at east side of building basement entry
-	BP #4 Building Concrete - Premium Concrete Inc	-	4	32	-	crew worked on rebar and forms for planters at front west side of building today
-	BP #7 Roofing - Filotto Roofing	-	1	8	-	worked on soffit and fascia at south and east side of site today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	4	32	-	crew worked on terrazzo flooring at lobby area of first floor today
-	BP #13 Electrical - CSN Electric	-	2	16	-	crew worked on exterior site lighting at planters and repair work for the lift station at east mechanical pad
<b>Totals:</b>			<b>12</b>	<b>96</b>	<b>0</b>	

## References

### Photos (8)



IMG\_1957

**Taken on** May 23, 2024, 3:01 PM CDT

**Added on** May 23, 2024, 3:24 PM CDT

**Added by** Ken Gleason



IMG\_1961

**Taken on** May 23, 2024, 3:07 PM CDT

**Added on** May 23, 2024, 3:24 PM CDT

**Added by** Ken Gleason



IMG\_1960

**Taken on** May 23, 2024, 3:05 PM CDT

**Added on** May 23, 2024, 3:24 PM CDT

**Added by** Ken Gleason



IMG\_1955

**Taken on** May 23, 2024, 3:01 PM CDT

**Added on** May 23, 2024, 3:24 PM CDT

**Added by** Ken Gleason



IMG\_1962

**Taken on** May 23, 2024, 3:07 PM CDT

**Added on** May 23, 2024, 3:24 PM CDT

**Added by** Ken Gleason



IMG\_1958

**Taken on** May 23, 2024, 3:04 PM CDT

**Added on** May 23, 2024, 3:24 PM CDT

**Added by** Ken Gleason



IMG\_1956

**Taken on** May 23, 2024, 3:01 PM CDT

**Added on** May 23, 2024, 3:24 PM CDT

**Added by** Ken Gleason



IMG\_1959

**Taken on** May 23, 2024, 3:05 PM CDT

**Added on** May 23, 2024, 3:24 PM CDT

**Added by** Ken Gleason



## Form detail

## #191: Weekly Report

**Forms**

---

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 24, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 24, 2024, 2:42 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	<a href="#">Assets</a>   <a href="#">Files</a>   <a href="#">Forms</a>   <a href="#">Issues</a>   <a href="#">Photos</a>

---

**Supporting information**

Kendall County New Office Project. CCCS Project Number 221071.

---

## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	1	8	-	worked on exterior door install at basement of east side of building today
-	BP #4 Building Concrete - Premium Concrete Inc	-	4	32	-	crew worked on forms for concrete at planters at west side of building today
-	BP #7 Roofing - Filotto Roofing	-	2	16	-	crew worked on soffit and fascia at south side of building today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	4	32	-	crew worked on terrazzo flooring at lobby area of first floor today
-	BP #12 Mechanical - Jensen's Plumbing & Heating	-	1	8	-	worked on mechanical hookups at mechanical pad exterior at east side of building today
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on forms for concrete bases for exterior site lighting as well as swapping out the generator today at mechanical pad
<b>Totals:</b>			<b>15</b>	<b>120</b>	<b>0</b>	

## References

### Photos (12)



Exterior NE Corner

**Taken on** May 24, 2024, 9:26 AM CDT

**Added on** May 24, 2024, 1:29 PM CDT

**Added by** Ken Gleason



Clerk Office 3

**Taken on** May 24, 2024, 9:40 AM CDT

**Added on** May 24, 2024, 1:29 PM CDT

**Added by** Ken Gleason



Clerk Office 2

**Taken on** May 24, 2024, 9:40 AM CDT

**Added on** May 24, 2024, 1:29 PM CDT

**Added by** Ken Gleason




Exterior North

**Taken on** May 24, 2024, 9:25 AM CDT

**Added on** May 24, 2024, 1:29 PM CDT

**Added by** Ken Gleason



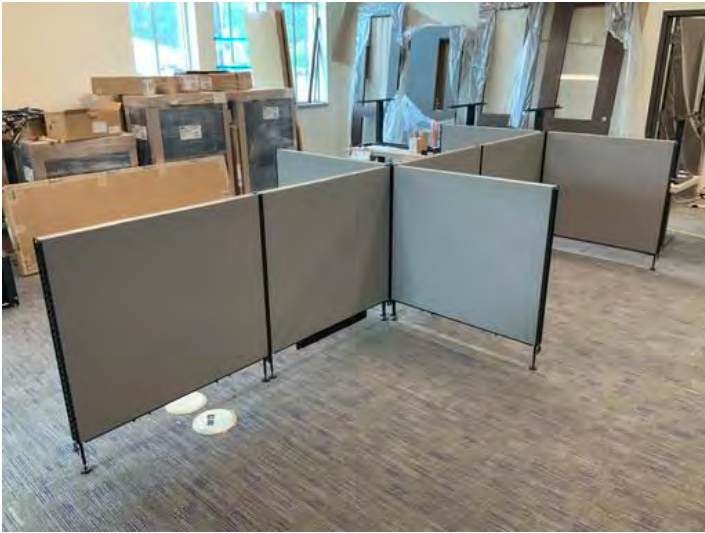

Clerk Dept

**Taken on** May 24, 2024, 9:40 AM CDT

**Added on** May 24, 2024, 1:29 PM CDT

**Added by** Ken Gleason



Lobby Terrazzo Flooring

**Taken on** May 24, 2024, 9:41 AM CDT

**Added on** May 24, 2024, 1:29 PM CDT

**Added by** Ken Gleason




Voter Registration/Training

**Taken on** May 24, 2024, 9:42 AM CDT

**Added on** May 24, 2024, 1:29 PM CDT

**Added by** Ken Gleason

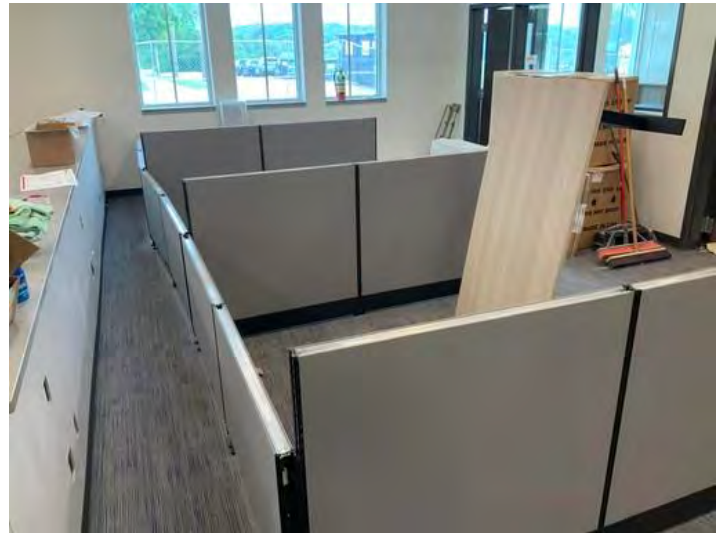

Voter Operations

**Taken on** May 24, 2024, 9:42 AM CDT

**Added on** May 24, 2024, 1:29 PM CDT

**Added by** Ken Gleason



Clerk Office 3

**Taken on** May 24, 2024, 9:42 AM CDT

**Added on** May 24, 2024, 1:29 PM CDT

**Added by** Ken Gleason



Voter Operations

**Taken on** May 24, 2024, 9:42 AM CDT

**Added on** May 24, 2024, 1:29 PM CDT

**Added by** Ken Gleason



Lobby Terrazzo Flooring

**Taken on** May 24, 2024, 9:40 AM CDT

**Added on** May 24, 2024, 1:29 PM CDT

**Added by** Ken Gleason



Exterior Lighting Base

**Taken on** May 24, 2024, 9:24 AM CDT

**Added on** May 24, 2024, 1:29 PM CDT

**Added by** Ken Gleason

## Form detail

## #192: Daily Report



## Forms

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 28, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 28, 2024, 4:37 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos

## Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

## Weather

🌧️ Rain: 0.16 inches

🍏 Weather [View Sources](#)

7:00 AM

Clear



Temperature: 55°F

Wind: → 4mph

Humidity: 90%

12:00 PM

Partly Cloudy



Temperature: 71°F

Wind: ↘ 8mph

Humidity: 59%

4:00 PM

Thunderstorms



Temperature: 67°F

Wind: ↘ 10mph

Humidity: 66%

Updated May 29, 2024 at 2:43 PM




## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	1	8	-	worked on doors at back entry of east side at basement
-	BP #4 Building Concrete - Premium Concrete Inc	-	4	32	-	crew worked on adjustments to forms per the ASI that was sent out as well as pouring of the concrete for the planters today
-	BP #7 Roofing - Filotto Roofing	-	2	16	-	crew worked on soffit and fascia around south side gable roof today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	4	32	-	crew worked on terrazzo flooring at lobby area today
-	BP #13 Electrical - CSN Electric	-	2	16	-	crew worked on exterior lighting today at planters and parking lots
<b>Totals:</b>			<b>13</b>	<b>104</b>	<b>0</b>	

## References

### Photos (8)

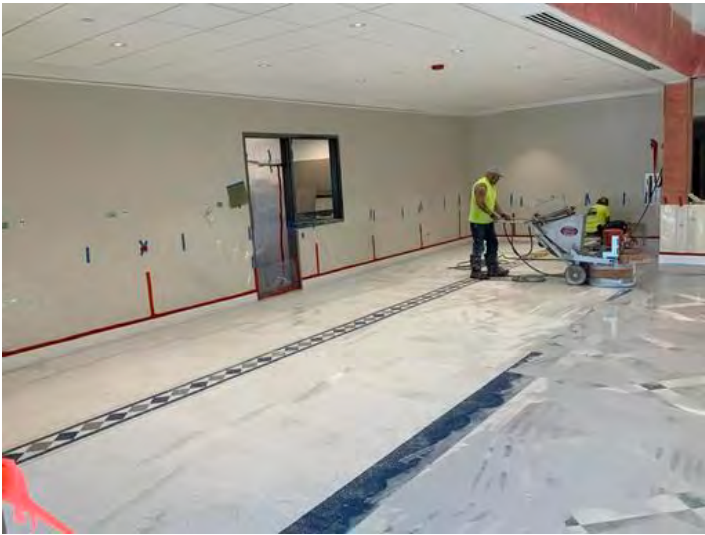

IMG\_1979

**Taken on** May 28, 2024, 11:31 AM CDT

**Added on** May 28, 2024, 4:37 PM CDT

**Added by** Ken Gleason



IMG\_1976

**Taken on** May 28, 2024, 11:27 AM CDT

**Added on** May 28, 2024, 4:37 PM CDT

**Added by** Ken Gleason



IMG\_1980

**Taken on** May 28, 2024, 11:54 AM CDT

**Added on** May 28, 2024, 4:37 PM CDT

**Added by** Ken Gleason



IMG\_1975

**Taken on** May 28, 2024, 11:27 AM CDT

**Added on** May 28, 2024, 4:37 PM CDT

**Added by** Ken Gleason



IMG\_1977

**Taken on** May 28, 2024, 11:31 AM CDT

**Added on** May 28, 2024, 4:37 PM CDT

**Added by** Ken Gleason



IMG\_1981

**Taken on** May 28, 2024, 11:54 AM CDT

**Added on** May 28, 2024, 4:37 PM CDT

**Added by** Ken Gleason



IMG\_1978

**Taken on** May 28, 2024, 11:31 AM CDT

**Added on** May 28, 2024, 4:37 PM CDT

**Added by** Ken Gleason



IMG\_1982

**Taken on** May 28, 2024, 11:56 AM CDT

**Added on** May 28, 2024, 4:37 PM CDT

**Added by** Ken Gleason



## Form detail

## #193: Daily Report



## Forms

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 29, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 29, 2024, 1:15 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos


## Supporting information


Kendall County New Office Project. CCCS Project Number 221071.


## Weather

🌧️ Rain: 0.00 inches

🍏 Weather [View Sources](#)

**7:00 AM**    **Mostly Clear**  
 Temperature: 54°F  
 Wind: ↘ 5mph  
 Humidity: 92%

**12:00 PM**    **Partly Cloudy**  
 Temperature: 67°F  
 Wind: ↓ 11mph  
 Humidity: 56%

**4:00 PM**    **Partly Cloudy**  
 Temperature: 70°F  
 Wind: ↙ 10mph  
 Humidity: 49%

Updated May 29, 2024 at 6:11 PM

## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	2	16	-	crew worked on prep work for crown molding trim work at lobby today
-	BP #4 Building Concrete - Premium Concrete Inc	-	3	24	-	crew worked on removal of forms where concrete planters were poured yesterday
-	BP #7 Roofing - Filotto Roofing	-	4	32	-	crew worked on soffit and fascia as well as gutters today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	4	32	-	crew worked on terrazzo flooring at lobby today
-	BP #13 Electrical - CSN Electric	-	2	16	-	crew worked on exterior site lighting today
<b>Totals:</b>			<b>15</b>	<b>120</b>	<b>0</b>	

## References

### Photos (3)



IMG\_1985

**Taken on** May 29, 2024, 9:12 AM CDT

**Added on** May 29, 2024, 1:15 PM CDT

**Added by** Ken Gleason



IMG\_1983

**Taken on** May 29, 2024, 8:58 AM CDT

**Added on** May 29, 2024, 1:15 PM CDT

**Added by** Ken Gleason



IMG\_1984

**Taken on** May 29, 2024, 8:58 AM CDT

**Added on** May 29, 2024, 1:15 PM CDT

**Added by** Ken Gleason



## Form detail

## #194: Daily Report



## Forms

Location	Kendall County New Office Building
Form date	May 30, 2024
Description	
Due date	
Submitted by	<b>Ken Gleason</b>
Status	Closed
Last update	May 30, 2024, 4:03 PM CDT
Last updated by	<b>Ken Gleason</b>
Included references	Assets   Files   Forms   Issues   Photos

## Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

## Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Clear



Temperature: 50°F

Wind: ↙ 4mph

Humidity: 71%

12:00 PM

Clear



Temperature: 69°F

Wind: ← 6mph

Humidity: 33%

4:00 PM

Clear



Temperature: 74°F

Wind: ← 6mph

Humidity: 28%

Updated May 30, 2024 at 8:54 PM

## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	1	8	-	worked on exterior Knox box install, interior ceiling panels in IT room, other minor touch ups
-	BP #3 Exc / Site Util - Plainfield Grading	-	2	16	-	crew worked on final site grading today
-	BP #7 Roofing - Filotto Roofing	-	2	16	-	crew worked on soffit and fascia at west side of building today
-	BP #9 Flooring - TSI Commercial Floor Covering	-	4	32	-	crew worked on finishing up with the terrazzo flooring at lobby area today
-	BP #13 Electrical - CSN Electric	-	2	16	-	crew worked on exterior site lighting today
<b>Totals:</b>			<b>11</b>	<b>88</b>	<b>0</b>	

## References

### Photos (8)



IMG\_1991

**Taken on** May 30, 2024, 2:49 PM CDT

**Added on** May 30, 2024, 4:02 PM CDT

**Added by** Ken Gleason



IMG\_1985

**Taken on** May 29, 2024, 9:12 AM CDT

**Added on** May 30, 2024, 4:02 PM CDT

**Added by** Ken Gleason



IMG\_1989

**Taken on** May 30, 2024, 2:48 PM CDT

**Added on** May 30, 2024, 4:02 PM CDT

**Added by** Ken Gleason



IMG\_1990

**Taken on** May 30, 2024, 2:48 PM CDT

**Added on** May 30, 2024, 4:03 PM CDT

**Added by** Ken Gleason





IMG\_1988

**Taken on** May 30, 2024, 10:53 AM CDT

**Added on** May 30, 2024, 4:03 PM CDT

**Added by** Ken Gleason



IMG\_1986

**Taken on** May 30, 2024, 9:33 AM CDT

**Added on** May 30, 2024, 4:03 PM CDT

**Added by** Ken Gleason



IMG\_1992

**Taken on** May 30, 2024, 2:49 PM CDT

**Added on** May 30, 2024, 4:03 PM CDT

**Added by** Ken Gleason



IMG\_1987

**Taken on** May 30, 2024, 10:53 AM CDT

**Added on** May 30, 2024, 4:03 PM CDT

**Added by** Ken Gleason

## Form detail

## #195: Weekly Report

**Forms**

---

<b>Location</b>	Kendall County New Office Building
<b>Form date</b>	May 31, 2024
<b>Description</b>	
<b>Due date</b>	
<b>Submitted by</b>	<b>Ken Gleason</b>
<b>Status</b>	Closed
<b>Last update</b>	May 31, 2024, 3:47 PM CDT
<b>Last updated by</b>	<b>Ken Gleason</b>
<b>Included references</b>	Assets   Files   Forms   Issues   Photos

---

**Supporting information**

Kendall County New Office Project. CCCS Project Number 221071.

---

## 1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	2	16	-	crew worked on casework and trim in lobby at first floor today along with install of countertops
-	BP #3 Excav/Site Util - Plainfield Grading	-	2	16	-	crew worked on site grading, install of drain tile at west side of building today, excavation at areas of frost walls at exterior front entry area
-	BP #9 Flooring - TSI Commercial Floor Covering	-	1	8	-	worked on install of tiles in bathrooms on first floor today
-	BP #13 Electrical - CSN Electric	-	2	16	-	crew worked on install of exterior site lighting poles today
-	BP #4 Building Concrete - Premium Concrete Inc	-	2	16	-	crew worked on waterproofing at planter boxes at west side of building today
<b>Totals:</b>			<b>9</b>	<b>72</b>	<b>0</b>	



### References

#### Photos (10)



Countertop install at lobby  
**Taken on** May 31, 2024, 3:17 PM CDT  
**Added on** May 31, 2024, 3:41 PM CDT  
**Added by** Ken Gleason



Counter top install at lobby  
**Taken on** May 31, 2024, 3:17 PM CDT  
**Added on** May 31, 2024, 3:41 PM CDT  
**Added by** Ken Gleason



Exterior site lighting  
**Taken on** May 31, 2024, 8:41 AM CDT  
**Added on** May 31, 2024, 3:41 PM CDT  
**Added by** Ken Gleason



Roof drain tile being installed  
**Taken on** May 31, 2024, 3:13 PM CDT  
**Added on** May 31, 2024, 3:41 PM CDT  
**Added by** Ken Gleason



Countertop install in lobby  
**Taken on** May 31, 2024, 3:17 PM CDT  
**Added on** May 31, 2024, 3:41 PM CDT  
**Added by** Ken Gleason



Rubbed finish install at ADA ramp  
**Taken on** May 31, 2024, 3:26 PM CDT  
**Added on** May 31, 2024, 3:41 PM CDT  
**Added by** Ken Gleason



Exterior site lighting  
**Taken on** May 31, 2024, 8:42 AM CDT  
**Added on** May 31, 2024, 3:41 PM CDT  
**Added by** Ken Gleason



Flatstock trim being installed at lobby  
**Taken on** May 31, 2024, 3:16 PM CDT  
**Added on** May 31, 2024, 3:41 PM CDT  
**Added by** Ken Gleason





Planter box with waterproofing work  
**Taken on** May 31, 2024, 8:25 AM CDT  
**Added on** May 31, 2024, 3:41 PM CDT  
**Added by** Ken Gleason



Planter box & excavation  
**Taken on** May 31, 2024, 8:25 AM CDT  
**Added on** May 31, 2024, 3:41 PM CDT  
**Added by** Ken Gleason



SECTION 5







# PHOTOGRAPHIC DOCUMENTATION

Date: 2024-05-07

Observation Time: 3:30 PM

Re: KENDALL COUNTY PHASE 1 CLERK BLDG  
Project: 221071

Weather Conditions: 65F  
Sunny




Paint Color at Concrete Jamb



Electrical Box at Door Frame 104A



Resinous Terrazzo Progress in Lobby

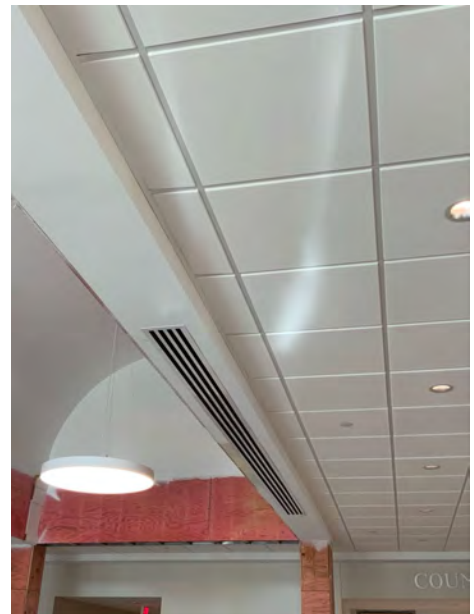

Perimeter Trim Piece Missing



# PHOTOGRAPHIC DOCUMENTATION

Date: 2024-05-07

Observation Time: 3:30 PM

Re: KENDALL COUNTY PHASE 1 CLERK BLDG

Weather Conditions: 65F

Project: 221071

Sunny



Interior Corner Gap at Reception



P.Lam Seams at Reception




Counter Misaligned in Voter



Light Poles near Overhead Power Lines




Wood Trim and Kendall County Sign at Gable

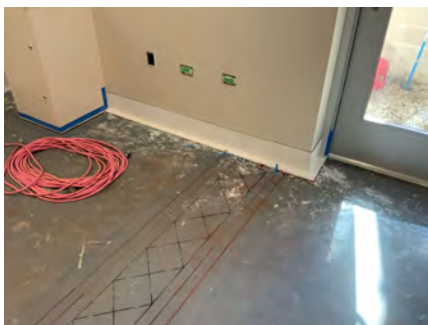

Cove Base Conflict with Desk



Ceramic Wall Tile in TLT

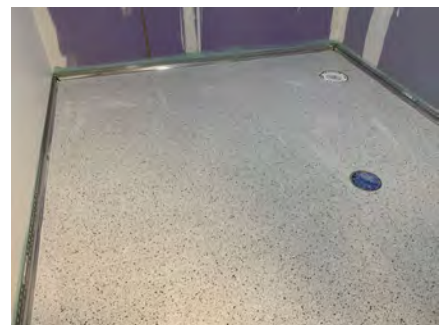

Ceramic Floor Tile in TLT





# PHOTOGRAPHIC DOCUMENTATION

Date: 2024-05-14

Observation Time: 3:08 PM

Re: KENDALL COUNTY PHASE 1 CLERK BLDG  
Project: 221071

Weather Conditions: 65F  
Sunny




Expansion Joint



Kendall County Halo Lit Sign and Trim Boards



Different Laminate Colors at Reception

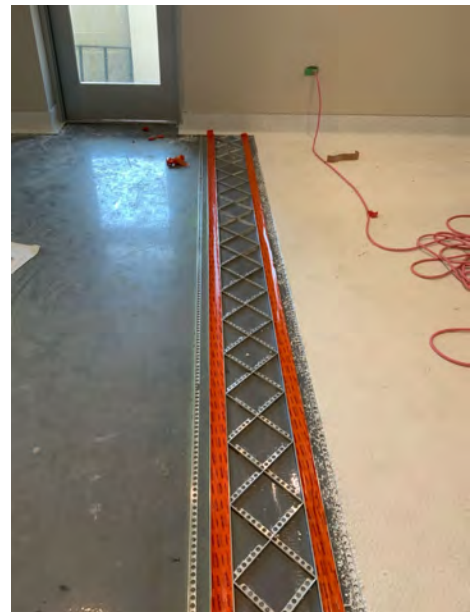

Dividers for Resinous Terrazzo



# PHOTOGRAPHIC DOCUMENTATION

Date: 2024-05-14

Observation Time: 3:08 PM

Re: KENDALL COUNTY PHASE 1 CLERK BLDG

Weather Conditions: 65F

Project: 221071

Sunny



Ceramic Tiling in Toilet Rooms



Shaft Wall Construction



Concrete Wall Finish in Stair



Condensate Pipe in JC




Cast Stone Jamb Repair and Sealant



Edge Return Trim



Additional Framing on North

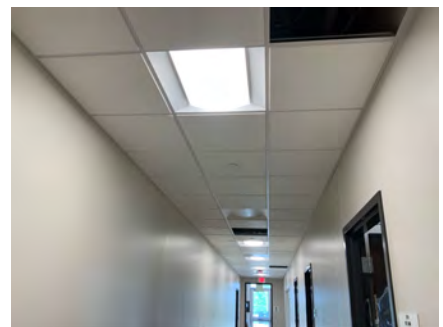

Corridor 107 Ceiling

## FIELD OBSERVATION CONFIRMATION

Date: 2024-05-28 Observation Time: 6:21 PM  
Re: KENDALL COUNTY PHASE 1 CLERK BLDG Weather Conditions: 72F  
Client: Kendall County Overcast  
Project: 221071 --  
Prepared By: Lauren Kiley Phone: 630.896.4678  
Cordogan Clark & Associates Fax: 630.896.4987

Field Report Number: 240528

Est % Completion: 82% Conformance With Schedule (+/-): -7 days

Work In Progress: Concrete planter box, resinous terrazzo flooring application, furniture installation, generator hookup, concrete sidewalk prep and pouring.

### Observations:

1. In Lobby, the resinous floor application is still in progress, base layer primer, colored mortar/grout with granite chip aggregates and cove appears to be poured. Flooring is currently being ground and polished.
2. Furniture installation is in progress in Voter Operations and Clerk Department.
3. In Stair, concrete walls are being patched for holes and prepped for paint.
4. In Break Room, control joint in gypsum board is not flush in corner.
5. In JC, pipe was not installed per M1.2 or shop drawings.
6. Exterior gypsum board ceiling has a gap between top of stone at exit door but not at adjacent window.
7. Planter box foundation walls appear to be framed, and pouring is in progress.
8. The fence along retaining wall appears to be installed, except for section next to the building.

### Items to Verify:

1. Verify location to install panic devices at workstation cubicles.
2. Water was discovered on carpeting near door 118C, verify water is completely dried and did not damage gypsum board and verify carpeting is adequately adhered.
3. Verify if resinous terrazzo flooring material is being applied under mailbox.
4. Exterior double door 006A is missing a hinge, verify this will be installed.

### Information Or Action Required:

1. In Voter Operations, casework seams are not flush on end and do not align on face. Realign.
2. In EV VBM, window muntin is not fully adhered, re-adhere to be flush.
3. In Toilet 1, 2, 4, 5, and 6 owner requested tile be applied to wall adjacent to sink. Tile to extend full height up to door frame, contractor to provide pricing.
4. On exterior, soffit panels are not aligned, realign to be flush.
5. In Elevator, one of the back panels is dented, replace with new.
6. Bollards in southeast corner were removed from scope in PR-003R2. Bollards appear to conflict with new landscaping, remove without damaging the gas line.

### Attachments:

Progress Photos

# PHOTOGRAPHIC DOCUMENTATION

Date: 2024-05-28

Observation Time: 6:21 PM

Re: KENDALL COUNTY PHASE 1 CLERK BLDG

Weather Conditions: 72F

Project: 221071

Overcast



Wall in Toilet Room



Resinous Terrazzo Floor Progress



Terrazzo Application at Mailbox



Muntin in Window



# PHOTOGRAPHIC DOCUMENTATION

Date: 2024-05-28

Observation Time: 6:21 PM

Re: KENDALL COUNTY PHASE 1 CLERK BLDG

Weather Conditions: 72F

Project: 221071

Overcast



Soffit Panels at Gable



Door 006A




Exterior Gyp. Bd. At Door



Bollards on Southeast Corner




Dented Panel in Elevator

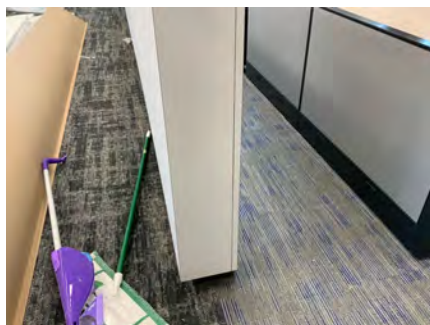

Casework in Voter Operations



Control Joint in Break Room

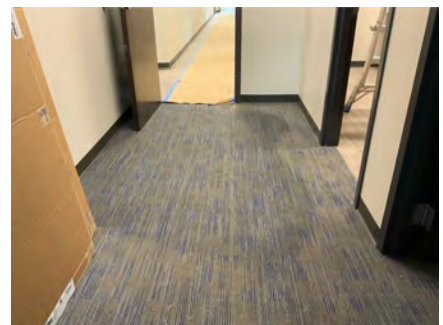

Wet Carpeting near Door 118C



960 Ridgeway Avenue  
Aurora, Illinois 60506  
T: 630.896.4678  
F: 630.896.4987

Aurora, Illinois  
Chicago, Illinois  
Cleveland, Ohio  
Davenport, Iowa  
Lafayette, Indiana  
St. Louis, Missouri  
Sawyer, Michigan  
Madrid, Spain

[cordoganclark.com](http://cordoganclark.com)
