

Form detail

#108: Weekly Report

**Forms**

Location Kendall County New Office Building

Form date Jan 26, 2024

Description

Due date

Submitted by Ken Gleason

Status Closed

Last update Jan 26, 2024, 2:55 PM CST

Last updated by Ken Gleason

Included references Assets | Files | Forms | Issues | Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	2	16	crew worked on,site clean up, they worked with the roofers to get the saddles completed at chimneys in order for roofers to add flashing and get the roof to a closed and dry state.
BP #13 Electrical - CSN Electric	2	16	crew worked on electrical piping and wiring in basement, they will be moving to the first floor next week to get started on that level with electrical rough in as well
BP #7 Roofing - Filotto Roofing	4	32	crew worked on completing the ice and water shield and was able to get started on the shingles for the roof
BP #12 Mechanical - Jensen's Plumbing & Heating	1	8	worked on mechanical piping in basement and at mechanical pad at exterior
Totals	9	72	

References

Photos (15)



IMG_1007

Taken on Jan 26, 2024, 8:23 AM CST

Added on Jan 26, 2024, 2:54 PM CST

Added by Ken Gleason



IMG_1009

Taken on Jan 26, 2024, 8:26 AM CST

Added on Jan 26, 2024, 2:54 PM CST

Added by Ken Gleason



IMG_1010

Taken on Jan 26, 2024, 8:26 AM CST

Added on Jan 26, 2024, 2:54 PM CST

Added by Ken Gleason



IMG_1008

Taken on Jan 26, 2024, 8:24 AM CST

Added on Jan 26, 2024, 2:54 PM CST

Added by Ken Gleason



IMG_1013

Taken on Jan 26, 2024, 8:28 AM CST

Added on Jan 26, 2024, 2:54 PM CST

Added by Ken Gleason



IMG_1012

Taken on Jan 26, 2024, 8:26 AM CST

Added on Jan 26, 2024, 2:54 PM CST

Added by Ken Gleason



IMG_1021

Taken on Jan 26, 2024, 11:36 AM CST

Added on Jan 26, 2024, 2:54 PM CST

Added by Ken Gleason



IMG_1014

Taken on Jan 26, 2024, 8:29 AM CST

Added on Jan 26, 2024, 2:54 PM CST

Added by Ken Gleason



IMG_1020

Taken on Jan 26, 2024, 11:35 AM CST

Added on Jan 26, 2024, 2:54 PM CST

Added by Ken Gleason



IMG_1019

Taken on Jan 26, 2024, 11:33 AM CST

Added on Jan 26, 2024, 2:54 PM CST

Added by Ken Gleason



IMG_1011

Taken on Jan 26, 2024, 8:26 AM CST

Added on Jan 26, 2024, 2:54 PM CST

Added by Ken Gleason



IMG_1015

Taken on Jan 26, 2024, 8:29 AM CST

Added on Jan 26, 2024, 2:54 PM CST

Added by Ken Gleason



IMG_1018

Taken on Jan 26, 2024, 8:32 AM CST

Added on Jan 26, 2024, 2:54 PM CST

Added by Ken Gleason




IMG_1016

Taken on Jan 26, 2024, 8:29 AM CST

Added on Jan 26, 2024, 2:54 PM CST

Added by Ken Gleason

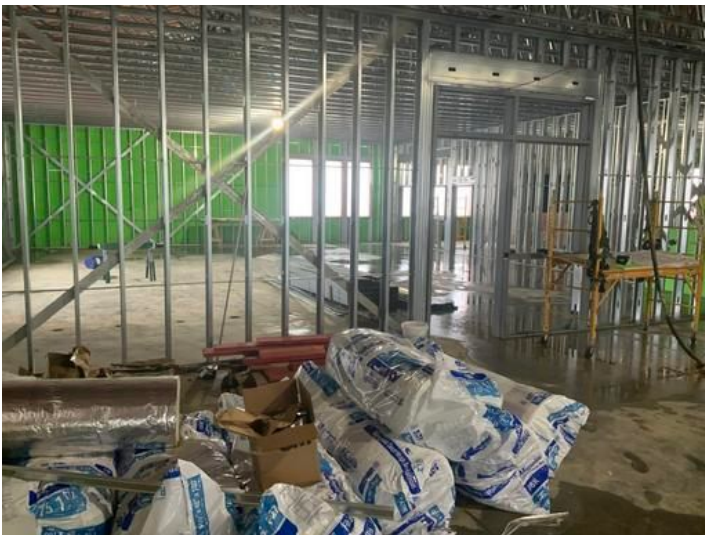

IMG_1017

Taken on Jan 26, 2024, 8:32 AM CST

Added on Jan 26, 2024, 2:54 PM CST

Added by Ken Gleason
