

Form detail

#137: Weekly Report

**Forms**

Location	Kendall County New Office Building
Form date	Mar 8, 2024
Description	
Due date	
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 8, 2024, 2:36 PM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	7	56	crew worked on drywall, taping and sanding most rooms as well as hanging drywall in the barrel vaulted ceiling in lobby area
BP #8 Painting - Nedrow Painting	2	16	crew got started with priming walls in the rooms on the southern half of the interior today
BP #12 Mechanical - Jensen's Plumbing & Heating	1	8	worked on mechanical piping overhead on the first floor today
BP #13 Electrical - CSN Electric	3	24	crew worked on electrical piping on first floor and basement today
Totals	13	104	

References

Photos (18)



IMG_1380

Taken on Mar 8, 2024, 8:15 AM CST

Added on Mar 8, 2024, 2:35 PM CST

Added by Ken Gleason



IMG_1381

Taken on Mar 8, 2024, 8:15 AM CST

Added on Mar 8, 2024, 2:35 PM CST

Added by Ken Gleason



IMG_1382

Taken on Mar 8, 2024, 8:16 AM CST

Added on Mar 8, 2024, 2:35 PM CST

Added by Ken Gleason




IMG_1390

Taken on Mar 8, 2024, 8:19 AM CST

Added on Mar 8, 2024, 2:35 PM CST

Added by Ken Gleason

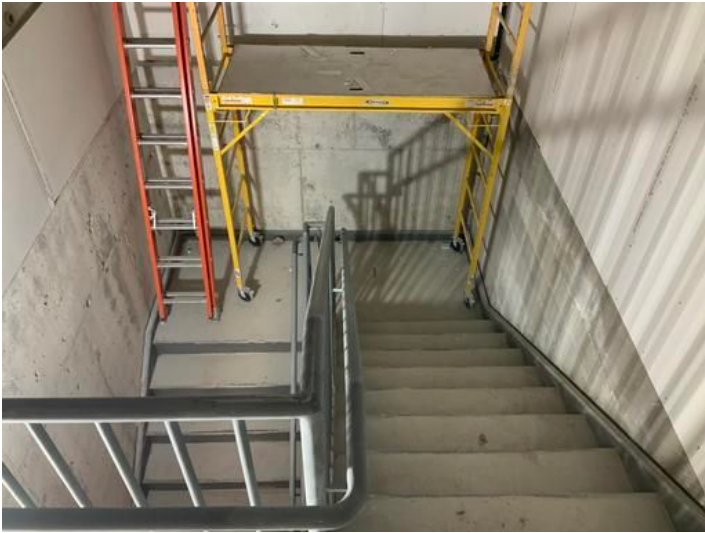

IMG_1383

Taken on Mar 8, 2024, 8:17 AM CST
Added on Mar 8, 2024, 2:35 PM CST
Added by Ken Gleason



IMG_1385

Taken on Mar 8, 2024, 8:18 AM CST
Added on Mar 8, 2024, 2:35 PM CST
Added by Ken Gleason



IMG_1389

Taken on Mar 8, 2024, 8:19 AM CST
Added on Mar 8, 2024, 2:35 PM CST
Added by Ken Gleason



IMG_1384

Taken on Mar 8, 2024, 8:17 AM CST
Added on Mar 8, 2024, 2:35 PM CST
Added by Ken Gleason



IMG_1386

Taken on Mar 8, 2024, 8:18 AM CST

Added on Mar 8, 2024, 2:36 PM CST

Added by Ken Gleason



IMG_1388

Taken on Mar 8, 2024, 8:19 AM CST

Added on Mar 8, 2024, 2:36 PM CST

Added by Ken Gleason



IMG_1387

Taken on Mar 8, 2024, 8:18 AM CST

Added on Mar 8, 2024, 2:36 PM CST

Added by Ken Gleason



IMG_1391

Taken on Mar 8, 2024, 8:25 AM CST

Added on Mar 8, 2024, 2:36 PM CST

Added by Ken Gleason



IMG_1397

Taken on Mar 8, 2024, 8:27 AM CST

Added on Mar 8, 2024, 2:36 PM CST

Added by Ken Gleason



IMG_1393

Taken on Mar 8, 2024, 8:26 AM CST

Added on Mar 8, 2024, 2:36 PM CST

Added by Ken Gleason



IMG_1396

Taken on Mar 8, 2024, 8:27 AM CST

Added on Mar 8, 2024, 2:36 PM CST

Added by Ken Gleason



IMG_1392

Taken on Mar 8, 2024, 8:25 AM CST

Added on Mar 8, 2024, 2:36 PM CST

Added by Ken Gleason



IMG_1394

Taken on Mar 8, 2024, 8:26 AM CST

Added on Mar 8, 2024, 2:36 PM CST

Added by Ken Gleason



IMG_1395

Taken on Mar 8, 2024, 8:27 AM CST

Added on Mar 8, 2024, 2:36 PM CST

Added by Ken Gleason
