

Form detail

#141: Weekly Report

**Forms**

Location	Kendall County New Office Building
Form date	Mar 15, 2024
Description	
Due date	
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 15, 2024, 12:55 PM CDT
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	5	40	crew worked on drywall taping/finishing as well as getting started with the ceiling grids
BP #6 Masonry - Jimmy'z Masonry	9	72	crew worked on install of exterior stone/veneer at southwest and southern side of the building
BP #12 Mechanical - Jensen's Plumbing & Heating	2	16	crew worked on mechanical piping at the first floor level
BP #13 Electrical - CSN Electric	3	24	crew worked on electrical piping and wiring in basement and first floor
BP #15 Elevator - Otis Elevator Company	2	16	crew worked on elevator install
Totals	21	168	

References

Photos (12)



IMG_1435

Taken on Mar 15, 2024, 8:36 AM CDT
Added on Mar 15, 2024, 12:54 PM CDT
Added by Ken Gleason



IMG_1434

Taken on Mar 15, 2024, 8:36 AM CDT
Added on Mar 15, 2024, 12:54 PM CDT
Added by Ken Gleason



IMG_1431

Taken on Mar 15, 2024, 8:35 AM CDT
Added on Mar 15, 2024, 12:55 PM CDT
Added by Ken Gleason




IMG_1433

Taken on Mar 15, 2024, 8:36 AM CDT
Added on Mar 15, 2024, 12:55 PM CDT
Added by Ken Gleason



IMG_1432

Taken on Mar 15, 2024, 8:35 AM CDT
Added on Mar 15, 2024, 12:55 PM CDT
Added by Ken Gleason

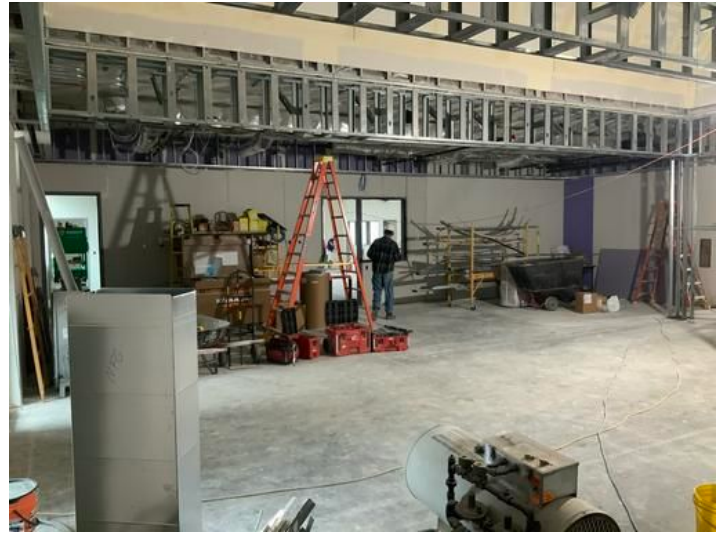

IMG_1436

Taken on Mar 15, 2024, 8:36 AM CDT
Added on Mar 15, 2024, 12:55 PM CDT
Added by Ken Gleason



IMG_1437

Taken on Mar 15, 2024, 8:37 AM CDT
Added on Mar 15, 2024, 12:55 PM CDT
Added by Ken Gleason



IMG_1438

Taken on Mar 15, 2024, 11:03 AM CDT
Added on Mar 15, 2024, 12:55 PM CDT
Added by Ken Gleason



IMG_1439

Taken on Mar 15, 2024, 11:04 AM CDT
Added on Mar 15, 2024, 12:55 PM CDT
Added by Ken Gleason



IMG_1440

Taken on Mar 15, 2024, 11:04 AM CDT
Added on Mar 15, 2024, 12:55 PM CDT
Added by Ken Gleason



IMG_1441

Taken on Mar 15, 2024, 11:04 AM CDT
Added on Mar 15, 2024, 12:55 PM CDT
Added by Ken Gleason



IMG_1442

Taken on Mar 15, 2024, 11:05 AM CDT
Added on Mar 15, 2024, 12:55 PM CDT
Added by Ken Gleason
