

MONTHLY PROGRESS REPORT

KENDALL COUNTY

NEW OFFICE BUILDING

MARCH 2024





March Monthly Report

Construction Management Services

April 2024

Contents

Section 1: Project Update

Section 2: Project Cost Report

Section 3: Schedule

Section 4: Construction Field Reports and Photos

Section 5: Architectural & Engineering Field Reports

SECTION 1



Kendall County

New Office Building

Monthly Project Summary 3/29/24
Work Completed in March 2024

To date we have completed the following activities:

- Rough In Mechanical Piping & Ductwork
- Fire Protection Piping
- Rough In Plumbing
- Rough In Electrical
- HVAC Equipment Install & Hookup
- Drywall – Taping & Finishing

We are currently progressing on the following activities:

- Elevator Install
- Painting
- Ceilings
- MEP Trim Work
- Exterior Stone/Brick Veneer
- Roof Overhead Returns/Soffit/Fascia/Gutters

The following phases of construction scheduled for the near future:

- Flooring
- Casework
- Doors/Finished Carpentry
- Paint Touch Ups & Final Finishes
- Generator Install & Testing
- Site Excavation

SECTION 2




Kendall County – New Office Building


Cost Report & Contingency Reductions

PCO #	Date Approved By Owner	Contractor	Description	Potential Contingency Reduction Amount	Contingency Reduction Amount Approved	Comments
CONTINGENCY REDUCTIONS APPROVED IN OCTOBER 2023:					\$45,035	
CONTINGENCY REDUCTIONS APPROVED IN NOVEMBER 2023:					\$75,448	
CONTINGENCY REDUCTIONS APPROVED IN DECEMBER 2023:					\$6,580	
CONTINGENCY REDUCTIONS APPROVED IN JANUARY 2024:					\$145,632	
CONTINGENCY REDUCTIONS TO BE APPROVED IN FEBRUARY 2024:					\$22,713	
CONTINGENCY REDUCTIONS TO BE APPROVED IN MARCH 2024:					\$38,046	
13, 14 & 18		LCI	PR 15 Relocate & increase size of flagpoles, PR16 Changes as a result of data and power verification as result of County walk through, and Material & labor for additional signage (County request)	\$12,412	\$12,412	
15 & 19		LCI	Material & labor to build protection around HVAC units, required site snow removal, securing site from heavy winds and storms	\$4,469	\$4,469	
		Plainfield Grading	PR-003 Excavation and backfill for ramp	\$5,545	\$5,545	
		Premium Concrete	Winter Conditions for concrete pours and reinstall drainage boards due to weather conditions	\$6,875	\$6,875	
		Premium Concrete	Credit for elimination of stairs in lieu of ramp and credit for foundations under mechanical equipment pads.	(\$11,006)	(\$11,006)	
CONTINGENCY REDUCTIONS TO BE APPROVED IN APRIL 2024:					\$18,295	

SECTION 3



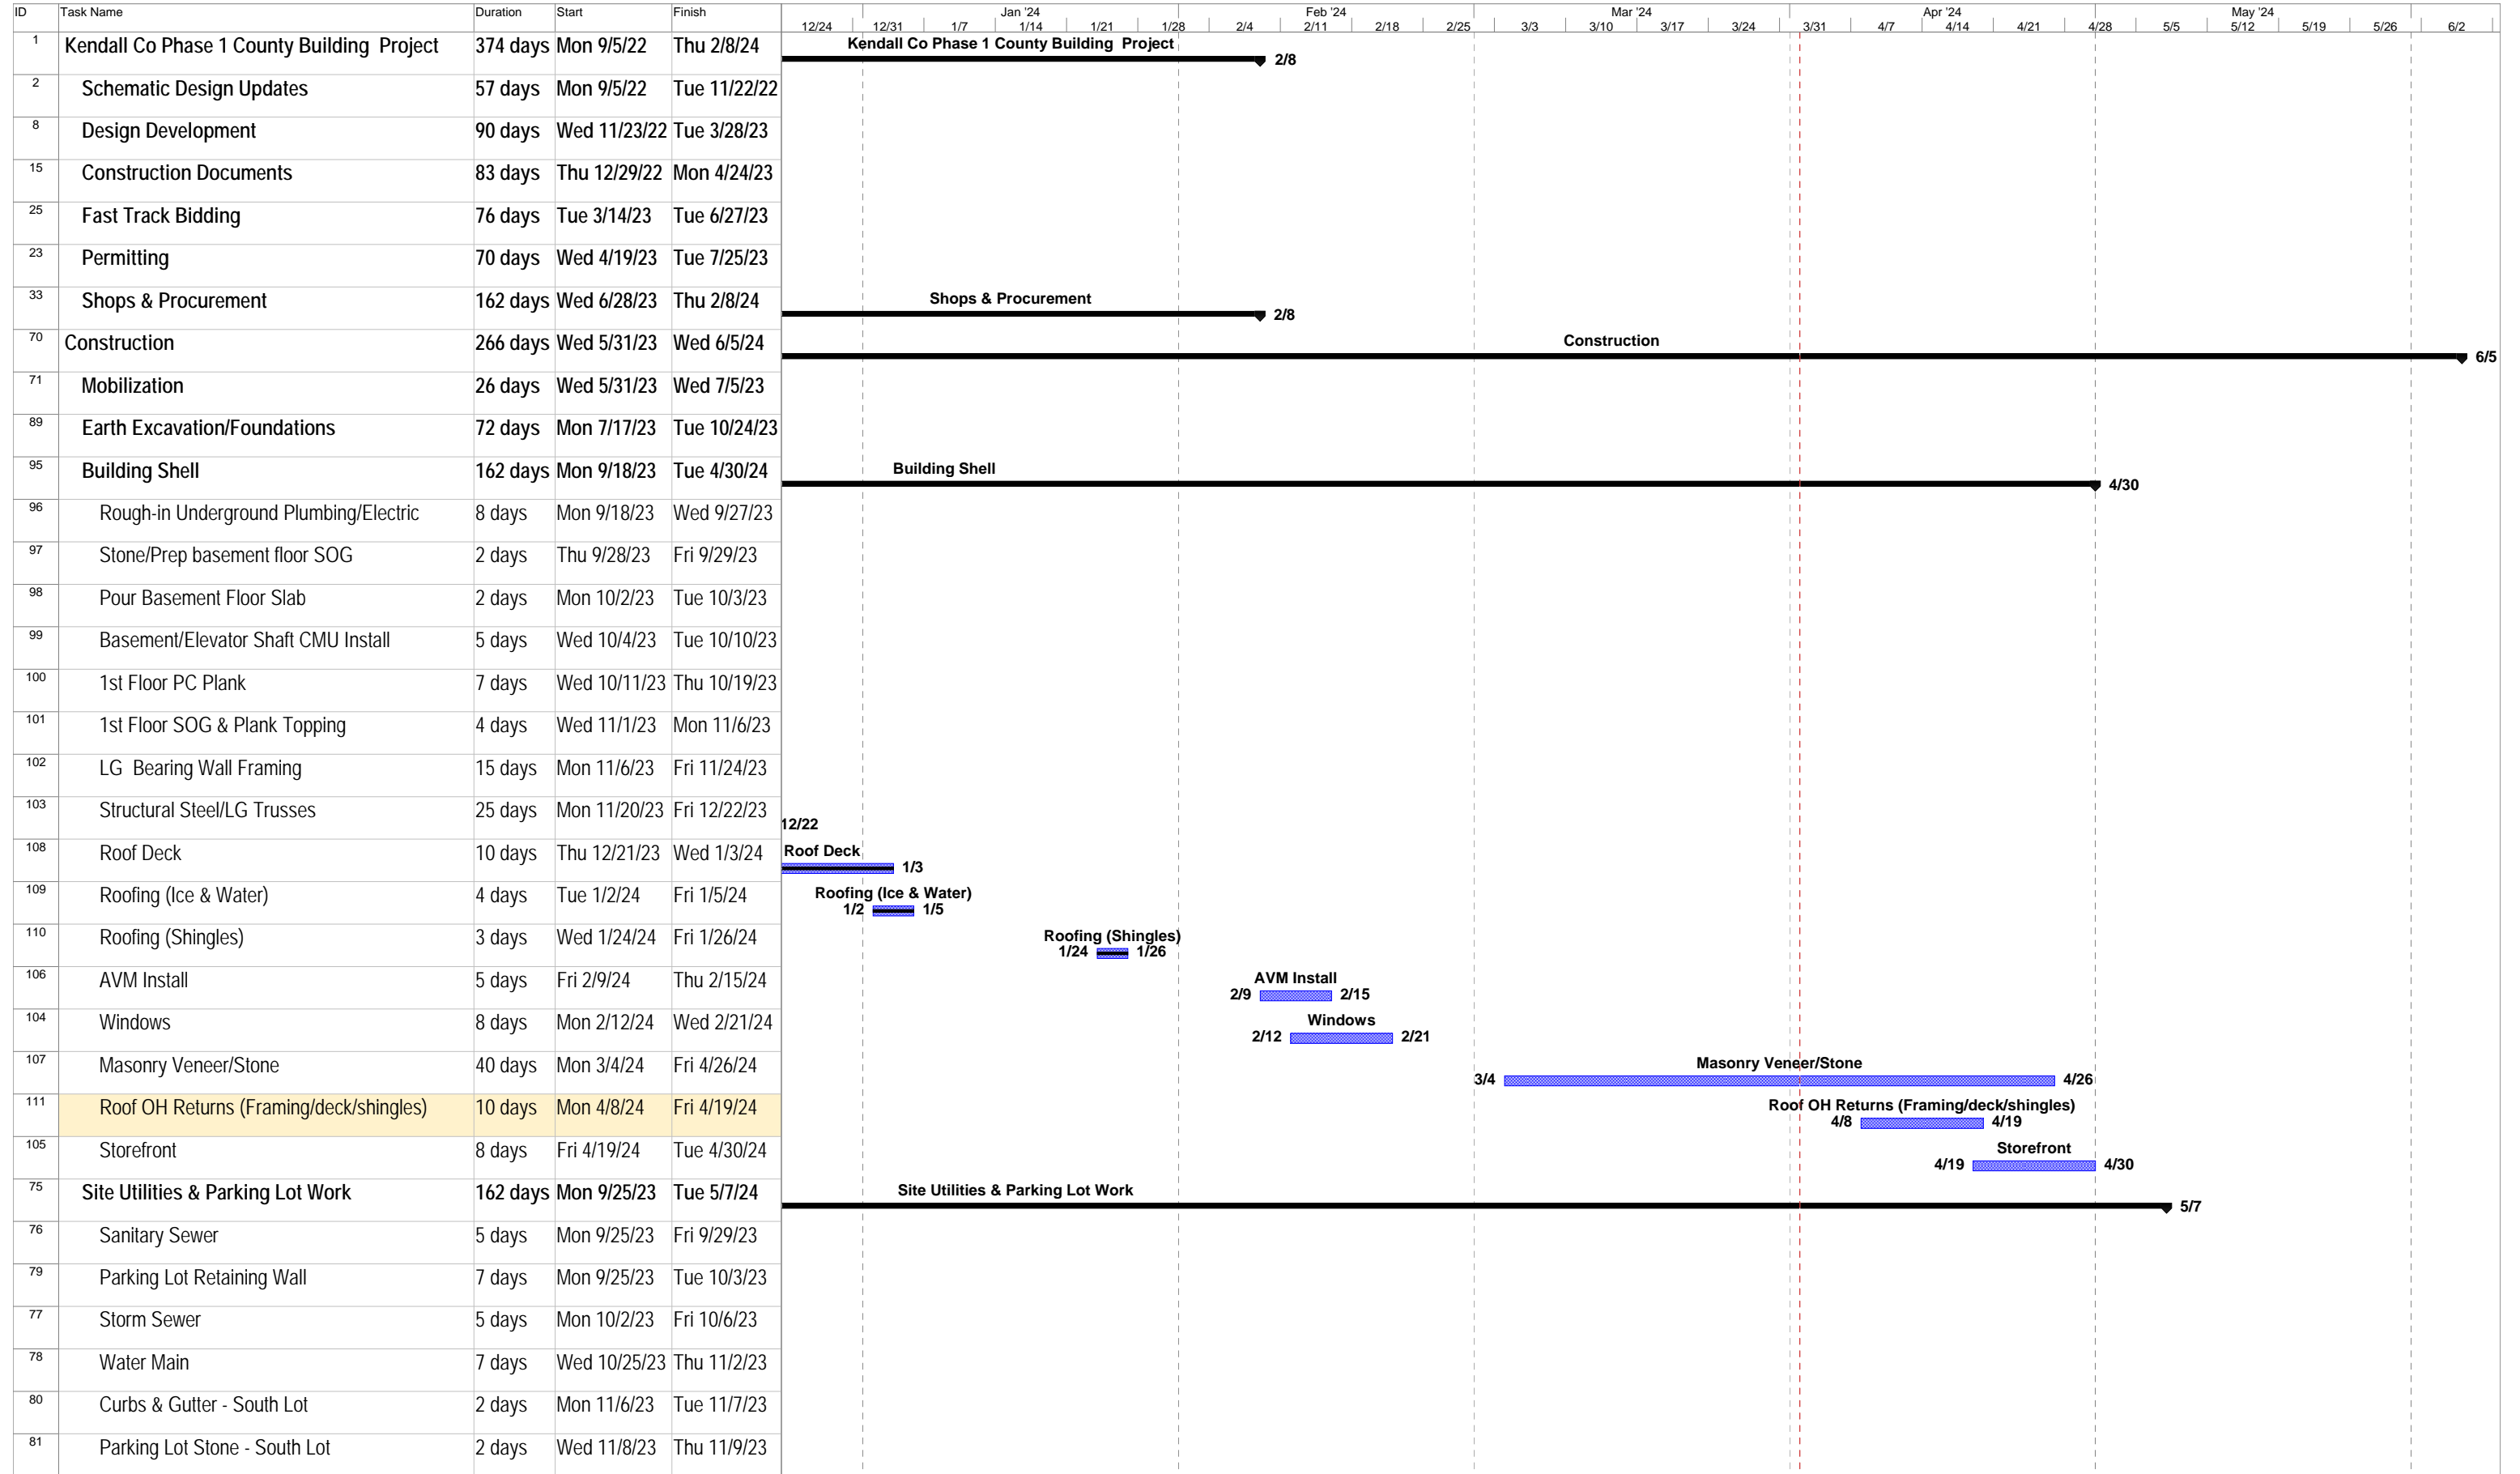

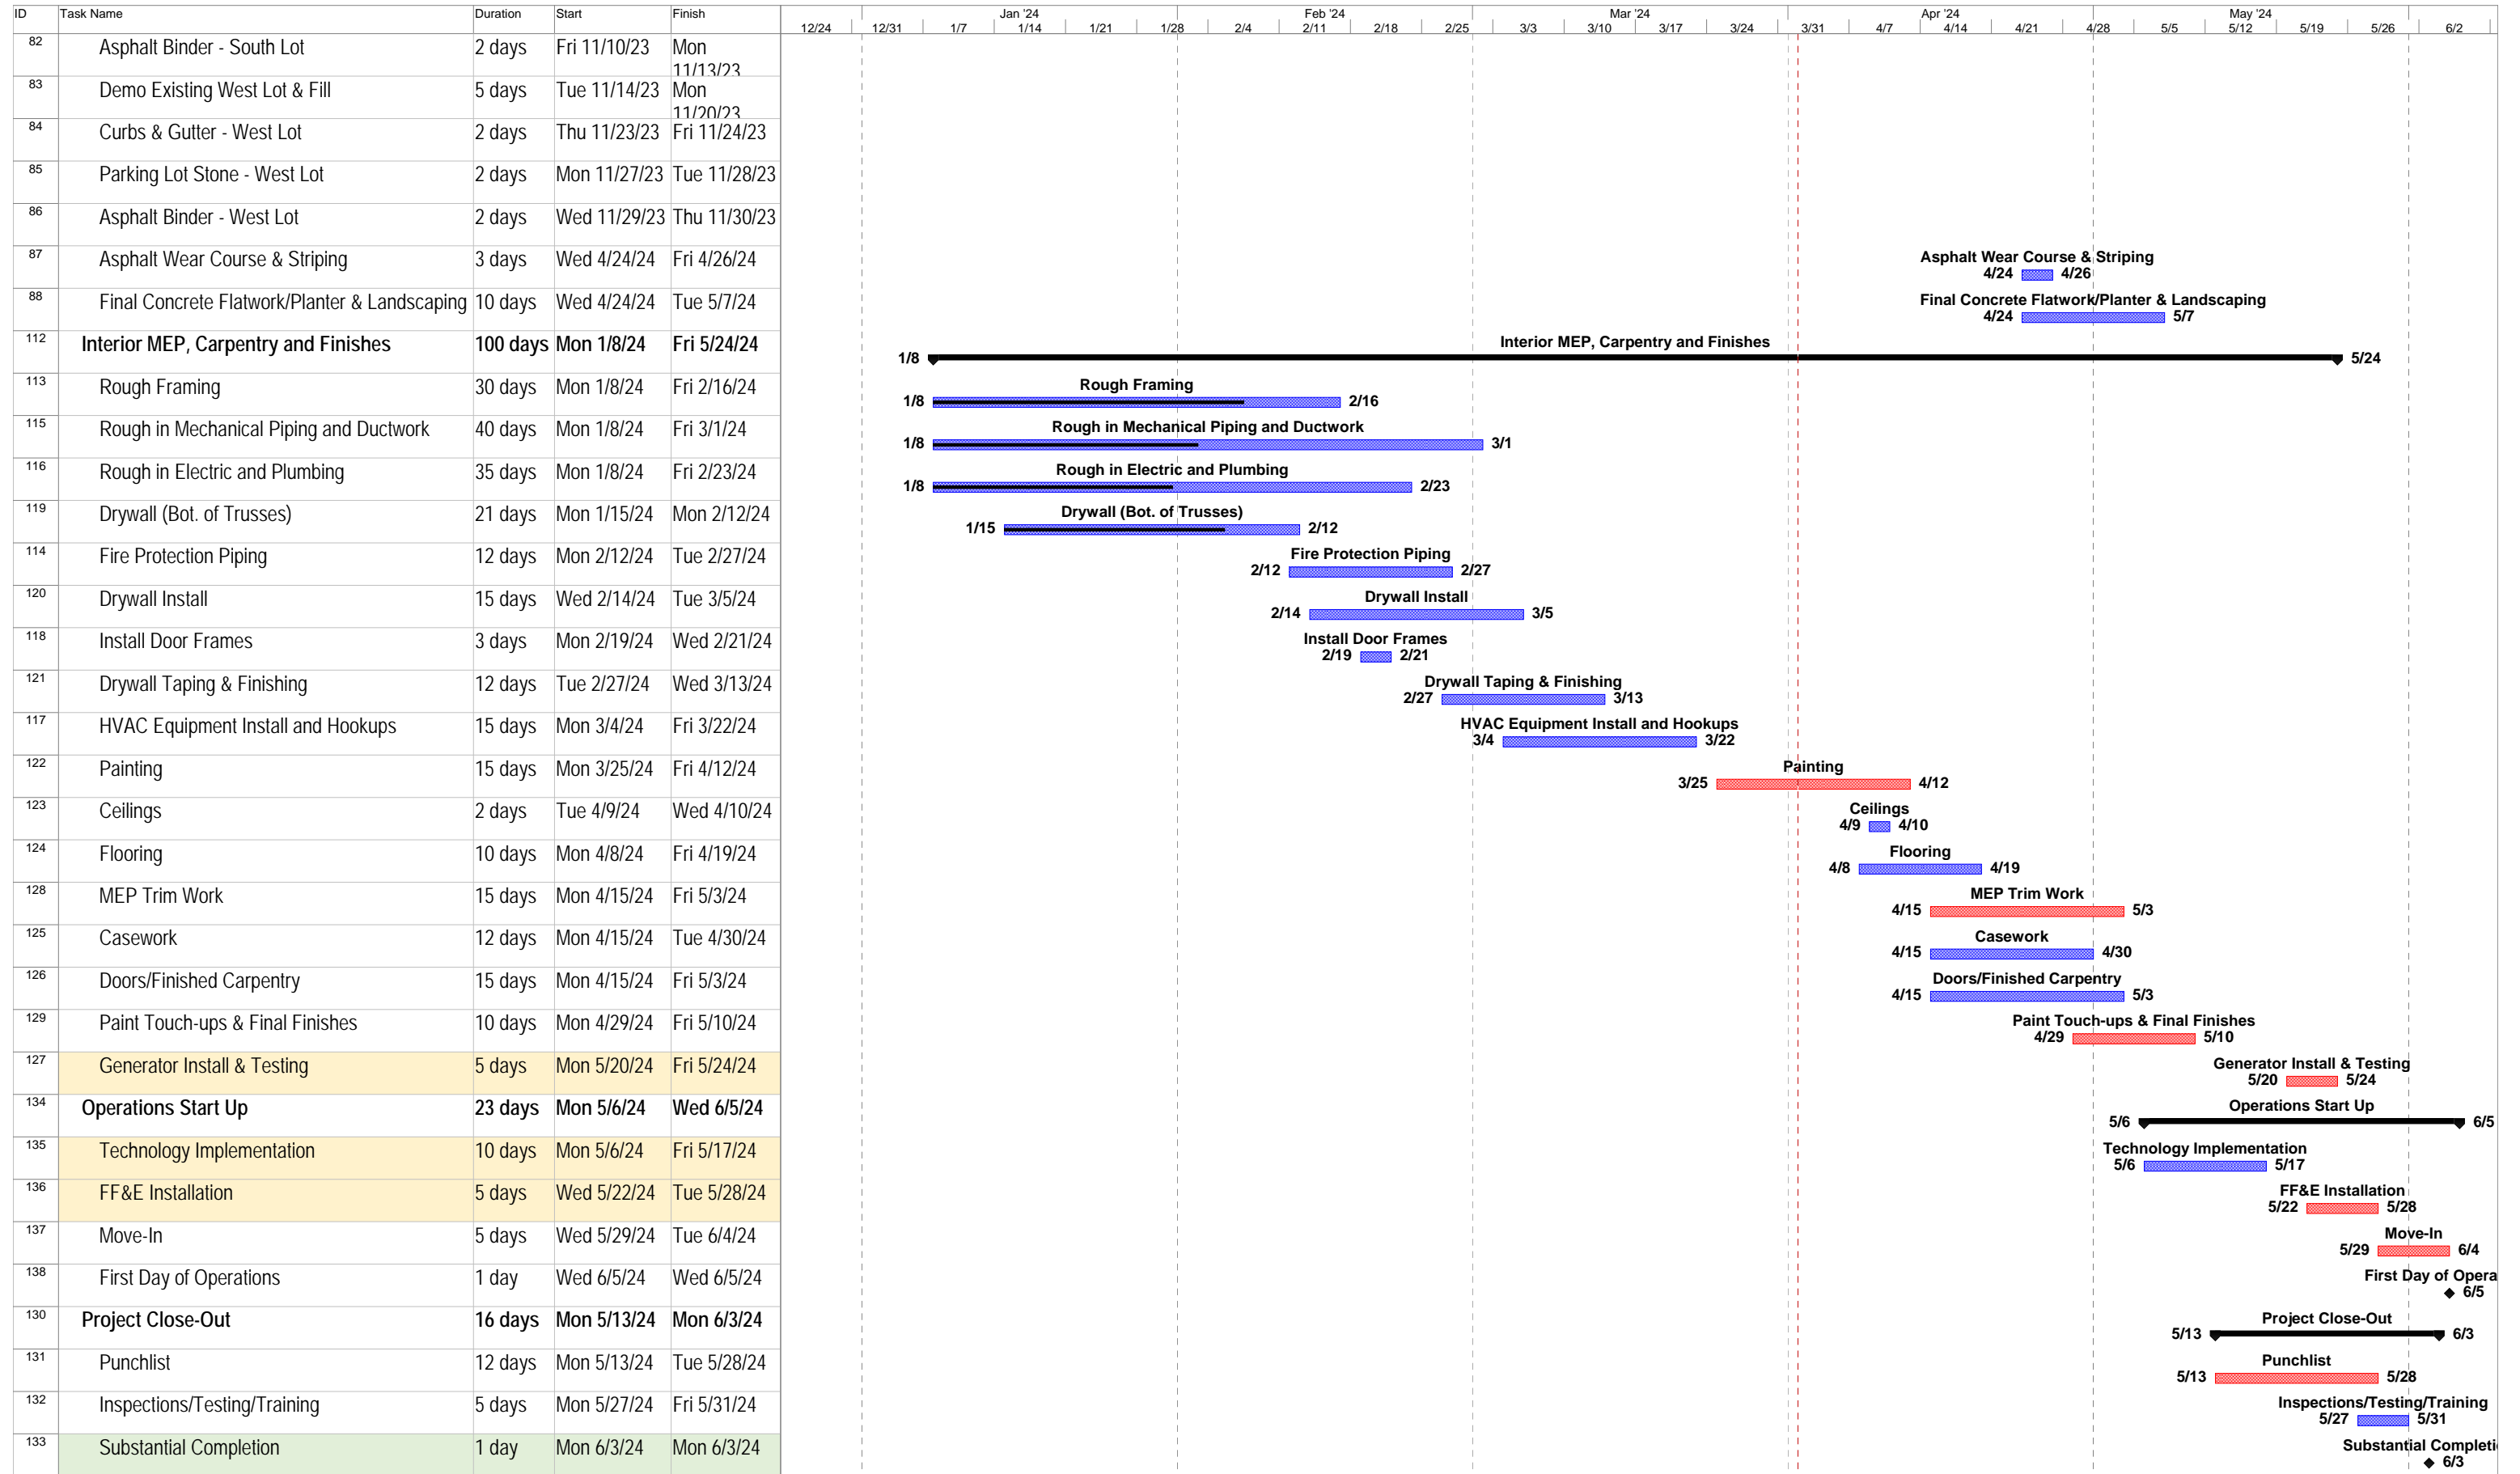

SECTION 4



Form detail

#133: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Mar 4, 2024
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 4, 2024, 11:28 AM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0.24 inches

🍏 Weather [View Sources](#)

7:00 AM

Partly Cloudy



Temperature: 50°F

Wind: ↻ 4mph

Humidity: 94%

12:00 PM

Cloudy



Temperature: 65°F

Wind: ↑ 11mph

Humidity: 76%

4:00 PM

Windy



Temperature: 73°F

Wind: ↑ 16mph

Humidity: 62%

Updated Mar 19, 2024 at 2:54 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	7	56	crew worked on interior framing drywall and taping today on first floor
BP #6 Masonry - Jimmy'z Masonry	6	48	crew worked on stone work at south west corner of building, setting up scaffolding throughout
BP #10 Fire Protection - CL Doucette Inc	2	16	crew worked on fire protection piping in basement today
BP #12 Mechanical - Jensen's Plumbing & Heating	3	24	crew worked on mechanical piping and ductwork with insulation today
BP #13 Electrical - CSN Electric	2	16	crew worked on exterior wiring at electrical panels today
BP #15 Elevator - Otis Elevator Company	3	24	crew worked on install of the elevator today, work began at basement level
Totals	23	184	

References

Photos (15)



IMG_1336

Taken on Mar 4, 2024, 10:36 AM CST

Added on Mar 4, 2024, 11:27 AM CST

Added by Ken Gleason



IMG_1337

Taken on Mar 4, 2024, 10:36 AM CST

Added on Mar 4, 2024, 11:27 AM CST

Added by Ken Gleason



IMG_1338

Taken on Mar 4, 2024, 10:38 AM CST

Added on Mar 4, 2024, 11:27 AM CST

Added by Ken Gleason



IMG_1342

Taken on Mar 4, 2024, 10:44 AM CST

Added on Mar 4, 2024, 11:27 AM CST

Added by Ken Gleason



IMG_1339

Taken on Mar 4, 2024, 10:38 AM CST

Added on Mar 4, 2024, 11:27 AM CST

Added by Ken Gleason



IMG_1341

Taken on Mar 4, 2024, 10:39 AM CST

Added on Mar 4, 2024, 11:27 AM CST

Added by Ken Gleason



IMG_1340

Taken on Mar 4, 2024, 10:38 AM CST

Added on Mar 4, 2024, 11:27 AM CST

Added by Ken Gleason



IMG_1343

Taken on Mar 4, 2024, 10:44 AM CST

Added on Mar 4, 2024, 11:27 AM CST

Added by Ken Gleason



IMG_1344

Taken on Mar 4, 2024, 10:44 AM CST

Added on Mar 4, 2024, 11:27 AM CST

Added by Ken Gleason



IMG_1345

Taken on Mar 4, 2024, 10:44 AM CST

Added on Mar 4, 2024, 11:28 AM CST

Added by Ken Gleason




IMG_1347

Taken on Mar 4, 2024, 10:45 AM CST

Added on Mar 4, 2024, 11:28 AM CST

Added by Ken Gleason

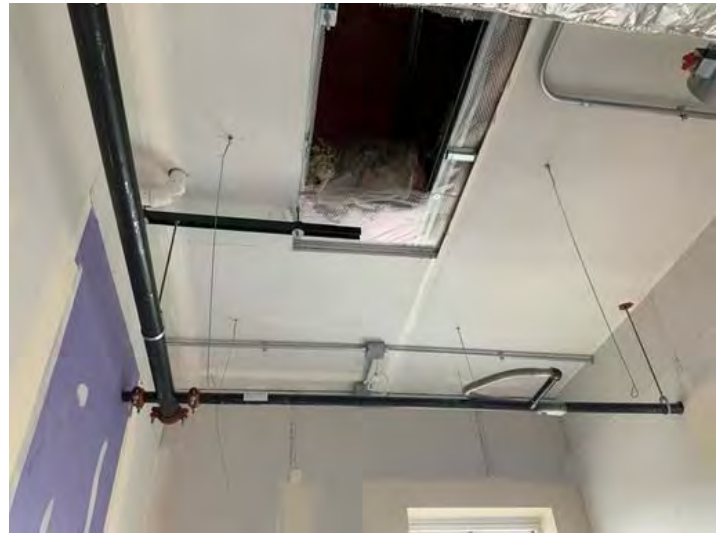

IMG_1346

Taken on Mar 4, 2024, 10:45 AM CST

Added on Mar 4, 2024, 11:28 AM CST

Added by Ken Gleason



IMG_1349

Taken on Mar 4, 2024, 10:46 AM CST

Added on Mar 4, 2024, 11:28 AM CST

Added by Ken Gleason



IMG_1348

Taken on Mar 4, 2024, 10:45 AM CST

Added on Mar 4, 2024, 11:28 AM CST

Added by Ken Gleason



IMG_1350

Taken on Mar 4, 2024, 10:46 AM CST

Added on Mar 4, 2024, 11:28 AM CST

Added by Ken Gleason

Form detail

#134: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Mar 5, 2024
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 5, 2024, 4:40 PM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0.94 inches

🍏 Weather [View Sources](#)

7:00 AM

Cloudy



Temperature: 42°F

Wind: ↙ 11mph

Humidity: 91%

12:00 PM

Cloudy



Temperature: 47°F

Wind: ↙ 9mph

Humidity: 80%

4:00 PM

Cloudy



Temperature: 49°F

Wind: ↙ 8mph

Humidity: 74%

Updated Mar 19, 2024 at 2:55 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	7	56	crew worked on hanging drywall and taping along with framing of the barrel vault ceiling at front lobby area today
BP #10 Fire Protection - CL Doucette Inc	2	16	crew worked on fire protection piping in basement today
BP #12 Mechanical - Jensen's Plumbing & Heating	3	24	crew worked on mechanical piping and ductwork and insulation install today
BP #13 Electrical - CSN Electric	3	24	crew worked on electrical piping in basement and exterior at mechanical pad today
Totals	15	120	

References

Photos (10)



IMG_1351

Taken on Mar 5, 2024, 4:03 PM CST

Added on Mar 5, 2024, 4:39 PM CST

Added by Ken Gleason



IMG_1354

Taken on Mar 5, 2024, 4:30 PM CST

Added on Mar 5, 2024, 4:39 PM CST

Added by Ken Gleason



IMG_1352

Taken on Mar 5, 2024, 4:03 PM CST

Added on Mar 5, 2024, 4:39 PM CST

Added by Ken Gleason



IMG_1358

Taken on Mar 5, 2024, 4:32 PM CST

Added on Mar 5, 2024, 4:39 PM CST

Added by Ken Gleason



IMG_1360
Taken on Mar 5, 2024, 4:32 PM CST
Added on Mar 5, 2024, 4:40 PM CST
Added by Ken Gleason



IMG_1359
Taken on Mar 5, 2024, 4:32 PM CST
Added on Mar 5, 2024, 4:40 PM CST
Added by Ken Gleason



IMG_1356
Taken on Mar 5, 2024, 4:32 PM CST
Added on Mar 5, 2024, 4:40 PM CST
Added by Ken Gleason



IMG_1357
Taken on Mar 5, 2024, 4:32 PM CST
Added on Mar 5, 2024, 4:40 PM CST
Added by Ken Gleason



IMG_1353

Taken on Mar 5, 2024, 4:04 PM CST

Added on Mar 5, 2024, 4:40 PM CST

Added by Ken Gleason



IMG_1355

Taken on Mar 5, 2024, 4:31 PM CST

Added on Mar 5, 2024, 4:40 PM CST

Added by Ken Gleason

Form detail

#135: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Mar 6, 2024
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 6, 2024, 12:47 PM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Mostly Cloudy



Temperature: 40°F

Wind: ↙ 8mph

Humidity: 87%

12:00 PM

Mostly Clear



Temperature: 51°F

Wind: ↙ 10mph

Humidity: 65%

4:00 PM

Clear



Temperature: 52°F

Wind: ↙ 10mph

Humidity: 53%

Updated Mar 19, 2024 at 2:56 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	7	56	crew worked on framing, drywall and taping today on the first floor
BP #6 Masonry - Jimmy'z Masonry	7	56	crew worked on exterior stone setting along south side of building
BP #12 Mechanical - Jensen's Plumbing & Heating	3	24	crew worked on mechanical piping and ductwork at first floor today
BP #13 Electrical - CSN Electric	3	24	crew worked on main electrical box at mechanical pad, interior electrical piping on first floor
BP #15 Elevator - Otis Elevator Company	2	16	crew worked on install of elevator at basement level today
Totals	22	176	

References

Photos (10)



IMG_1367

Taken on Mar 6, 2024, 11:58 AM CST

Added on Mar 6, 2024, 12:47 PM CST

Added by Ken Gleason




IMG_1361

Taken on Mar 6, 2024, 11:56 AM CST

Added on Mar 6, 2024, 12:47 PM CST

Added by Ken Gleason

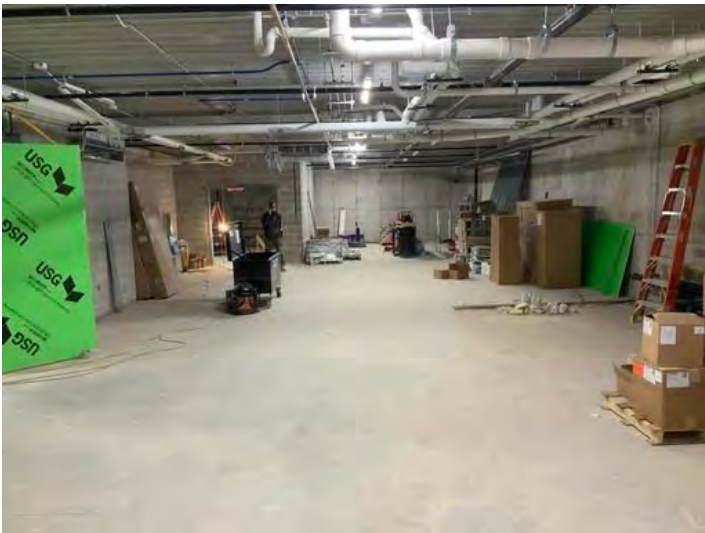

IMG_1364

Taken on Mar 6, 2024, 11:57 AM CST

Added on Mar 6, 2024, 12:47 PM CST

Added by Ken Gleason



IMG_1365

Taken on Mar 6, 2024, 11:57 AM CST

Added on Mar 6, 2024, 12:47 PM CST

Added by Ken Gleason



IMG_1368

Taken on Mar 6, 2024, 11:58 AM CST

Added on Mar 6, 2024, 12:47 PM CST

Added by Ken Gleason



IMG_1366

Taken on Mar 6, 2024, 11:58 AM CST

Added on Mar 6, 2024, 12:47 PM CST

Added by Ken Gleason



IMG_1370

Taken on Mar 6, 2024, 11:59 AM CST

Added on Mar 6, 2024, 12:47 PM CST

Added by Ken Gleason



IMG_1362

Taken on Mar 6, 2024, 11:56 AM CST

Added on Mar 6, 2024, 12:47 PM CST

Added by Ken Gleason



IMG_1369

Taken on Mar 6, 2024, 11:59 AM CST
Added on Mar 6, 2024, 12:47 PM CST
Added by Ken Gleason



IMG_1363

Taken on Mar 6, 2024, 11:57 AM CST
Added on Mar 6, 2024, 12:47 PM CST
Added by Ken Gleason

Form detail

#136: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Mar 7, 2024
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 7, 2024, 4:54 PM CST
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Cloudy



Temperature: 37°F

Wind: ← 4mph

Humidity: 85%

12:00 PM

Cloudy



Temperature: 46°F

Wind: ↻ 5mph

Humidity: 83%

4:00 PM

Cloudy



Temperature: 49°F

Wind: ← 6mph

Humidity: 79%

Updated Mar 19, 2024 at 2:56 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	7	56	crew worked on barrel vaulted ceiling framing along with drywall and taping today
BP #6 Masonry - Jimmy's Masonry	9	72	crew worked on exterior stone install today
BP #12 Mechanical - Jensen's Plumbing & Heating	1	5	HVAC. rough in for controls was being worked on
BP #13 Electrical - CSN Electric	3	24	crew worked on electrical piping at first floor today
Totals	20	157	

References

Photos (8)



IMG_1372

Taken on Mar 7, 2024, 12:41 PM CST

Added on Mar 7, 2024, 4:54 PM CST

Added by Ken Gleason



IMG_1374

Taken on Mar 7, 2024, 12:41 PM CST

Added on Mar 7, 2024, 4:54 PM CST

Added by Ken Gleason




IMG_1376

Taken on Mar 7, 2024, 12:42 PM CST

Added on Mar 7, 2024, 4:54 PM CST

Added by Ken Gleason

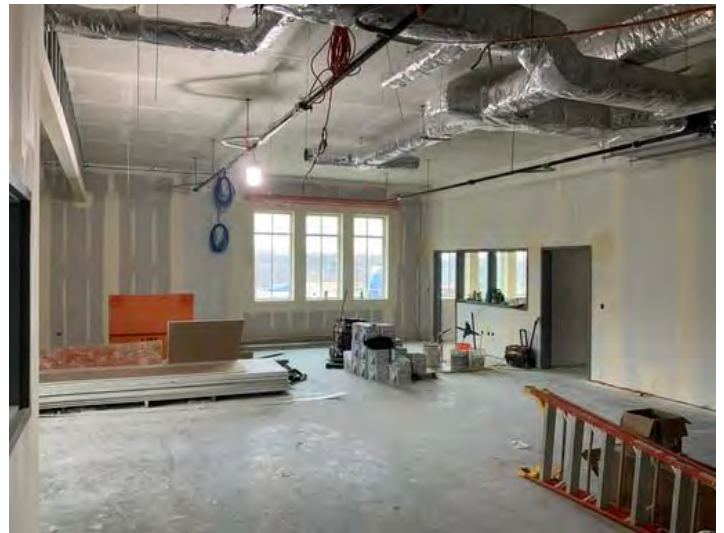

IMG_1375

Taken on Mar 7, 2024, 12:42 PM CST

Added on Mar 7, 2024, 4:54 PM CST

Added by Ken Gleason



IMG_1373

Taken on Mar 7, 2024, 12:41 PM CST

Added on Mar 7, 2024, 4:54 PM CST

Added by Ken Gleason



IMG_1377

Taken on Mar 7, 2024, 12:43 PM CST

Added on Mar 7, 2024, 4:54 PM CST

Added by Ken Gleason



IMG_1379

Taken on Mar 7, 2024, 12:43 PM CST

Added on Mar 7, 2024, 4:54 PM CST

Added by Ken Gleason



IMG_1378

Taken on Mar 7, 2024, 12:43 PM CST

Added on Mar 7, 2024, 4:54 PM CST

Added by Ken Gleason

Form detail

#138: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Mar 11, 2024
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 11, 2024, 3:29 PM CDT
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Clear



Temperature: 30°F

Wind: ↑ 4mph

Humidity: 73%

12:00 PM

Clear



Temperature: 56°F

Wind: ↗ 13mph

Humidity: 46%

4:00 PM

Windy



Temperature: 67°F

Wind: ↗ 17mph

Humidity: 39%

Updated Mar 19, 2024 at 2:57 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	7	56	crew worked on framing and drywall today on the first floor area
BP #6 Masonry - Jimmy'z Masonry	9	72	crew worked on exterior stone install at southern side of building today
BP #12 Mechanical - Jensen's Plumbing & Heating	1	8	mechanical pipe work on first floor was worked on today
BP #7 Roofing - Filotto Roofing	2	16	crew worked on the rework of the fascia around building today
BP #13 Electrical - CSN Electric	3	24	crew worked on piping and wiring at first floor and exterior mechanical pad today
Totals	22	176	

References

Photos (9)



IMG_1401

Taken on Mar 11, 2024, 12:36 PM CDT

Added on Mar 11, 2024, 3:29 PM CDT

Added by Ken Gleason



IMG_1400

Taken on Mar 11, 2024, 12:36 PM CDT

Added on Mar 11, 2024, 3:29 PM CDT

Added by Ken Gleason



IMG_1402

Taken on Mar 11, 2024, 12:36 PM CDT

Added on Mar 11, 2024, 3:29 PM CDT

Added by Ken Gleason



IMG_1399

Taken on Mar 11, 2024, 8:39 AM CDT

Added on Mar 11, 2024, 3:29 PM CDT

Added by Ken Gleason



IMG_1398

Taken on Mar 11, 2024, 8:38 AM CDT

Added on Mar 11, 2024, 3:29 PM CDT

Added by Ken Gleason



IMG_1403

Taken on Mar 11, 2024, 12:37 PM CDT

Added on Mar 11, 2024, 3:29 PM CDT

Added by Ken Gleason



IMG_1404

Taken on Mar 11, 2024, 12:37 PM CDT

Added on Mar 11, 2024, 3:29 PM CDT

Added by Ken Gleason



IMG_1405

Taken on Mar 11, 2024, 12:37 PM CDT

Added on Mar 11, 2024, 3:29 PM CDT

Added by Ken Gleason



IMG_1406

Taken on Mar 11, 2024, 12:37 PM CDT

Added on Mar 11, 2024, 3:29 PM CDT

Added by Ken Gleason

Form detail

#139: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Mar 13, 2024
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 13, 2024, 1:19 PM CDT
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM **Mostly Clear**



Temperature: 44°F

Wind: ↗ 2mph

Humidity: 85%

12:00 PM **Partly Cloudy**



Temperature: 66°F

Wind: ← 6mph

Humidity: 50%

4:00 PM **Cloudy**



Temperature: 68°F

Wind: ↖ 5mph

Humidity: 51%

Updated Mar 19, 2024 at 2:58 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	5	40	crew worked on drywall taping, framing at exterior for barrel vaulted area
BP #6 Masonry - Jimmy'z Masonry	9	72	crew worked on exterior stone installment today
BP #8 Painting - Nedrow Painting	2	16	crew worked on interior paint coats on first floor level
BP #12 Mechanical - Jensen's Plumbing & Heating	2	16	crew worked on mechanical piping and ductwork at first floor today
BP #7 Roofing - Filotto Roofing	1	8	crew worked on rework for the fascia of building
BP #13 Electrical - CSN Electric	3	24	crew worked on electrical piping and wiring in basement today
BP #15 Elevator - Otis Elevator Company	2	16	crew worked on elevator install today
Totals	24	192	

References

Photos (7)



IMG_1416

Taken on Mar 13, 2024, 1:06 PM CDT

Added on Mar 13, 2024, 1:19 PM CDT

Added by Ken Gleason




IMG_1421

Taken on Mar 13, 2024, 1:11 PM CDT

Added on Mar 13, 2024, 1:19 PM CDT

Added by Ken Gleason

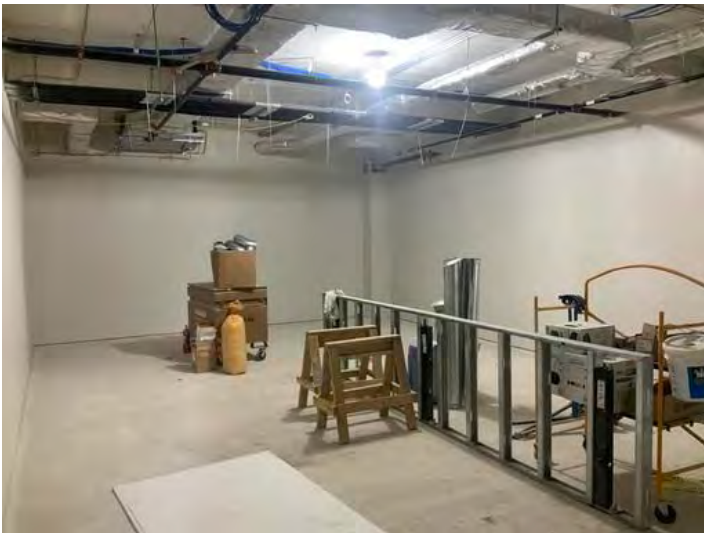

IMG_1422

Taken on Mar 13, 2024, 1:11 PM CDT

Added on Mar 13, 2024, 1:19 PM CDT

Added by Ken Gleason



IMG_1418

Taken on Mar 13, 2024, 1:10 PM CDT

Added on Mar 13, 2024, 1:19 PM CDT

Added by Ken Gleason



IMG_1417

Taken on Mar 13, 2024, 1:10 PM CDT

Added on Mar 13, 2024, 1:19 PM CDT

Added by Ken Gleason



IMG_1419

Taken on Mar 13, 2024, 1:10 PM CDT

Added on Mar 13, 2024, 1:19 PM CDT

Added by Ken Gleason



IMG_1420

Taken on Mar 13, 2024, 1:11 PM CDT

Added on Mar 13, 2024, 1:19 PM CDT

Added by Ken Gleason

Form detail

#140: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Mar 14, 2024
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 14, 2024, 4:32 PM CDT
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0.43 inches

🍏 Weather [View Sources](#)

7:00 AM

Rain



Temperature: 47°F

Wind: ← 6mph

Humidity: 92%

12:00 PM

Cloudy



Temperature: 62°F

Wind: ↑ 6mph

Humidity: 85%

4:00 PM

Mostly Cloudy



Temperature: 59°F

Wind: ↘ 12mph

Humidity: 78%

Updated Mar 19, 2024 at 2:58 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	5	40	crew worked on drywall taping, patching, site clean up today
BP #12 Mechanical - Jensen's Plumbing & Heating	2	16	crew worked on mechanical piping on first floor today
BP #13 Electrical - CSN Electric	3	24	crew worked on piping and wiring in basement
Totals	10	80	

References

Photos (8)



IMG_1428

Taken on Mar 14, 2024, 9:35 AM CDT

Added on Mar 14, 2024, 4:32 PM CDT

Added by Ken Gleason



IMG_1424

Taken on Mar 14, 2024, 9:34 AM CDT

Added on Mar 14, 2024, 4:32 PM CDT

Added by Ken Gleason




IMG_1430

Taken on Mar 14, 2024, 9:42 AM CDT

Added on Mar 14, 2024, 4:32 PM CDT

Added by Ken Gleason

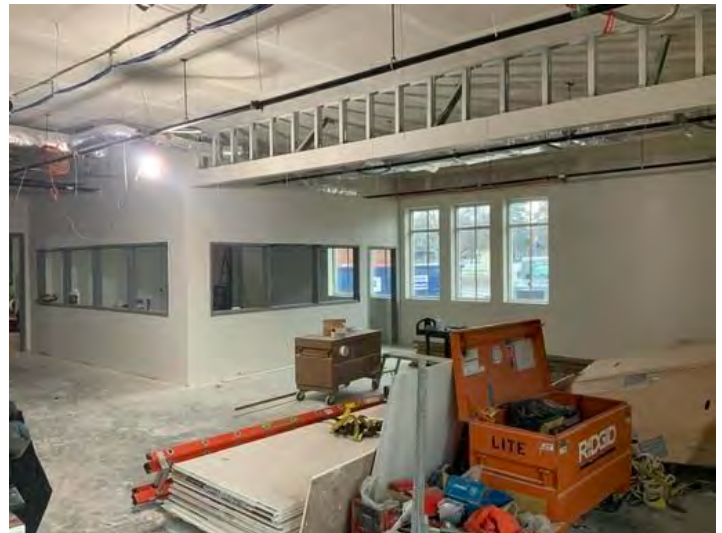

IMG_1427

Taken on Mar 14, 2024, 9:35 AM CDT

Added on Mar 14, 2024, 4:32 PM CDT

Added by Ken Gleason



IMG_1426

Taken on Mar 14, 2024, 9:35 AM CDT

Added on Mar 14, 2024, 4:32 PM CDT

Added by Ken Gleason



IMG_1423

Taken on Mar 14, 2024, 9:33 AM CDT

Added on Mar 14, 2024, 4:32 PM CDT

Added by Ken Gleason



IMG_1429

Taken on Mar 14, 2024, 9:37 AM CDT

Added on Mar 14, 2024, 4:32 PM CDT

Added by Ken Gleason



IMG_1425

Taken on Mar 14, 2024, 9:34 AM CDT

Added on Mar 14, 2024, 4:32 PM CDT

Added by Ken Gleason

Form detail

#142: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Mar 18, 2024
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 18, 2024, 3:40 PM CDT
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Partly Cloudy



Temperature: 24°F

Wind: ↘ 7mph

Humidity: 65%

12:00 PM

Mostly Cloudy



Temperature: 32°F

Wind: ↘ 10mph

Humidity: 55%

4:00 PM

Mostly Cloudy



Temperature: 36°F

Wind: ↘ 10mph

Humidity: 52%

Updated Mar 19, 2024 at 2:59 PM

1. Work Log

Crew	# Workers	# Total hours	Work performed
BP #2 General Trades - Lite Construction	4	32	crew worked on drywall taping of walls and installing ceiling grid throughout first floor
BP #10 Fire Protection - CL Doucette Inc	1	8	crew worked on fire protection piping in basement today
BP #11 Plumbing - Omega Plumbing	2	12	crew worked on main water line connections in sprinkler room in basement today
BP #12 Mechanical - Jensen's Plumbing & Heating	2	16	crew worked on mechanical piping on first floor today
BP #13 Electrical - CSN Electric	3	24	crew worked on electrical piping and wiring in basement today
BP #15 Elevator - Otis Elevator Company	2	16	crew worked on elevator install today
Totals	14	108	

References

Photos (7)



IMG_1443

Taken on Mar 18, 2024, 12:47 PM CDT

Added on Mar 18, 2024, 3:40 PM CDT

Added by Ken Gleason




IMG_1445

Taken on Mar 18, 2024, 12:49 PM CDT

Added on Mar 18, 2024, 3:40 PM CDT

Added by Ken Gleason

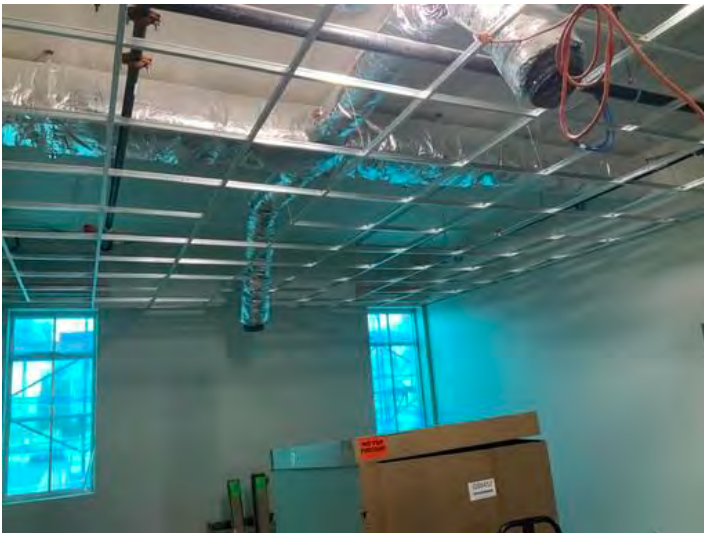

IMG_1446

Taken on Mar 18, 2024, 12:49 PM CDT

Added on Mar 18, 2024, 3:40 PM CDT

Added by Ken Gleason



IMG_1447

Taken on Mar 18, 2024, 12:50 PM CDT

Added on Mar 18, 2024, 3:40 PM CDT

Added by Ken Gleason




IMG_1444

Taken on Mar 18, 2024, 12:47 PM CDT

Added on Mar 18, 2024, 3:40 PM CDT

Added by Ken Gleason

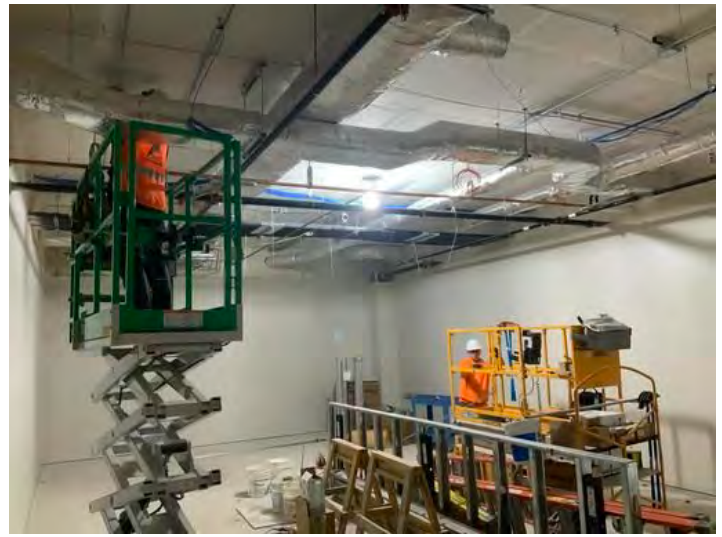

IMG_1448

Taken on Mar 18, 2024, 12:50 PM CDT

Added on Mar 18, 2024, 3:40 PM CDT

Added by Ken Gleason



IMG_1449

Taken on Mar 18, 2024, 12:50 PM CDT

Added on Mar 18, 2024, 3:40 PM CDT

Added by Ken Gleason

Form detail

#143: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Mar 19, 2024
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 19, 2024, 3:52 PM CDT
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Mostly Clear



Temperature: 28°F

Wind: ↗ 11mph

Humidity: 67%

12:00 PM

Windy



Temperature: 47°F

Wind: → 18mph

Humidity: 44%

4:00 PM

Windy



Temperature: 59°F

Wind: → 15mph

Humidity: 37%

Updated Apr 1, 2024 at 3:29 PM

1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	4	32	-	crew worked on ceiling grid install on first floor today
-	BP #6 Masonry - Jimmy'z Masonry	-	9	72	-	crew worked on stone install at exterior of building today
-	BP #12 Mechanical - Jensen's Plumbing & Heating	-	2	16	-	crew installed mechanical piping and ductwork at first floor today
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on install of electrical piping and wiring at basement and first floor today
-	BP #15 Elevator - Otis Elevator Company	-	2	16	-	crew worked on install of elevator today
Totals:			20	160	0	

References

Photos (15)



IMG_1456

Taken on Mar 19, 2024, 11:33 AM CDT

Added on Mar 19, 2024, 3:51 PM CDT

Added by Ken Gleason



IMG_1454

Taken on Mar 19, 2024, 10:57 AM CDT

Added on Mar 19, 2024, 3:51 PM CDT

Added by Ken Gleason




IMG_1457

Taken on Mar 19, 2024, 11:33 AM CDT

Added on Mar 19, 2024, 3:51 PM CDT

Added by Ken Gleason

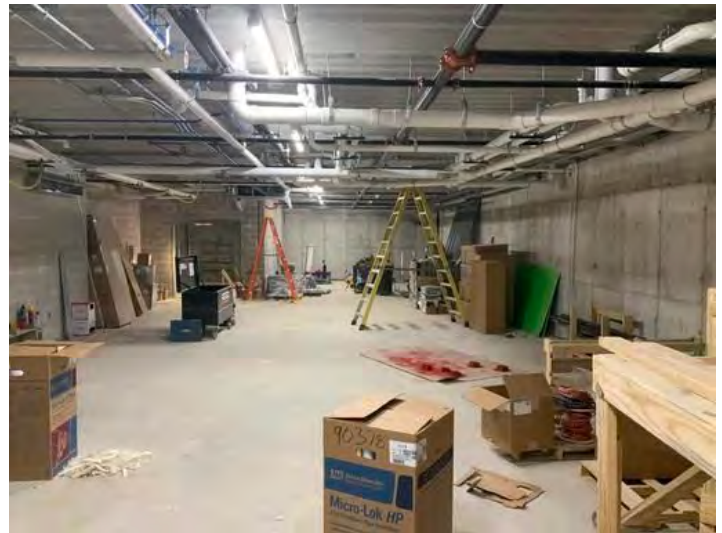

IMG_1455

Taken on Mar 19, 2024, 11:33 AM CDT

Added on Mar 19, 2024, 3:51 PM CDT

Added by Ken Gleason



IMG_1453

Taken on Mar 19, 2024, 10:56 AM CDT

Added on Mar 19, 2024, 3:51 PM CDT

Added by Ken Gleason



IMG_1452

Taken on Mar 19, 2024, 10:56 AM CDT

Added on Mar 19, 2024, 3:51 PM CDT

Added by Ken Gleason



IMG_1460

Taken on Mar 19, 2024, 11:34 AM CDT

Added on Mar 19, 2024, 3:51 PM CDT

Added by Ken Gleason



IMG_1464

Taken on Mar 19, 2024, 11:40 AM CDT

Added on Mar 19, 2024, 3:51 PM CDT

Added by Ken Gleason



IMG_1466
Taken on Mar 19, 2024, 11:40 AM CDT
Added on Mar 19, 2024, 3:51 PM CDT
Added by Ken Gleason




IMG_1463
Taken on Mar 19, 2024, 11:39 AM CDT
Added on Mar 19, 2024, 3:51 PM CDT
Added by Ken Gleason



IMG_1462
Taken on Mar 19, 2024, 11:39 AM CDT
Added on Mar 19, 2024, 3:51 PM CDT
Added by Ken Gleason



IMG_1458
Taken on Mar 19, 2024, 11:34 AM CDT
Added on Mar 19, 2024, 3:51 PM CDT
Added by Ken Gleason

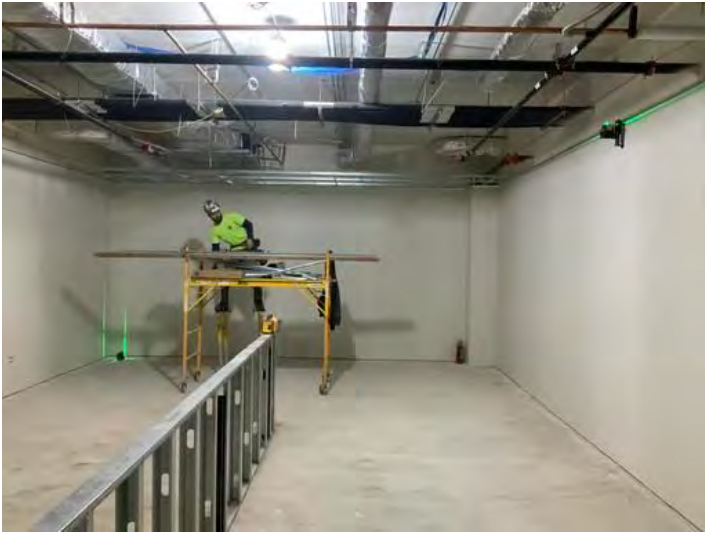

IMG_1459

Taken on Mar 19, 2024, 11:34 AM CDT

Added on Mar 19, 2024, 3:52 PM CDT

Added by Ken Gleason



IMG_1465

Taken on Mar 19, 2024, 11:40 AM CDT

Added on Mar 19, 2024, 3:52 PM CDT

Added by Ken Gleason



IMG_1461

Taken on Mar 19, 2024, 11:35 AM CDT

Added on Mar 19, 2024, 3:52 PM CDT

Added by Ken Gleason

Form detail

#144: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Mar 20, 2024
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 20, 2024, 12:53 PM CDT
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Clear



Temperature: 32°F

Wind: ↘ 7mph

Humidity: 54%

12:00 PM

Clear



Temperature: 39°F

Wind: ↘ 12mph

Humidity: 36%

4:00 PM

Clear



Temperature: 42°F

Wind: ↘ 10mph

Humidity: 31%

Updated Apr 1, 2024 at 3:30 PM

1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	4	32	-	crew worked on interior ceiling grid install at first floor as well as drywall install and taping on first floor
-	BP #12 Mechanical - Jensen's Plumbing & Heating	-	2	16	-	crew worked on mechanical piping and ductwork for first floor today
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on electrical piping and wiring at first floor and basement today
-	BP #15 Elevator - Otis Elevator Company	-	2	16	-	crew worked on elevator install today
Totals:			11	88	0	

References

Photos (7)



IMG_1468

Taken on Mar 20, 2024, 8:51 AM CDT
Added on Mar 20, 2024, 12:52 PM CDT
Added by Ken Gleason



IMG_1467

Taken on Mar 20, 2024, 8:50 AM CDT
Added on Mar 20, 2024, 12:52 PM CDT
Added by Ken Gleason



IMG_1472

Taken on Mar 20, 2024, 8:54 AM CDT
Added on Mar 20, 2024, 12:52 PM CDT
Added by Ken Gleason



IMG_1471

Taken on Mar 20, 2024, 8:54 AM CDT
Added on Mar 20, 2024, 12:52 PM CDT
Added by Ken Gleason




IMG_1469

Taken on Mar 20, 2024, 8:51 AM CDT
Added on Mar 20, 2024, 12:53 PM CDT
Added by Ken Gleason



IMG_1473

Taken on Mar 20, 2024, 11:48 AM CDT
Added on Mar 20, 2024, 12:53 PM CDT
Added by Ken Gleason

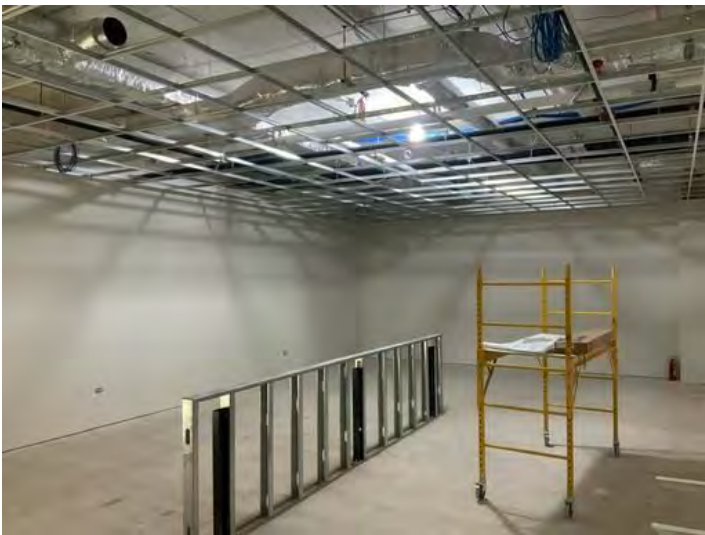

IMG_1470

Taken on Mar 20, 2024, 8:54 AM CDT
Added on Mar 20, 2024, 12:53 PM CDT
Added by Ken Gleason

Form detail

#145: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Mar 21, 2024
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 21, 2024, 2:50 PM CDT
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Mostly Cloudy



Temperature: 26°F

Wind: ← 1mph

Humidity: 76%

12:00 PM

Partly Cloudy



Temperature: 37°F

Wind: ↖ 4mph

Humidity: 46%

4:00 PM

Mostly Clear



Temperature: 42°F

Wind: ← 4mph

Humidity: 40%

Updated Apr 1, 2024 at 3:30 PM

1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	4	32	-	crew worked on drywall taping as well as ceiling grid and wall paneling for the janitors closet on first floor today
-	BP #12 Mechanical - Jensen's Plumbing & Heating	-	2	16	-	crew worked on ductwork install at first floor today
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on electrical wiring in basement today as well as install of the switches for the window shades at first floor today
Totals:			9	72	0	

References


Photos (7)



IMG_1474
Taken on Mar 21, 2024, 11:57 AM CDT
Added on Mar 21, 2024, 2:50 PM CDT
Added by Ken Gleason



IMG_1477
Taken on Mar 21, 2024, 11:57 AM CDT
Added on Mar 21, 2024, 2:50 PM CDT
Added by Ken Gleason

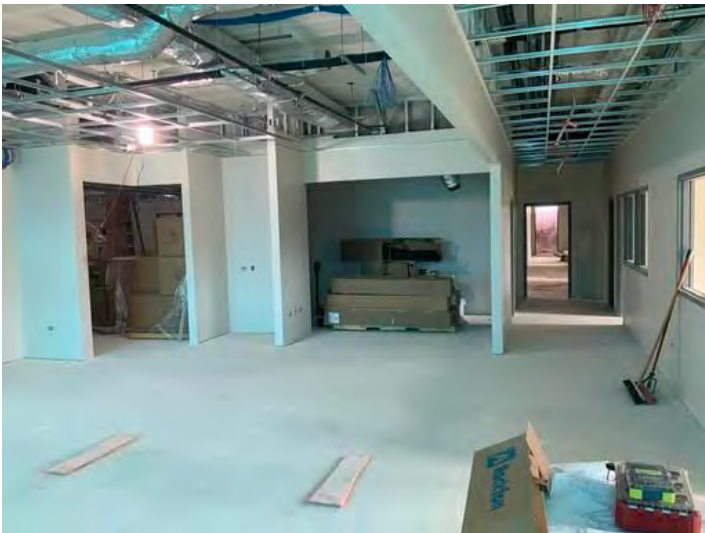

IMG_1478
Taken on Mar 21, 2024, 11:58 AM CDT
Added on Mar 21, 2024, 2:50 PM CDT
Added by Ken Gleason



IMG_1480
Taken on Mar 21, 2024, 11:59 AM CDT
Added on Mar 21, 2024, 2:50 PM CDT
Added by Ken Gleason



IMG_1476

Taken on Mar 21, 2024, 11:57 AM CDT

Added on Mar 21, 2024, 2:50 PM CDT

Added by Ken Gleason



IMG_1475

Taken on Mar 21, 2024, 11:57 AM CDT

Added on Mar 21, 2024, 2:50 PM CDT

Added by Ken Gleason



IMG_1479

Taken on Mar 21, 2024, 11:59 AM CDT

Added on Mar 21, 2024, 2:50 PM CDT

Added by Ken Gleason

Form detail

#147: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Mar 25, 2024
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 25, 2024, 2:42 PM CDT
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0.59 inches

🍏 Weather [View Sources](#)

7:00 AM

Cloudy



Temperature: 48°F

Wind: ↻ 10mph

Humidity: 53%

12:00 PM

Windy



Temperature: 57°F

Wind: ↑ 16mph

Humidity: 69%

4:00 PM

Cloudy



Temperature: 57°F

Wind: ↑ 9mph

Humidity: 79%

Updated Apr 1, 2024 at 3:31 PM

1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	3	24	-	crew worked on framing and drywall at lobby area as well as elevator area on first floor
-	BP #6 Masonry - Jimmy'z Masonry	-	9	0	-	crew showed up in the morning but were not able to work on the exterior stone/brick due to raining weather
-	BP #10 Fire Protection - CL Doucette Inc	-	1	8	-	crew worked on rerouting pipe at stairway, fire caulk of penetrations
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on electrical piping and wiring in basement today
-	BP #15 Elevator - Otis Elevator Company	-	2	16	-	crew worked on elevator install today
Totals:			18	72	0	

References

Photos (6)



IMG_1496

Taken on Mar 25, 2024, 9:57 AM CDT

Added on Mar 25, 2024, 2:41 PM CDT

Added by Ken Gleason



IMG_1493

Taken on Mar 22, 2024, 1:44 PM CDT

Added on Mar 25, 2024, 2:41 PM CDT

Added by Ken Gleason



IMG_1498

Taken on Mar 25, 2024, 10:19 AM CDT

Added on Mar 25, 2024, 2:41 PM CDT

Added by Ken Gleason



IMG_1495

Taken on Mar 25, 2024, 9:57 AM CDT

Added on Mar 25, 2024, 2:42 PM CDT

Added by Ken Gleason



IMG_1497

Taken on Mar 25, 2024, 10:19 AM CDT

Added on Mar 25, 2024, 2:42 PM CDT

Added by Ken Gleason



IMG_1494

Taken on Mar 22, 2024, 1:44 PM CDT

Added on Mar 25, 2024, 2:42 PM CDT

Added by Ken Gleason

Form detail

#148: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Mar 26, 2024
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 26, 2024, 4:08 PM CDT
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0.16 inches

🍏 Weather [View Sources](#)

7:00 AM

Cloudy



Temperature: 51°F

Wind: ↑ 11mph

Humidity: 92%

12:00 PM

Cloudy



Temperature: 47°F

Wind: ↗ 14mph

Humidity: 84%

4:00 PM

Windy



Temperature: 43°F

Wind: ↗ 15mph

Humidity: 80%


Updated Apr 1, 2024 at 3:32 PM

1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	3	24	-	crew worked on interior ceiling grid and panels as well as framing and drywall at elevator area
-	BP #6 Masonry - Jimmy'z Masonry	-	12	96	-	crew worked on exterior stone and brick install today
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on electrical piping and wiring in basement
-	BP #15 Elevator - Otis Elevator Company	-	2	16	-	crew worked on elevator install today
Totals:			20	160	0	

References

Photos (6)

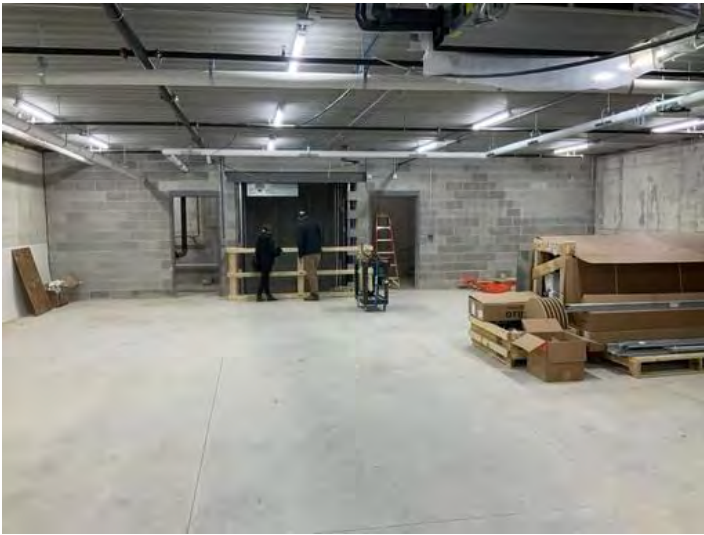

IMG_1503

Taken on Mar 26, 2024, 3:28 PM CDT

Added on Mar 26, 2024, 4:08 PM CDT

Added by Ken Gleason




IMG_1507

Taken on Mar 26, 2024, 4:04 PM CDT

Added on Mar 26, 2024, 4:08 PM CDT

Added by Ken Gleason

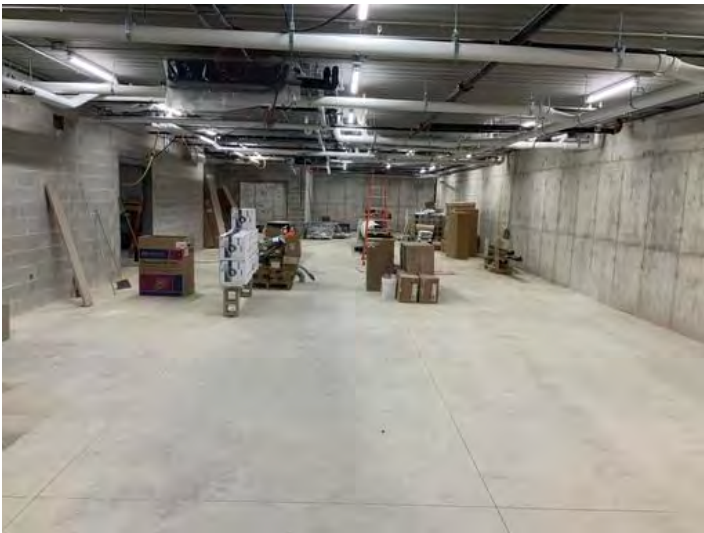

IMG_1502

Taken on Mar 26, 2024, 3:27 PM CDT

Added on Mar 26, 2024, 4:08 PM CDT

Added by Ken Gleason



IMG_1506

Taken on Mar 26, 2024, 4:03 PM CDT

Added on Mar 26, 2024, 4:08 PM CDT

Added by Ken Gleason



IMG_1504

Taken on Mar 26, 2024, 4:02 PM CDT

Added on Mar 26, 2024, 4:08 PM CDT

Added by Ken Gleason



IMG_1505

Taken on Mar 26, 2024, 4:03 PM CDT

Added on Mar 26, 2024, 4:08 PM CDT

Added by Ken Gleason

Form detail

#149: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Mar 27, 2024
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 27, 2024, 2:02 PM CDT
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Cloudy



Temperature: 27°F

Wind: → 12mph

Humidity: 75%

12:00 PM

Partly Cloudy



Temperature: 36°F

Wind: → 11mph

Humidity: 63%

4:00 PM

Partly Cloudy



Temperature: 42°F

Wind: → 12mph

Humidity: 54%

Updated Apr 1, 2024 at 3:32 PM

1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	4	32	-	crew worked on setting ceiling tiles and taping up drywall at lobby area
-	BP #8 Painting - Nedrow Painting	-	1	8	-	worked on painting bathrooms on first floor and prep work in basement
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on running wiring and setting lights on first floor today
-	BP #6 Masonry - Jimmy'z Masonry	-	0	0	-	crew did not work today due to cold temps
Totals:			8	64	0	

References

Photos (11)



IMG_1517

Taken on Mar 27, 2024, 12:45 PM CDT

Added on Mar 27, 2024, 2:02 PM CDT

Added by Ken Gleason



IMG_1512

Taken on Mar 27, 2024, 12:43 PM CDT

Added on Mar 27, 2024, 2:02 PM CDT

Added by Ken Gleason



IMG_1508

Taken on Mar 27, 2024, 12:42 PM CDT

Added on Mar 27, 2024, 2:02 PM CDT

Added by Ken Gleason



IMG_1509

Taken on Mar 27, 2024, 12:43 PM CDT

Added on Mar 27, 2024, 2:02 PM CDT

Added by Ken Gleason



IMG_1510

Taken on Mar 27, 2024, 12:43 PM CDT

Added on Mar 27, 2024, 2:02 PM CDT

Added by Ken Gleason



IMG_1516

Taken on Mar 27, 2024, 12:45 PM CDT

Added on Mar 27, 2024, 2:02 PM CDT

Added by Ken Gleason




IMG_1514

Taken on Mar 27, 2024, 12:44 PM CDT

Added on Mar 27, 2024, 2:02 PM CDT

Added by Ken Gleason

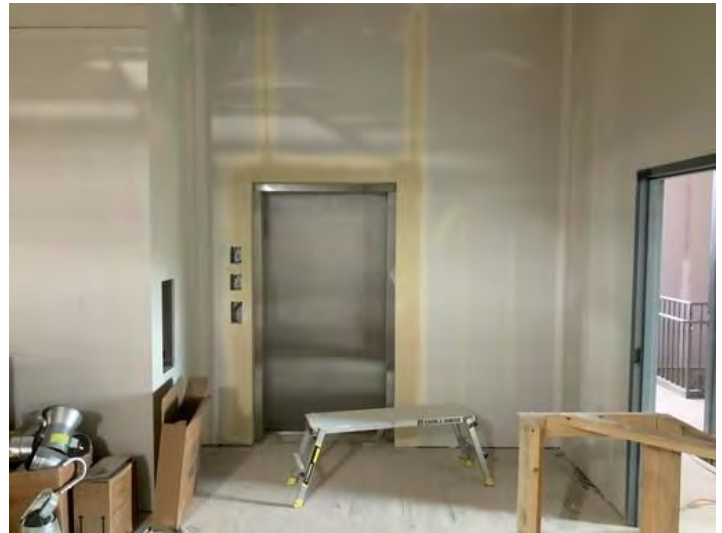


IMG_1519

Taken on Mar 27, 2024, 12:53 PM CDT

Added on Mar 27, 2024, 2:02 PM CDT

Added by Ken Gleason

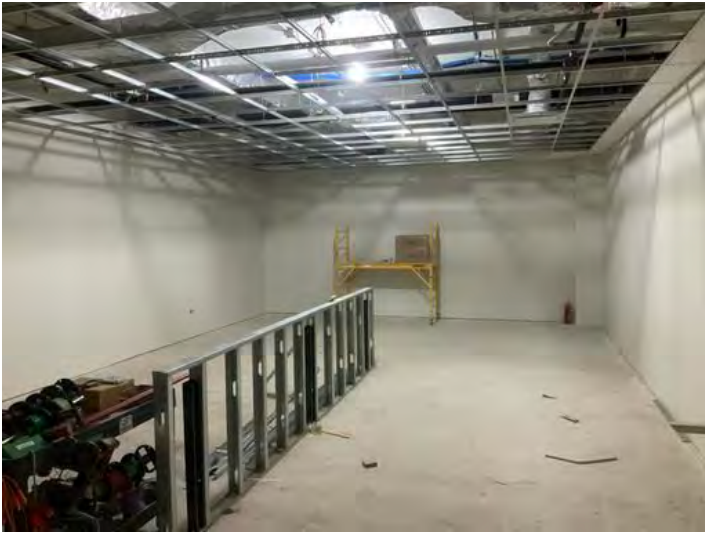

IMG_1518

Taken on Mar 27, 2024, 12:53 PM CDT

Added on Mar 27, 2024, 2:02 PM CDT

Added by Ken Gleason



IMG_1515

Taken on Mar 27, 2024, 12:45 PM CDT

Added on Mar 27, 2024, 2:02 PM CDT

Added by Ken Gleason



IMG_1513

Taken on Mar 27, 2024, 12:44 PM CDT

Added on Mar 27, 2024, 2:02 PM CDT

Added by Ken Gleason

Form detail

#151: Daily Report



Forms

Location	Kendall County New Office Building
Form date	Mar 28, 2024
Submitted by	Ken Gleason
Status	Closed
Last update	Mar 28, 2024, 2:43 PM CDT
Last updated by	Ken Gleason
Included references	Assets Files Forms Issues Photos

Supporting information

Kendall County New Office Project. CCCS Project Number 221071.

Weather

🌧️ Rain: 0 inches

🍏 Weather [View Sources](#)

7:00 AM

Mostly Cloudy



Temperature: 30°F

Wind: ↑ 2mph

Humidity: 79%

12:00 PM

Mostly Clear



Temperature: 44°F

Wind: ↗ 7mph

Humidity: 56%

4:00 PM

Partly Cloudy



Temperature: 51°F

Wind: → 8mph

Humidity: 51%

Updated Apr 1, 2024 at 3:33 PM

1. Work Log

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	BP #2 General Trades - Lite Construction	-	3	24	-	crew worked on install of ceiling tiles and backer on walls of front lobby area soffits and columns as well as some framing at back/east side entryways
-	BP #6 Masonry - Jimmy'z Masonry	-	10	80	-	crew worked on install of stone and brick at south and east side of building today
-	BP #8 Painting - Nedrow Painting	-	2	16	-	crew worked on taping/prep work in basement as well as getting started on painting of basement today.
-	BP #10 Fire Protection - CL Doucette Inc	-	1	8	-	crew was on site filling all fire protection piping penetrations through walls and roof deck
-	BP #13 Electrical - CSN Electric	-	3	24	-	crew worked on pulling wiring at basement and first floor as well as install of light fixtures on first floor today
Totals:			19	152	0	

References

Photos (10)



IMG_1524

Taken on Mar 28, 2024, 12:59 PM CDT

Added on Mar 28, 2024, 2:42 PM CDT

Added by Ken Gleason




IMG_1520

Taken on Mar 28, 2024, 12:03 PM CDT

Added on Mar 28, 2024, 2:42 PM CDT

Added by Ken Gleason

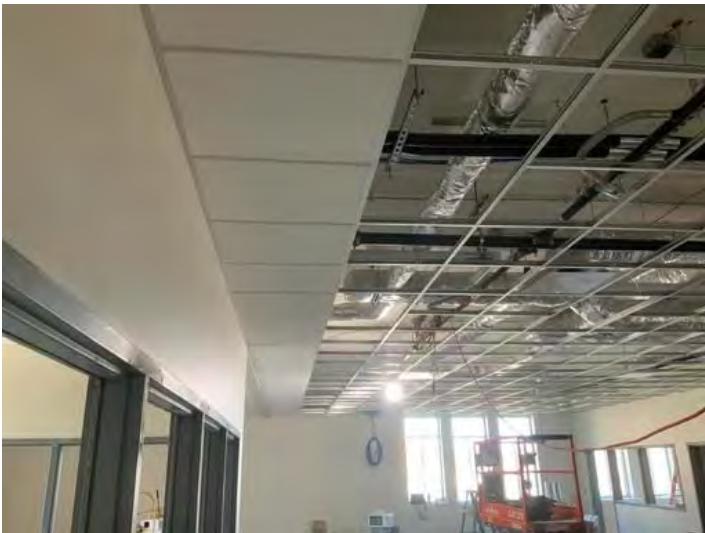

IMG_1523

Taken on Mar 28, 2024, 12:59 PM CDT

Added on Mar 28, 2024, 2:43 PM CDT

Added by Ken Gleason



IMG_1522

Taken on Mar 28, 2024, 12:58 PM CDT

Added on Mar 28, 2024, 2:43 PM CDT

Added by Ken Gleason



IMG_1521

Taken on Mar 28, 2024, 12:03 PM CDT

Added on Mar 28, 2024, 2:43 PM CDT

Added by Ken Gleason




IMG_1525

Taken on Mar 28, 2024, 1:00 PM CDT

Added on Mar 28, 2024, 2:43 PM CDT

Added by Ken Gleason

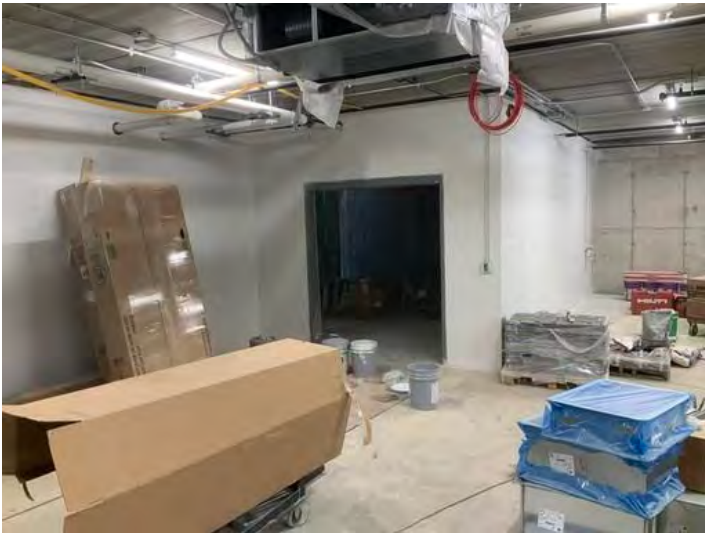

IMG_1528

Taken on Mar 28, 2024, 1:00 PM CDT

Added on Mar 28, 2024, 2:43 PM CDT

Added by Ken Gleason



IMG_1527

Taken on Mar 28, 2024, 1:00 PM CDT

Added on Mar 28, 2024, 2:43 PM CDT

Added by Ken Gleason




IMG_1526

Taken on Mar 28, 2024, 1:00 PM CDT

Added on Mar 28, 2024, 2:43 PM CDT

Added by Ken Gleason

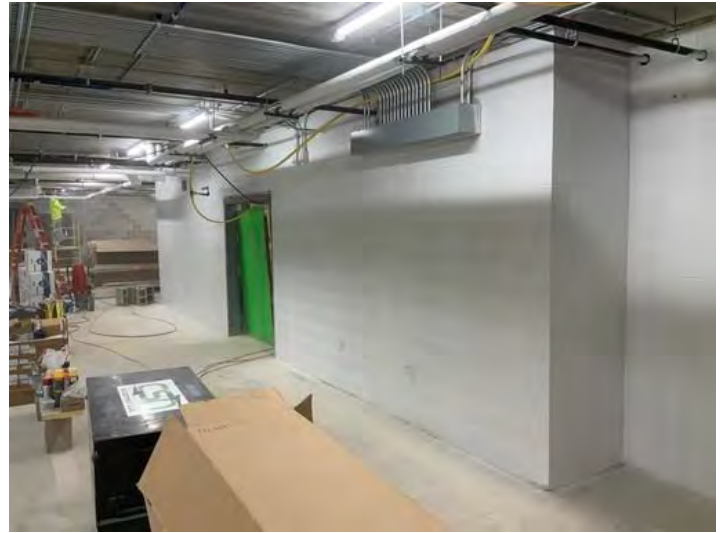

IMG_1529

Taken on Mar 28, 2024, 1:00 PM CDT

Added on Mar 28, 2024, 2:43 PM CDT

Added by Ken Gleason

SECTION 5



FIELD OBSERVATION CONFIRMATION

Date: 2024-03-12 Observation Time: 3:30 PM
Re: KENDALL COUNTY PHASE 1 CLERK BLDG Weather Conditions: 70F
Client: Kendall County Partly Cloudy
Project: 221071 --
Prepared By: Lauren Kiley Phone: 630.896.4678
Cordogan Clark & Associates Fax: 630.896.4987

Field Report Number: 240312

Est % Completion: 54% Conformance With Schedule (+/-): 0 days

Work In Progress: Cast stone, brick, polyiso insulation and flashing installation, reinstall of aluminum fascia, pipe insulation, elevator, gypsum board taping and base coat painting.

Observations:

1. Gypsum board installation appears to be near completion, taping and base coat painting is in progress
2. First layer of gypsum board appears to be scored and installed in barrel vault ceiling.
3. Aluminum fascia is being removed and replaced. The new appears to address the oil canning issue.
4. Modular cast stone, brick veneer, sill lugs and custom jamb installation is in progress.
5. Polyisocyanurate (polyiso) insulation appears to be installed prior to stone and brick installation.
5. In Sprinkler 005, water riser is installed in the center of room, aligned with incoming water line. Plan indicates the riser to be located along the north wall.
6. Hollow metal frames appear to be sanded and patched to address rust.

Items to Verify:

1. Where weeps are installed in stone at the top of the ramp landing, verify weeps are unobstructed.
2. Where piping penetrates through polyiso insulation, provide spray polyurethane foam insulation at any gaps or voids for system continuity per specification 072100 and notes on sheets A5.1/A5.2.
3. Blocking above windows for shades appears to have red coating, verify this is fire treated for code compliance per note on A5.1/A5.2.
4. Verify steel ladder installation for elevator pit access is coordinated with elevator contractor.
5. In Lobby 101, Verify resinous terrazzo flooring installation is continuous under ballot box.

Information Or Action Required:

1. At the set of 3 windows on the south, the s.s. flashing appears to be bent, and sill lugs are not fully aligned, adjust to be straight.
2. After review in field, there is not enough space in southwest corner of Vestibule 100 for the Kendall County information monitor, relocate power and data outlets to east side of window and mount at 60" to coordinate with monitor height.
3. Provide moisture testing for concrete prior to flooring installation per specifications 096813 and 096519.
4. At the south ramp the chamfer edges are rough, grind and clean for smooth finish.

Attachments:

Progress Photos

PHOTOGRAPHIC DOCUMENTATION

Date: 2024-03-12

Observation Time: 3:30 PM

Re: KENDALL COUNTY PHASE 1 CLERK BLDG
Project: 221071


Weather Conditions: 70F
Partly Cloudy



Gypsum Board in Barrel Vault



Aluminum Fascia Replacement on North

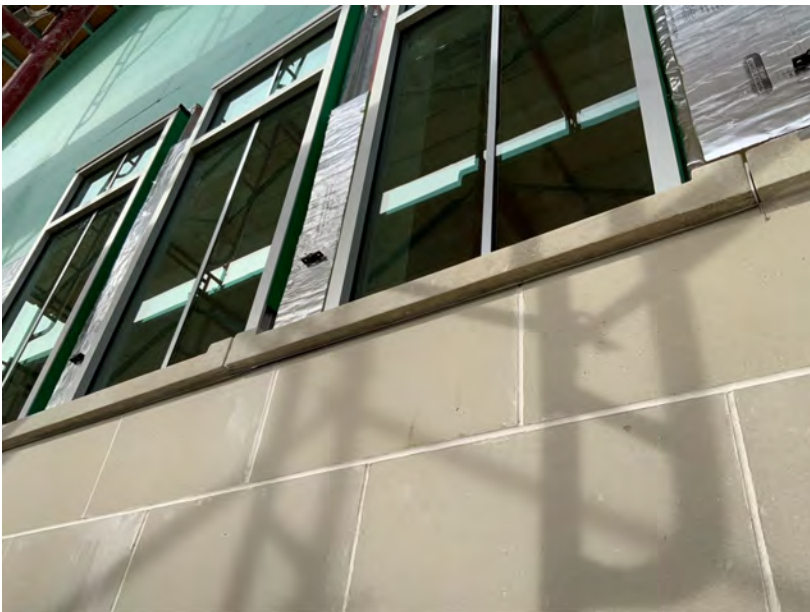

S.S. Flashing and Cast Stone Sill Lugs on South



Power/Data Location for Monitor

PHOTOGRAPHIC DOCUMENTATION

Date: 2024-03-12

Observation Time: 3:30 PM

Re: KENDALL COUNTY PHASE 1 CLERK BLDG
Project: 221071

Weather Conditions: 70F
Partly Cloudy



Window Shade Blocking



Weeps at Top of Ramp Landing



Chamfer Edges along Ramp




Water Riser in Sprinkler 005



Pipe Penetrations through Polyiso Insulation



Elevator Progress

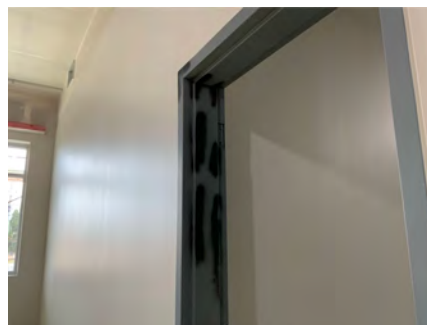

Hollow Metal Frame Repair



Ballot Box in Lobby 101

FIELD OBSERVATION CONFIRMATION

Date: 2024-03-26 Observation Time: 3:35 PM
Re: KENDALL COUNTY PHASE 1 CLERK BLDG Weather Conditions: 38F
Client: Kendall County Raining
Project: 221071 --
Prepared By: Lauren Kiley Phone: 630.896.4678
Cordogan Clark & Associates Fax: 630.896.4987

Field Report Number: 240326

Est % Completion: 58% Conformance With Schedule (+/-): 0 days

Work In Progress: Cast stone, brick veneer and polyiso insulation installation, first paint coating, plywood at barrel vault, elevator door installation on first floor.

Observations:

1. Cast stone and brick veneer installation appears complete on the south west and is in progress on the east and south. Thermal anchors appear to be installed at joints per details on A6.3 and as submitted.
2. Gypsum board wall installation is near completion, taping is in progress in the toilet rooms. Gypsum board ceiling and soffit installation are in progress.
3. Gypsum board has been installed for barrel vault ceiling and painted. See verification item no. 1.
4. Acoustical ceiling tile grid installation is in progress and appears to be near completion. Ceiling grid was relocated in Library 125 to align with hollow metal window frame adjacent to Lobby per request.
5. Exterior electrical boxes for card reader is installed at door 002A.
6. Stainless steel door and frame have been installed for the elevator on the first floor.

Items to Verify:

1. Verify a level 5 finish was provided at barrel vault ceiling per specification 092900.
2. Verify split tail anchors are installed at sills per detail 2/A6.3.
3. Verify all moisture and any remaining water is removed from elevator pit, prior to completing the elevator installation.
4. At the south ramp, verify dimension at intermediate landing is a minimum of 5'-0" clear between foundation walls and end of ramps.

Information Or Action Required:

1. Wood blocking appears to be missing for window shades in Recorder Office 124.
2. Provide fire resistant caulking around all through wall penetrations above ceiling.
3. Where piping penetrates through polyiso insulation, provide spray polyurethane foam insulation at any gaps or voids for system continuity per specification 071200 and notes on sheet A6.1/A6.2.
4. Plywood for interior columns at end of barrel vault and plywood along barrel vault perimeter are specified to be veneer plywood. Material installed does not appear to be veneered per details 7/A2.3 and 4/A8.7.

Attachments:

Progress Photos

PHOTOGRAPHIC DOCUMENTATION

Date: 2024-03-26

Observation Time: 6:35 PM

Re: KENDALL COUNTY PHASE 1 CLERK BLDG
Project: 221071

Weather Conditions: 38F
Raining



Cast Stone Installation on East



Barrel Vault Ceiling Progress in Lobby



Cast Stone and Brick Veneer on the South West



Cast Stone and Brick Veneer

PHOTOGRAPHIC DOCUMENTATION

Date: 2024-03-26

Observation Time: 6:35 PM

Re: KENDALL COUNTY PHASE 1 CLERK BLDG
Project: 221071

Weather Conditions: 38F
Raining



ACT in Library 125



Windows in Recorder Office 124



Attic Ceiling Access Panel




Plywood Columns at End of Barrel Vault



Thru Wall Penetrations Requiring Fire Caulking



Wall per PR-012

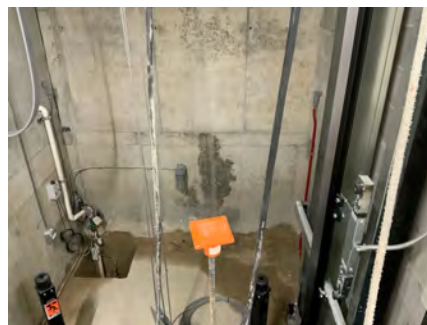

Moisture in Elevator Pit



Overall Progress from Southwest



CORDOGAN CLARK

ARCHITECTURE ■ ENGINEERING ■ CONSTRUCTION



960 Ridgeway Avenue
Aurora, Illinois 60506
T: 630.896.4678
F: 630.896.4987

Aurora, Illinois
Chicago, Illinois
Cleveland, Ohio
Davenport, Iowa
Lafayette, Indiana
St. Louis, Missouri
Sawyer, Michigan
Madrid, Spain

cordoganclark.com
